

NE Region US 41 Project

MONTHLY REPORT



FEBRUARY 2012


Winnebago County
Brown County

TABLE OF CONTENTS


- ◆ Project Location Maps & Schedules
 - Winnebago County..... 3
 - Brown County 4
- ◆ Public Outreach Meetings..... 5
- ◆ DBE Design & Construction Summary..... 6
- ◆ Labor Summary 7
- ◆ Program Financial Summary & Reserve Reports 8-9
- ◆ Top Issue & Risk List..... 10-11
- ◆ Construction Let Projects Financial Summary
 - Winnebago County 12
 - Brown County 13
- ◆ Construction Tasks Summary..... 14-16
- ◆ 2012 Construction Outlook
 - Winnebago County..... 17
 - Brown County..... 18
- ◆ Construction Project Detail
 - Current Lets..... 19-25
- ◆ Attachments..... 26
 - Winnebago County Contract Let Packages
 - Brown County Contract Let Packages
 - Calendar Year Delivery Schedules
 - US 41 Project/Total Majors Program Funding




Winnebago County (Wis 26 - Breezewood Ln)	
Current Budget:	
Expended to Date (Design, Utility, R/E, Const.)	
% Expended to Date (Design, Utility, R/E, Const.)	63.6%

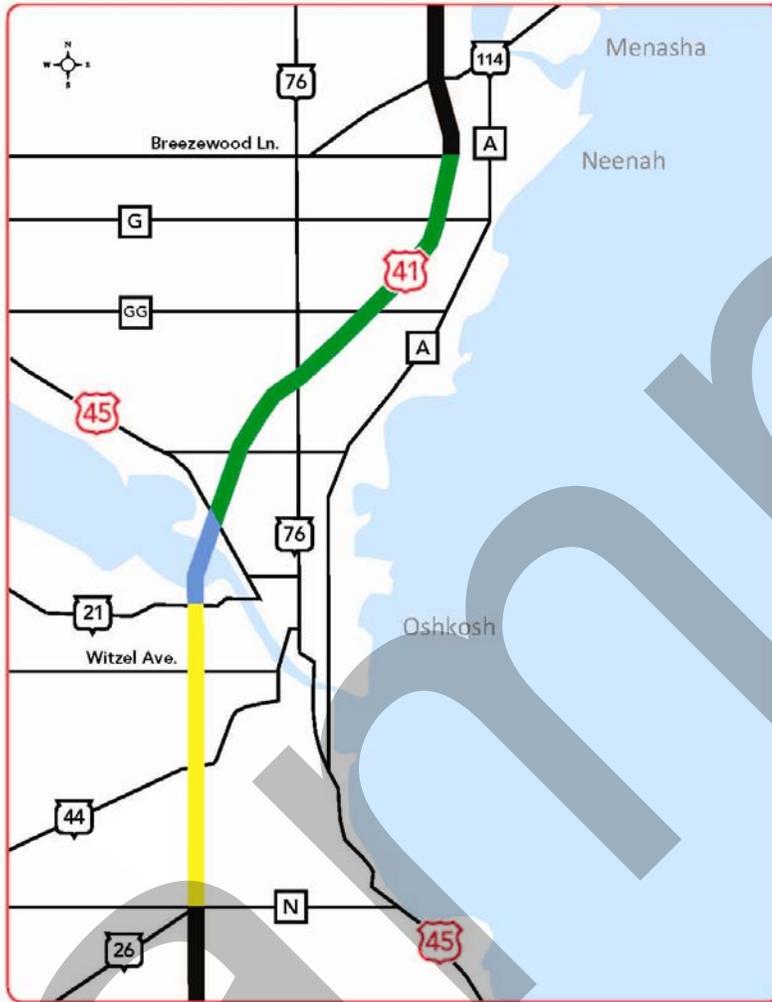

US 41 Project
Winnebago County
CONSTRUCTION
ACTIVITIES
and **SCHEDULE**

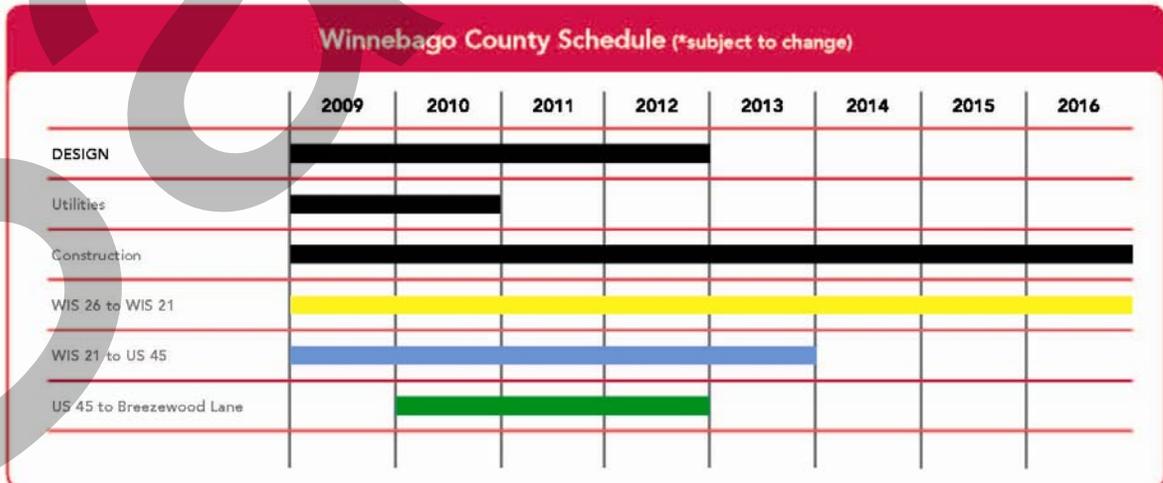

Brown County (Orange Ln - County M)	
Current Budget:	
Expended to Date (Design, Utility, R/E, Const.)	
% Expended to Date (Design, Utility, R/E, Const.)	22.8%

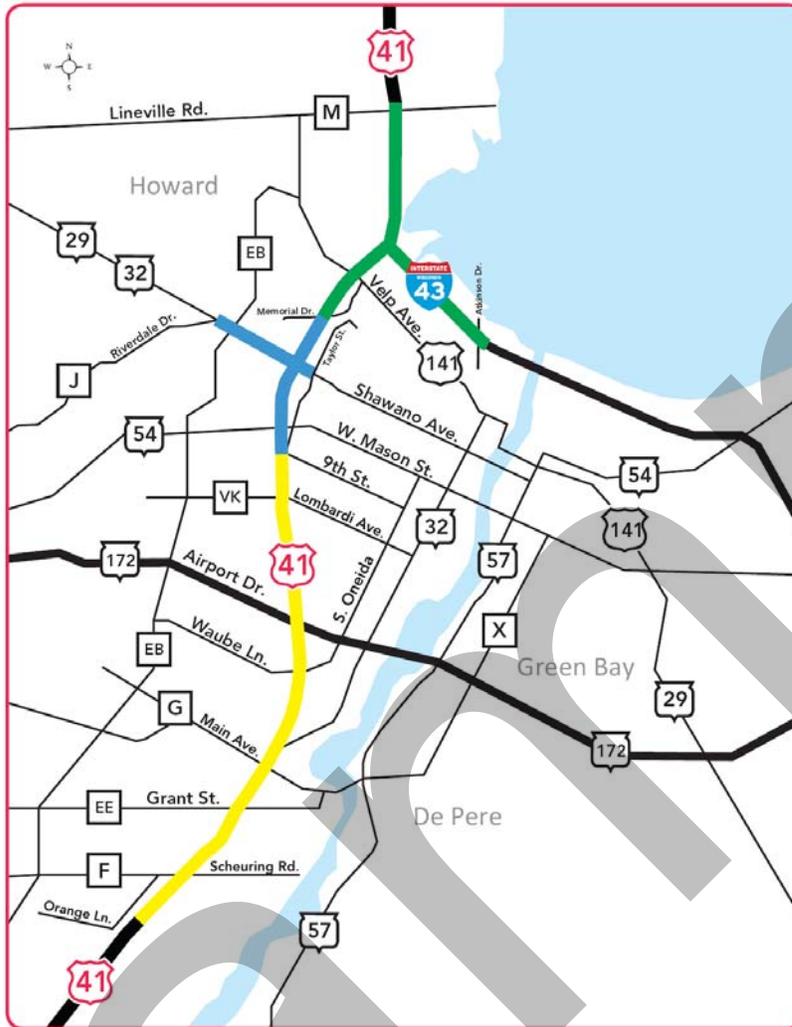

US 41 Project
Brown County
CONSTRUCTION
ACTIVITIES
and SCHEDULE



Brown County Schedule (*subject to change)								
	2010	2011	2012	2013	2014	2015	2016	2017
DESIGN	[Black bar spanning 2010-2014]							
Real Estate Acquisition	[Black bar spanning 2010-2015]							
Utilities	[Black bar spanning 2010-2016]							
Construction	[Black bar spanning 2010-2017]							
Orange Lane to Ninth Street	[Yellow bar spanning 2010-2016]							
Ninth Street to Memorial Drive, and WIS 29 (County J to Taylor Street)	[Blue bar spanning 2011-2016]							
Memorial Drive to Lineville Road, and I-43 (US 41 to Atkinson Drive)	[Green bar spanning 2012-2016]							



Public Outreach Meetings

Recent Meetings

Brown County Outreach

- Feb. 13 – PIM – County G preconstruction – De Pere
- Feb. 23 – US 41 Project booth – NWTC Engineering Open House – Green Bay
- Feb. 29 – Green Bay Business Expo- US 41 Project booth

Winnebago County Outreach

- Feb. 21 – US 41 Project presentation – Oshkosh Kiwanis
- Feb. 23 – PIM – WIS 21 preconstruction – Oshkosh

General Outreach

- Feb. 15 – US 41 Project presentation – Wisconsin Paper Group - Neenah

Outreach March 1, 2012 and Beyond

- March 5 – PIM – Lombardi Ave. preconstruction – Green Bay
- March 5 – US 41 Project Booth- Governor's Conference on Tourism – Green Bay
- March 19 – Oshkosh State of the City – US 41 Project booth
- March 27 – US 41 Project presentation – Green Bay Men's Club
- April 3 – US 41 Project presentation – Living in Retirement – Green Bay
- April 11 – US 41 Project presentation – Noon Optimists – Green Bay
- April 13 – US 41 Project presentation – Engineers Discovery Conference - Madison

Outreach Tools Development

- US 41 Project Spring 2012 newsletter at printer
- 2012 "Get Around Guide" printed and being circulated
- I-43 Repaving outreach plan developed
- WIS 21 - Mason Street interchange business websites up and running
- Facebook & Twitter website updates
- Project brief sheets
- 2012 PI schedule completed

DBE SUMMARY

CONSTRUCTION CONSULTANT DISADVANTAGED BUSINESS ENTERPRISE							
February 29, 2012	Total Contracted Amount	DBE Total Contracted Amount	% DBE Contracted	Total Paid To Date	DBE Total Paid To Date	% DBE Achieved	% Project Completion
Winnebago - Construction Management Subtotal	\$ 34,269,046	\$ 17,463,572	51.0%	\$ 18,842,599	\$ 10,321,644	54.8%	55.0%
Brown - Construction Management Subtotal	\$ 24,505,304	\$ 10,275,228	41.9%	\$ 6,002,355	\$ 3,261,781	54.3%	24.5%
Construction Management Total	\$ 58,774,350	\$ 27,738,800	47.2%	\$ 24,844,954	\$ 13,583,425	54.7%	42.3%
ARRA Program Total	\$ 4,293,440	\$ 2,376,759	55.4%	\$ 3,807,399	\$ 2,093,883	55.0%	88.7%

CONSTRUCTION CONTRACTOR DISADVANTAGED BUSINESS ENTERPRISE									
February 29, 2012	Assigned DBE Goal	Original DBE Committed	Total Contracted Amount	DBE Total Contracted Amount	% DBE Contracted	Total Paid To Date	DBE Total Paid To Date	% DBE Achieved	% Project Completion
WINNEBAGO - Construction Contracting									
Completed Projects (Final Payment) (Various)	0%	12.8%							
US 45 - Breezewood Ln Mainline (1120-09-71)	7%	11.0%							
US 45 - Breezewood Ln Fencing (1120-09-72)	16%	16.0%							
Brzwd Intchg & US45 to Brzwd NB Wdng (1120-09-83)	7%	6.2%							
9th Ave Intchg									
WIS 44 to WIS 21 - US 41 Mainline									
WIS 44 B-70-138 Painting (1120-10-72 1120-10-73 1120-10-79)	11%	10.9%							
WIS 44 to WIS 21 - US 41 Mainline (1120-10-74)	16%	16.1%							
WIS 26 - B-70-200 Stain									
WIS 26-WIS 44 Mainline (1120-10-78 1120-10-80)	9%	10.2%							
STH 26-STH 44 Fencing (1120-10-81)	16%	16.0%							
WIS 21 Intchg & Lkl Bdm Csway									
Weigh In Motion (1120-11-75 1120-11-84)	8%	6.3%							
US 45 Interchange (1120-11-83)	7%	7.1%							
Winnebago - Construction Contracting Subtotal									

BROWN - Construction Contracting									
Completed Projects (Final Payment) (Various)	0%	34.1%							
Mason St (WIS 54) Intchg									
Ninth St - Larsen Rd Mainline (1133-03-72 1133-04-84)	7%	7.3%							
Morris Ave - Ninth St TMP									
Ninth St - Larsen Rd TMP									
Orange Ln - Glory Rd TMP									
Glory Rd - Morris Ave TMP (1133-03-79 1133-04-83 1133-06-82 1133-09-77)	9%	8.7%							
Early Structures/Early Fill									
BeaverDamCreekBoxCulverts@VanBoxel									
Wetland Mitigation Site (Resort Rd) (1133-03-82 1133-03-84 9202-07-83)	7%	7.0%							
WIS 29 Steel Fabrication (1133-03-83)	0%	0.0%							
Orange Ln-LarsenRd Clearing&Grubbing (1133-04-78)	16%	18.5%							
US 41/STH 29 Intchg Wick Drain (1133-04-88)	7%	7.0%							
Hemlock Creek Box Culvert									
Dutchman's Creek Box Culvert	8%	11.3%							
Orange Ln - Glory Rd Mainline									
Ashland Ave B-05-110 & 120 Painting									
Main Ave (CTH G) Intchg									
Main Ave Intchg Stormwater Pond									
Main Ave Park & Ride									
Calaway Stormwater Pond (1133-06-71 1133-06-75 1133-06-80 1133-06-84 1133-06-86 1133-06-89)	8%	8.0%							
Scheuring Rd (CTH F) Intchg (1133-06-72)	8%	5.1%							
CTH F/MidValley Rd Re-alignment									
CTH G/MidValley Rd Re-alignment (1133-06-77 1133-06-81)	10%	10.9%							
Scheuring Road Lighting (1133-06-78)	12%	32.9%							
Glory Rd Bridge B-05-615 (1133-09-72)	7%	4.3%							
CTH RK (S Fmt Rd) E(Dck Crk-CTH EB)									
Parkside Court Noisewalls									
WIS 29/CTHEB South Stormwater Pond (9202-07-72 9202-07-75 9202-08-81)	9%	9.4%							
STH 29 Mainline (CTH J-Duck Creek)									
CTH RK South Frontage Rd Park & Ride									
Duck Creek B-05-85 & 651 (9202-07-73 9202-08-75 9202-08-84)	9%	10.5%							
Shawano Ave/Taylor St Intrscn TMP									
Shawano Ave/Taylor St Intersection									
Old Shawano Ave Connection (9202-07-74 9202-07-79 9202-07-80)	10%	14.7%							
Pckrind/Dalusman/Shawano Temp Signals (9202-07-84)	10%	1.2%							
Shawano, Southview, Viewpoint Oblit (9202-08-74)	11%	12.1%							
CTH EB / CN Railroad-Grading&Culverts (9202-08-79)	12%	14.8%							
CTH RK West-(CTH J-DuckCrk)									
CTH J Underpass Structures (9202-08-85 9202-08-86)	8%	11.3%							
Brown - Construction Contracting Subtotal									
Construction Contracting Total									



Program Financial Summary

Components	Current Budget	Projected Budget	Paid to Date
Design	\$ [REDACTED]	[REDACTED]	[REDACTED]
Public Relations/Public Involvement	\$ [REDACTED]	[REDACTED]	[REDACTED]
Program Controls	\$ [REDACTED]	[REDACTED]	[REDACTED]
Real Estate	[REDACTED]	[REDACTED]	[REDACTED]
Utility	[REDACTED]	[REDACTED]	[REDACTED]
Safety Program	[REDACTED]	[REDACTED]	[REDACTED]
Construction	[REDACTED]	[REDACTED]	[REDACTED]
TOTAL	[REDACTED]	[REDACTED]	[REDACTED]

Reserve Program Estimates

Project ID	Project Name - Description of Change	Adjustment Value
Program Estimate Debits		
Design		
9202-07-01	Additional Design	\$ [REDACTED]
		[REDACTED]
	Total Design Debit	[REDACTED]
Real Estate		
1133-09-21	Additional Delivery	\$ [REDACTED]
		[REDACTED]
	Total Real Estate Debit	\$ [REDACTED]
Utility		
Multiple	Programming adjustment	\$ [REDACTED]
1133-06-51	Additional Utility (JV for 90/10 split)	\$ [REDACTED]
		[REDACTED]
	Total Utility Debit	\$ [REDACTED]
Construction		
Multiple	January and February 2012 Letting	\$ [REDACTED]
		[REDACTED]
	Total Construction Debit	\$ [REDACTED]
	Total Program Estimate Debits	[REDACTED]
Program Estimate Credits		
Design		
		\$ -
	Total Design Credit	\$ -
Real Estate		
		\$ -
	Total Real Estate Credit	\$ -
Utility		
9202-07-45	Utility IDs Closed (Remaining Utility Balance)	\$ [REDACTED]
		[REDACTED]
	Total Utility Credit	\$ [REDACTED]
Construction		
Multiple	Programming adjustment	\$ [REDACTED]
		\$ -
		\$ -
	Total Construction Credit	\$ [REDACTED]
	Total Program Estimate Credits	[REDACTED]
	Net Program Estimate (Debit)	[REDACTED]



Reserve Change Management

Project ID	Project Name - Description of Change	Adjustment Value
Change Management Debits		
Design		
		\$ -
	Total Design Debit	\$ -
Real Estate		
		\$ -
	Total Real Estate Debit	\$ -
Utility		
		\$ -
	Total Utility Debit	\$ -
Construction		
1120-09-83	Brzwd Intchg & US 45 to Brzwd NB Widening (CM#42)	\$ [REDACTED]
1120-11-83	US 45 Intchg (CM#14)	\$ [REDACTED]
1133-03-82	Early Structures/Early Fill (CM#14)	\$ [REDACTED]
1133-04-75	Lambeau Street, City of Green Bay (PO Closeout)	\$ [REDACTED]
9202-07-72	CTH RK E (Duck Creek - CTH EB) (CM#13)	\$ [REDACTED]
9202-08-81	WIS 29/CTH EB South Stormwater Pond (CM#17)	\$ [REDACTED]
	Total Construction Debit	\$ [REDACTED]
	Total Change Management Debits	\$ [REDACTED]
Change Management Credits		
Design		
		\$ -
	Total Design Credit	\$ -
Real Estate		
		\$ -
	Total Real Estate Credit	\$ -
Utility		
		\$ -
	Total Utility Credit	\$ -
Construction		
1120-11-75	WIS 21 Intchg & Lk BdM Csway (CM#4)	\$ [REDACTED]
9202-07-73	WIS 29 ML (CTH J - Duck Creek) & EB Ramps (CM#2)	\$ [REDACTED]
9202-08-85	CTH RK West (CTH J - Duck Creek) (CM#24)	\$ [REDACTED]
	Total Construction Credit	\$ [REDACTED]
	Total Change Management Credits	\$ [REDACTED]
	Net Change Management (Debit)	\$ [REDACTED]

	January	February
ESTIMATED PROGRAM COSTS	[REDACTED]	[REDACTED]
DESIGN RESERVE *	[REDACTED]	[REDACTED]
REAL ESTATE RESERVE *	[REDACTED]	[REDACTED]
UTILITY RESERVE *	[REDACTED]	[REDACTED]
CONSTRUCTION RESERVE *	[REDACTED]	[REDACTED]
ESTIMATED PROGRAM RESERVES	[REDACTED]	[REDACTED]

* Includes: Design-Contingency
 R/E- Litigation, Contingency, Reserve
 Ut- Contingency, Reserve
 Construction- CCO, Program Reserve



TOP ISSUE LIST*

Item	Issue	Status	Action Required	Completion Date	Drop-Dead Date	Ball in Court
Construction Cost Estimating	Construction cost estimating variability, creating program instability and impacting design delivery schedules.	Project Team maintains a database of bid prices for the US 41 Project and a Cost Estimate Validation Process.	Continue to evaluate bid prices, develop database and validation process.	N/A	N/A	Brian Roper
CN Rail Abandonment	The existing CN rail crossing of Packerland Drive adjacent to the new WIS 29/Packerland Drive Interchange will result in safety and operational issues.	Railroad agreements were approved	Continue coordination with CN and Bureau to get track removed by Summer 2012.	Summer 2012	Fall 2012	Paul Vraney
North Segment (Brown County) ATC Relocation	Several large ATC transmission towers will need to be relocated prior to reconstruction of the North Segment. ATC has a planned window for de-energizing the transmission line. Significant money and schedule can be saved if WisDOT can coordinate the project impacts with the schedule shut-down.	Utility agreement for design approved by FHWA. Development of a relocation concept that accommodates both alternatives is complete. Proposed alignment submitted by ATC. Design team working on staging/scheduling plan.	The US 41 team and ATC will continue coordination for relocation.	Summer 2012	Fall 2012	Paul Vraney
Planned Development along Corridor	Developers requesting changes & quick decisions to accommodate development.	On-going	Meetings with developers and businesses as needed. Design adjustments where possible.	N/A	N/A	Chad DeGrave
Green Bay Packers Development along Lombardi Ave	The Green Bay Packers have plans for significant development and redevelopment along Lombardi Avenue. This project will be constructed (open to traffic) from April to September 2012.	Project Team is working with the Packers, Brown County and Ashwaubenon.	Argonne Street intersection improvement to be built in 2013.	Fall 2012	Fall 2012	Kurt Peters

***Issue** - Items of concern that are being MANAGED by the Project Team with specific sequential actions required to mitigate a least impactful resolution.



TOP RISK LIST*

Item	Risk	Impact	Action Required	Drop-Dead Date	Ball in Court
Construction Prices (Escalation)	Variability of construction prices	Impact on budget	Continuous monitoring of construction prices	N/A	NE Region
Real Estate (Brown County)	Real estate prices have escalated	Impact on budget	Continue to monitor real estate prices and adjust real estate budget	N/A	NE Region
	Complex real estate appraisals & relocations	Impact on schedule	Engage legal counsel on issues	On-going	NE Region Real Estate
Geotech/Soils	Complex geotechnical issues requiring mitigation and evaluation of risk for the department	Impact on budget and schedule	Continuous monitoring	On-going	NE Region/Central Office Soils

**Risk - Items of concern that are outside the direct control of the Project Team but are being MONITORED to mitigate the impact wherever possible.*

CONSTRUCTION LET PROJECTS FINANCIAL SUMMARY – Winnebago County
Thru February 2012

County	Project Status	Project ID	Project	Contract PTD Amount	Original Contract Amount	Approved Contract Changes	Approved Contract Amount	Original Contract vs. Approved Contract	Pending Contract Changes	Projected Cost at Complete	Original Contract vs. Projected Contract	% Complete Based on PTD	% Complete Based on Time	Change from Last End of Month Projected Cost at Complete	
WINNEBAGO COUNTY															
															0
	Winnebago County Total =														

Project Status

- A - Project Let - Work Not Started
- B - Under Construction
- C - Construction Contract Time Complete
- D - Contractor PO Closed in EAPS
- E - Project Closed in FIIPS except for journal vouchers

Notes:

1. < > Represents ARRA Projects
2. If percent complete based on time is greater than 100%, it is due to contractor not completing project by the required contract completion date.
3. Information obtained from Contract Manager.
4. Percent complete based in PTD uses projected cost at complete.



**CONSTRUCTION LET PROJECTS FINANCIAL SUMMARY – Brown County
Thru February 2012**

County	Project Status	Project ID	Project	Contract PTD Amount	Original Contract Amount	Approved Contract Changes	Approved Contract Amount	Original Contract vs. Approved Contract	Pending Contract Changes	Projected Cost at Complete	Original Contract vs. Projected Contract	% Complete Based on PTD	% Complete Based on Time	Change from Last End of Month Projected Cost at Complete	
BROWN COUNTY															
	Brown County Total =														
	Corridor Total =														

Project Status

- A - Project Let - Work Not Started
- B - Under Construction
- C - Construction Contract Time Complete
- D - Contractor PO Closed in EAPS
- E - Project Closed in FIIPS except for journal vouchers

Notes:

1. < > Represents ARRA Projects
2. If percent complete based on time is greater than 100%, it is due to contractor not completing project by the required contract completion date.
3. Information obtained from Contract Manager.
4. Percent complete based in PTD uses projected cost at complete.



CONSTRUCTION TASKS SUMMARY

WINNEBAGO COUNTY

Tasks Accomplished This Month

- **1120-11-83** (*US 45 Interchange*)
 - Winter Suspension.
- **1120-10-72,73,79** (*9th Ave Intchg*), (*WIS 44 to WIS 21 – US 41 Mainline*), (*WIS 44 B70-138 Bridge Staining*)
 - Winter Suspension
- **1120-10-78,80** (*WIS 26 – B-70-200 Staining, WIS 26 – WIS 44 Mainline*)
 - Winter Suspension
- **1120-09-71** (*US 45 to Breezewood Lane Mainline*)
 - Winter Suspension
- **1120-11-75,84** (*WIS 21 Interchange & Lk BDM Csway, Weigh in Motion*)
 - Continued building piers for B-70-266
- **1120-11-76** (*WIS 21 Intchg & Lk Bdm Csway Fencing*)
 - No Work Scheduled

Task Scheduled Next Month

- **1120-11-83** (*US 45 Interchange*)
 - Adjust bearings and begin decking B-70-269.
- **1120-10-72,73,79** (*9th Ave Intchg*), (*WIS 44 to WIS 21 – US 41 Mainline*), (*WIS 44 B70-138 Bridge Winter Suspension*)
- **1120-10-78,80** (*WIS 26 – B-70-200 Staining, WIS 26 – WIS 44 Mainline*)
 - Winter Suspension
- **1120-09-71** (*US 45 to Breezewood Lane Mainline*)
 - Winter Suspension
- **1120-11-75,84** (*WIS 21 Interchange & Lk BDM Csway, Weigh in Motion*)
 - Complete piers for B-70-266 and begin erecting girders.
- **1120-11-76** (*WIS 21 Intchg & Lk Bdm Csway Fencing*)
 - Pre-Construction Conference

BROWN COUNTY

Tasks Accomplished This Month

- **1133-03-83** (*WIS 29 Steel Fabrication*)
 - B-5-660: Complete fabrication
 - B-5-661: Complete with fabrication and paint.
 - B-5-658: Complete with fabrication and paint.
 - Completed bearing plates for all 3 structures.
- **1133-06-72** (*Scheuring Road (CTH F) Intchg*)
 - Winter Suspension
- **1133-09-72** (*Glory Rd Bridge B-05-615*)
 - Winter Suspension.
- **9202-08-85,86** (*CTH RK (South Frontage Rd.) West (CTH J – Duck Creek), CTH J Underpass Structures*)
 - Finished re-grouting and testing the tiebacks for the retaining wall under WIS 29.
- **1133-03-82,84,9202-07-85** (*Early Structures/Early Fill, Beaver Dam Creek Box Culvert @ Van Boxtel, Wetland Mitigation Site (Resort Road)*)
 - Completed concrete masonry piers for structures B-05-654, B-05-655 & B-05-642.
 - Continued to work on construction of MSE walls to allowable lifts base on settlement.
 - Start concrete footings for MSE wall stand up concrete panels on Larson St and started placing panels.
 - Start Forming and pouring abutments for B-05-646 & 647.
 - Started Construction of Box Culvert B-05-690.
- **9202-08-79** (*CTH EB/CN Railroad – Grading & Culverts*)
 - Winter Suspension
- **1133-03-72,04-84** (*Mason St (WIS 54) Interchange, Ninth St – Larsen Rd Mainline*)
 - Closed down the Mason Street Interchange.
 - Completed demolition of the existing Mason Street Bridge over US 41.
 - Completed structure excavation and started pile driving for B-5-637 (Mason over US 41).
 - Prepared for deck pour on Bridge B-5-635 (US 41 NB over 9th St.)
 - Continued work on Retaining Wall R-5-223, R-5-222, R-5-227 & R-5-230.
- **1133-04-78** (*Orange Ln - Ninth St & Larsen Rd - Memorial Dr Clearing & Grubbing*)
 - Continued clearing, grubbing, and restoration along Pilgrim Way.
- **9202-07-84** (*Packerland Dr/Dousman St/Shawano Ave Temporary Traffic Signals*)
 - Installed pedestrian signals at the intersection of Cormier & Packerland.
- **1133-06-71,75,80,84,86,89** (*Glory Rd – Morris Ave Mainline, Nain Ave (CTH G) Intchg, Main Ave Intchg Stormwater Pond, Calaway Stormwater Pond, Main Ave Park & Ride, Ashland Ave B-05-119 & 120 Painting*)
 - None
- **9202-07-73,08-75,84** (*WIS29 Mainline (CTH J-Duck Creek), CTH EB Ramps, US 41 SB Off ramp, New Shawano Ave, WIS 29/CTH EB North Stormwater Pond, Shawano Ave Cul-de-sac South, Duck Creek B-05-650 & 651, CTH RK (South Frontage Rd) Park & Ride*)
 - Razed buildings and cleared and grubbed trees & brush in conflict with project.
 - Began storm sewer work.
- **1133-03-78** (*Lombardi Ave (CTH VK) Interchange*)
 - Project Let
- **1133-10-84** (*North Segment Razing/Removal Phase 1*)
 - Project Let

Tasks Scheduled Next Month

- **1133-03-83** (WIS 29 Steel Fabrication).
 - B-5-660: Begin cycling tubs through paint shop.
 - B-5-660: Continued assembly of Unit-1&3.
- **1133-06-72** (Scheuring Road (CTH F) Intchg)
 - Winter Suspension
- **1133-09-72** (Glory Rd Bridge B-05-615)
 - Winter Suspension
- **9202-08-85,86** (CTH RK (South Frontage Rd.) West (CTH J – Duck Creek), CTH J Underpass Structures)
 - Begin placing concrete for the retaining wall faces under WIS 29 and continue work on pilasters.
 - Begin excavation. Storm sewer work and grading on CTH J north of WIS 29.
 - CTH J under WIS 29 will be closed once retaining wall work starts, around the middle of March.
- **1133-03-82,84,9202-07-85** (Early Structures/Early Fill, Beaver Dam Creek Box Culvert@ Van Bortel, Wetland Mitigation Site (Resort Road))
 - Continue work on the construction of MSE walls to allowable lifts base on settlement.
 - Continue placing concrete panels for retaining walls throughout project.
 - Complete the forming and pouring of the abutments for B-05-646 and B-05-647, set the concrete girders and start decking.
 - Complete the construction of B-05-690 Box Culvert, and start backfilling.
 - Start back up on the Storm Sewer operations.
- **9202-08-79** (CTH EB/CN Railroad – Grading & Culverts)
 - Winter Suspension
- **1133-03-72,04-84** (Mason St (WIS 54) Interchange, Ninth St – Larsen Rd Mainline)
 - Begin abutment and pier work for B-05-637.
 - Pour Deck for B-05-635 (US 41 NB over 9th Street) pending weather conditions.
 - Continue work on retaining walls.
 - Begin pavement removal and earthwork on Mason Street and Interchange ramps and continue storm sewer work.
- **1133-04-78** (Orange Ln - Ninth St & Larsen Rd - Memorial Dr Clearing & Grubbing)
 - No work scheduled for the month of March.
- **9202-07-84** (Packerland Dr/Dousman St/Shawano Ave Temporary Traffic Signals)
 - No work scheduled
- **9202-07-73,08-75,84** (WIS29 Mainline (CTH J-Duck Creek), CTH EB Ramps, US 41 SB Off ramp, New Shawano Ave, WIS 29/CTH EB North Stormwater Pond, Shawano Ave Cul-de-sac South, Duck Creek B-05-650 & 651, CTH RK (South Frontage Rd) Park & Ride)
 - Continue storm sewer work and bore 66-Inch pipe under STH 29.
 - Strip topsoil and begin placing strip drains.
 - Excavate detention pond and begin earthwork activities.
 - Install temporary barrier wall and traffic control items as required.
- **1133-06-71,75,80,84,86,89** (Glory Rd – Morris Ave Mainline, Main Ave (CTH G) Intchg, Main Ave Intchg Stormwater Pond, Calaway Stormwater Pond, Main Ave Park & Ride, Ashland Ave B-05-119 & 120 Painting)
 - Pre-Construction Conference.
 - Shift USH 41 Mainline traffic to outside lanes.
 - Demolition of multiple bridges.
 - Begin removals and roadwork on SUH 41 and CTH G.
 - Begin grading and storm sewer work on USH 41 from Orange Lane to CTH G.
- **1133-03-78** (Lombardi Ave (CTH VK) Interchange)
 - Pre-Construction Conference.
- **1133-10-84** (North Segment Razing/Removal Phase 1)
 - Pre-Construction Conference.

2012 Construction Outlook – Winnebago County

The 2012 construction season will continue to be busy with the completion of the US 45 and WIS 21 interchanges and the construction of the Lake Butte des Morts Causeway. Additionally, crews will continue paving the mainline segments from US 45 to Brezewood Lane and from Witzel Avenue to US 45.

US 41 Mainline Paving

Construction: (US 45 to Brezewood Lane) April 2011 through June 2013; (Witzel Avenue to US 45) August 2011 through July 2013

Reconstruction of northbound US 41 lanes. The US 41 mainline will have two lanes of traffic in each direction. Expect periodic night-time lane CLOSURES from 7 p.m. to 5 a.m.

Lake Butte des Morts Causeway

Construction: September 2011 through September 2013

Construction began in September 2011 on three new bridge structures on the new southbound lanes west of the existing roadway. Two lanes of traffic will remain open in both directions, but lanes and shoulders will be narrow; motorists may experience temporary night-time CLOSURES as trucks and equipment move in and out of the work zone.

US 45 Interchange PARTIALLY CLOSED

Construction: August 2010 through August 2012

Completion of the interchange to provide free-flow movements between US 41 and US 45.


The northbound entrance and exit ramps at US 41 and the northbound flyover ramp to US 45 will be CLOSED until July 2012.

WIS 21 Interchange CLOSED

Construction: August 2011 through November 2012

Reconstruct the existing interchange and roundabouts on WIS 21 and ramp ends, including bicycle and pedestrian accommodations.

The interchange will CLOSE from March through November 2012. Movements to North Washburn Street/Brooks Lane and Rath Lane will always be available via WIS 21 and/or local street connections.

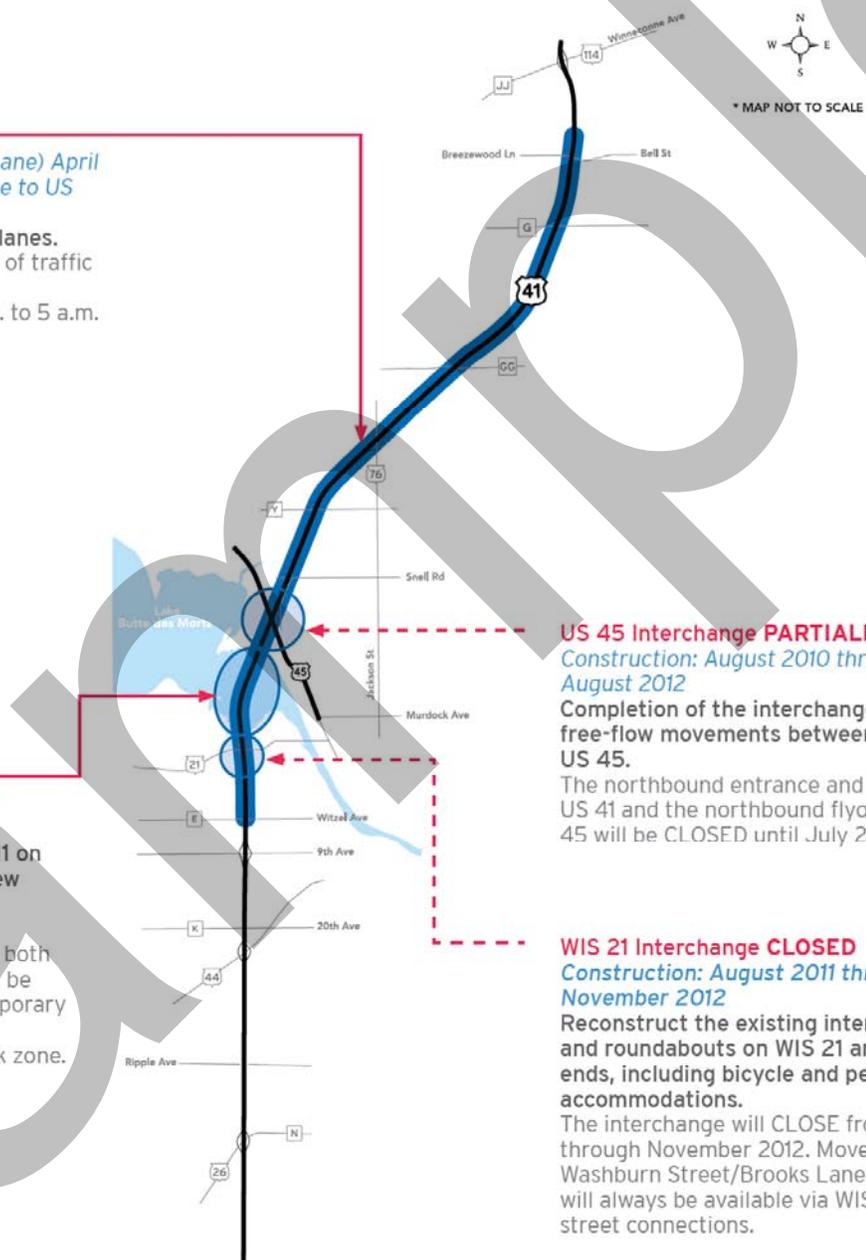

2012 Construction Outlook – Brown County

Major construction ramps up in Brown County in 2012. The County G, Lombardi Avenue and Mason Street interchanges will be reconstructed. The reconstruction of mainline segments from Orange Lane to Glory Road and 9th Street to Memorial Drive will be fully underway in 2012.

New Shawano Avenue and Packerland Drive (County EB)

Construction: March 2012 through November 2012

Construction of new Shawano Avenue, located north of the existing WIS 29 facility, along with ramps connecting Packerland Drive with WIS 29 to and from the west.

Traffic will utilize existing WIS 29 and Packerland Drive (County EB) during construction of the new facilities.

WIS 29 Mainline (County J to Duck Creek)

Construction: March 2012 through November 2012

Reconstruction of the WIS 29 mainline.

Two lanes of traffic will be maintained on WIS 29 in each direction, with possible night-time lane CLOSURES. Access to and from Packerland Drive (County EB) will be maintained.

County RK and County J

Construction: June 2011 through May 2012
Completion of the County RK and County J construction near WIS 29.

In spring of 2012, County J will CLOSE for six weeks north of WIS 29. County RK will remain open to traffic with intermittent lane CLOSURES for paving operations.

Main Avenue (County G) Interchange CLOSED

Construction: April 2012 through November 2012

Reconstruction of Main Avenue interchange; expand and improve park and ride lot. Between April and July 2012, the US 41 southbound entrance ramp will CLOSE. All other ramps will remain open. County G under US 41 will also remain open with one lane of traffic in each direction. The interchange, including access across (under) US 41, will be CLOSED to traffic with no access to or from US 41 for 60 days between August through November 2012. The Lawrence Drive park and ride lot may be CLOSED from March to October 2012 – exact closure dates to be determined (see www.dot.wisconsin.gov/travel/parkride/brow.htm for alternate lots).

Lakeview Drive Bridge

Construction: August 2012 through December 2012

Reconstruction of the Lakeview Drive overpass.

Lakeview Drive at US 41 will be CLOSED while a new bridge is constructed over US 41.

Mason Street (WIS 54) Interchange CLOSED

Construction: February 2012 through August 2012

Reconstruction of Mason Street interchange.

The Mason Street interchange and bridge and Mason/Taylor intersection will be CLOSED starting February 2012 and will reopen August 2012.

Lombardi Avenue (County VK) Interchange

Construction: March 2012 through September 2012

Reconstruction of Lombardi Avenue interchange.


Lombardi Avenue will have two lanes open each direction throughout construction, with possible lane reductions at night. The one exception is from August to September when there will be one lane open in each direction along a short segment of Lombardi Avenue near Shady Lane. Access to and from US 41 will be maintained.

US 41 Mainline

Construction: (Orange Lane to Glory Road) March 2012 through June 2013; (9th Street to Larsen Road) September 2011 through October 2012; (Larsen Road to Memorial Drive) August 2012 through August 2014

Reconstruction of the US 41 mainline, including construction to replace box culverts along the mainline and the 9th Street bridge.

The US 41 mainline will have two lanes of traffic in each direction, with possible night-time lane CLOSURES.

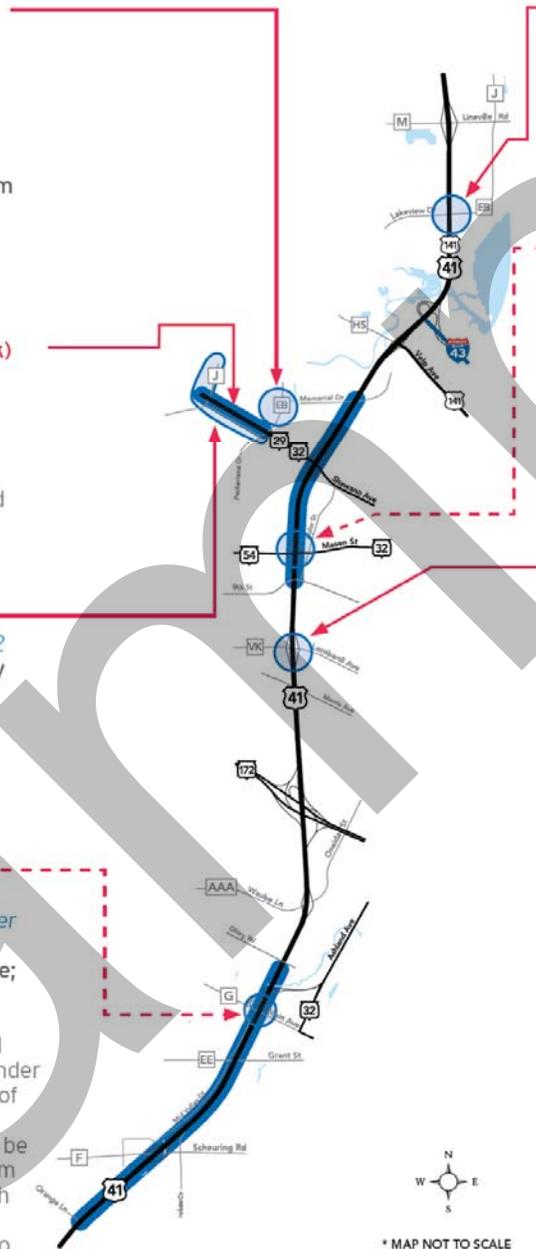

CONSTRUCTION PROJECT DETAIL

US 45 Interchange – 1120-11-83

Prime Contractor: Hoffman Construction Co.

Project Construction Leader: Kapur & Assoc.



Key Work Accomplished:

- Began decking on B-70-269 flyover ramp.

Key Work Scheduled:

- Continue decking on B-70-269.
- Install shear studs on B-70-269.

Public Relations:

- Working with local residents and business owners to address their questions.

Current Contract Status

Date of Award	July 1, 2010
Notice to Proceed	June 25, 2010
Original Contract Completion	Sept. 7, 2012
DBE Goal/Committed	7%/7%
Anticipated/Actual Completion	Sept. 7, 2012

Category	Contract Amount	Approved Changes	Total	Pending Changes	Cost At Complete	Paid-To-Date
WisDOT Management	\$ [REDACTED]	[REDACTED]	[REDACTED]	\$ -	\$ [REDACTED]	[REDACTED]
Consultant Services	\$ [REDACTED]	[REDACTED]	[REDACTED]	\$ [REDACTED]	\$ [REDACTED]	[REDACTED]
Prime Contractor	\$ [REDACTED]	[REDACTED]	[REDACTED]	\$ [REDACTED]	[REDACTED]	[REDACTED]
Change Allowance	\$ [REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]	[REDACTED]
Total	\$ [REDACTED]	[REDACTED]	[REDACTED]	\$ [REDACTED]	[REDACTED]	[REDACTED]

Activity Name	Original Duration	Start	Finish	2012												
				Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec		
11201183 USH 45 Interchange (Hoffman Constr	668	01-Feb-10 A	07-Sep-12													
PS&E FINAL (DUE IN MADISON) - USH 45 Interchange	1	01-Feb-10 A	01-Feb-10 A													
PS&E Ready For Letting - USH 45 Interchange	1	05-Jun-10 A	05-Jun-10 A													
Award - USH 45 Interchange	20	09-Jun-10 A	01-Jul-10 A													
Issue Construction NTP - USH 45 Interchange	1	27-Jul-10 A	27-Jul-10 A													
Construction - P - USH 45 Interchange	537	04-Aug-10 A	07-Sep-12*													
..... USH 41 NB Widening - Stage 1A - USH 45 Interchange	59	04-Aug-10 A	05-Oct-10 A													
..... Construct Temporary By Pass - Stage 1A - USH 45 Interchange	22	04-Aug-10 A	04-Nov-10 A													
..... Construction - Stage 1A - USH 45 Interchange	69	04-Aug-10 A	04-Nov-10 A													
..... 45/41 NB On Ramp Closure - Stage 1A - USH 45 Interchange	22	20-Aug-10 A	03-Sep-10 A													
..... Stage 1b - Winter Shut Down - USH 45 Interchange	99	13-Nov-10 A	01-Mar-11 A													
..... Close USH NB 45/41 & On/Off Ramps - Stage 1B - USH 45 Interch	1	04-Apr-11 A	04-Apr-11 A													
..... Construction - Stage 1B - USH 45 Interchange	11	04-Apr-11 A	14-Apr-11 A													
..... Complete Construction ; Traffic Switch to USH 41 NB Lanes - Stag	11	04-Apr-11 A	02-May-11 A													
..... Construction - Stage 3A - USH 45 Interchange	149	14-Apr-11 A	01-Mar-12													
..... Construction - Stage 2A - USH 45 Interchange	80	15-Apr-11 A	06-Sep-11 A													
..... Traffic Switch; USH 41 SB Traffic to New SB USH 41 Lanes - Stag	10	15-Aug-11 A	26-Aug-11 A													
..... Re Open Ramps ALB - Stage 2A - USH 45 Interchange	10	15-Aug-11 A	26-Aug-11 A													
..... Construction - Stage 2B - USH 45 Interchange	22	15-Aug-11 A	03-Oct-11 A													
..... Traffic Switch; All USH 41 Traffic to USH 41 SB Lanes - Stage 2B	0	03-Oct-11 A	03-Oct-11 A													
..... Re Open USH 45 & Ramps ALA, ALB, & ALG - Stage 3A - USH 45	0	05-Dec-11 A	05-Dec-11 A													
..... Stage 3B - Winter Shut Down - USH 45 Interchange	44	01-Feb-12 A	02-Apr-12													
..... Construction - Stage 3B - USH 45 Interchange	54	03-Apr-12*	18-Jun-12													
..... Traffic Switch; USH 41 NB to New USH 41 NB Lanes - Stage 3B -	1	18-Jun-12*	18-Jun-12													
..... Re Open Ramps ALC, ALD, & ALF - Stage 3D - USH 45 Interchan	1	18-Jun-12*	18-Jun-12													
..... Construction - Stage 4A - USH 45 Interchange	22	20-Jun-12*	20-Jul-12													
..... Traffic Switch; All USH 41 Traffic to New USH 41 SB Lanes - Stag	1	20-Jul-12*	20-Jul-12													
..... Construction - Stage 4B - USH 45 Interchange	28	30-Jul-12*	06-Sep-12													
..... All Work Complete - Stage 4B - USH 45 Interchange	1	06-Sep-12*	06-Sep-12													

■ Actual Work
■ Remaining Work
■ Critical Remaining Work
◆ Milestone

MONTHLY PROGRESS REPORT SCHEDULE

March 2012

USH 45 Interchange; Project ID 1120-11-83

Data Date: 01-Mar-12
 Run Date: 13-Mar-12
 Page 1 of 1



CONSTRUCTION PROJECT DETAIL
Early Structures/Early Fill, Beaver Dam Creek Box Culvert, Wetland Mitigation Site (Resort Road) – 1133-03-82, 84, 9202-07-83 Bundled Projects
Prime Contractor: Hoffman Construction Co.
Project Construction Leader: DAAR



Key Work Accomplished:

- Completed concrete masonry piers for structures B-05-654, B-05-655 & B-05-642.
- Continued to work on construction of MSE walls to allowable lifts base on settlement.
- Start concrete footings for MSE wall stand up concrete panels on Larson St and started placing panels.
- Start Forming and pouring abutments for B-05-646 & 647.
- Started Construction of Box Culvert B-05-690.

Key Work Scheduled:

- Continue work on the construction of MSE walls to allowable lifts base on settlement.
- Continue placing concrete panels for retaining walls throughout project.
- Complete the forming and pouring of the abutments for B-05-646 and B-05-647, set the concrete girders and start decking.
- Complete the construction of B-05-690 Box Culvert, and start backfilling.
- Start back up on the Storm Sewer operations.

Public Relations:

- Working with local residents and business owners to address their questions.

Current Contract Status

Date of Award	June 28, 2011
Notice to Proceed	July 22, 2011
Original Contract Completion	Oct. 5, 2012
DBE Goal/Committed	7%/7%

Category	Contract Amount	Approved Changes	Total	Pending Changes	Cost At Complete	Paid-To-Date
WisDOT Management	\$	\$ -	\$			
Consultant Services	\$		\$			
Prime Contractor	\$		\$	\$		
Change Allowance	\$	\$ -	\$			
Total	\$	\$	\$			

Activity Name	Original Duration	Start	Finish	2012											
				Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	
11330382 Early Structures / Early Fill	431	01-Feb-11 A	11-Oct-12												
PS&E FINAL (DUE IN MADISON) - Early Structures / Early Fill	1	01-Feb-11 A	01-Feb-11 A												
PS&E Ready For Letting - Early Structures / Early Fill	1	14-Jun-11 A	14-Jun-11 A												
Award - Early Structures / Early Fill	20	15-Jun-11 A	13-Jul-11 A												
Issue Construction NTP - Early Structures / Early Fill	1	22-Jul-11 A	22-Jul-11 A												
Construction ; P - Early Structures / Early Fill	304	25-Jul-11 A	11-Oct-12*												
11330384 Beaver Dam Creek Box Culvert @ Var	431	01-Feb-11 A	05-Dec-11 A												
PS&E FINAL (DUE IN MADISON) - Beaver Dam Creek Box Culvert @ V	1	01-Feb-11 A	01-Feb-11 A												
PS&E Ready For Letting - Beaver Dam Creek Box Culvert @ Van Boxtel	1	14-Jun-11 A	14-Jun-11 A												
Award - Beaver Dam Creek Box Culvert @ Van Boxtel	20	15-Jun-11 A	15-Jul-11 A												
Issue Construction NTP - Beaver Dam Creek Box Culvert @ Van Boxtel	1	22-Jul-11 A	22-Jul-11 A												
Construction ; P - Beaver Dam Creek Box Culvert @ Van Boxtel	309	25-Jul-11 A	05-Dec-11 A												
92020783 Wetland Mitigation Site (Resort Rd)	431	01-Feb-11 A	01-Jun-12												
PS&E FINAL (DUE IN MADISON) - Wetland Mitigation Site (Resort Rd)	1	01-Feb-11 A	01-Feb-11 A												
PS&E Ready For Letting - Wetland Mitigation Site (Resort Rd)	1	14-Jun-11 A	14-Jun-11 A												
Award - Wetland Mitigation Site (Resort Rd)	20	15-Jun-11 A	15-Jul-11 A												
Issue Construction NTP - Wetland Mitigation Site (Resort Rd)	1	22-Jul-11 A	22-Jul-11 A												
Construction ; P - Wetland Mitigation Site (Resort Rd)	309	25-Jul-11 A	01-Jun-12*												



CONSTRUCTION PROJECT DETAIL
WIS 21 Interchange & Lake Butte Des Morts Causeway, Weigh in Motion
1120-11-75, 84 Bundled Projects
Prime Contractor: Lunda Construction Co.
Project Construction Leader: Kapur



Key Work Accomplished:

- Completed building substructures units for B-70-266

Key Work Scheduled:

- Began installing false work to pour deck on B-70-266.
- Close the STH 21 Interchange around the 19th of March.
- Begin work on the temporary bypass and the STH 21 Interchange

Public Relations:

- Working with local residents and business owners to address their questions.

Current Contract Status

Date of Award	July 25, 2011
Notice to Proceed	Aug. 19, 2011
Original Contract Completion	July 26, 2013
DBE Goal/Committed	8%/6% GFW
Anticipated/Actual Completion	July 26, 2013

Category	Contract Amount	Approved Changes	Total	Pending Changes	Cost At Complete	Paid-To-Date
WisDOT Management	\$					
Consultant Services	\$					
Prime Contractor	\$					
Change Allowance	\$					
Total	\$					

Activity Name	Original Duration	Start	Finish	2012												2013						
				Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	
11201175 WIS 21 Intchg & Lk Bdrm Csway	635	01-Feb-11 A	25-Jul-13																			
PS&E FINAL (DUE IN MADISON) - STH 21 Interchange & Lake Butte Des Morts C	1	01-Feb-11 A	01-Feb-11 A																			
PS&E Ready For Letting - STH 21 Interchange & Lake Butte Des Morts C	1	12-Jul-11 A	12-Jul-11 A																			
Award - STH 21 Interchange & Lake Butte Des Morts Causeway	20	13-Jul-11 A	18-Jul-11 A																			
Issue: Construction NTP - STH 21 Interchange & Lake Butte Des Morts C	1	19-Jul-11 A	17-Aug-11 A																			
Construction ; P - STH 21 Interchange & Lake Butte Des Morts Causeway	490	25-Aug-11 A	25-Jul-13*																			
11201184 Weigh In Motion	660	01-Feb-11 A	25-Jul-13																			
PS&E FINAL (DUE IN MADISON) - Weigh-in-Motion	1	01-Feb-11 A	01-Feb-11 A																			
PS&E Ready For Letting - Weigh-in-Motion	1	12-Jul-11 A	12-Jul-11 A																			
Award - Weigh-in-Motion	20	13-Jul-11 A	09-Aug-11 A																			
Issue: Construction NTP - Weigh-in-Motion	1	17-Aug-11 A	17-Aug-11 A																			
Construction ; P - Weigh-in-Motion	514	25-Aug-11 A	25-Jul-13*																			

█ Actual Work
█ Remaining Work
█ Critical Remaining Work
◆ Milestone

MONTHLY PROGRESS REPORT SCHEDULE
 March 2012
 WIS 21 IC and LBDM Causeway; Project ID 1120-11-75
 Weigh-in-Motion; Project ID 1120-11-84

Date Date: 01-Mar-12
 Run Date: 13-Mar-12
 Page 1 of 1



CONSTRUCTION PROJECT DETAIL
Mason Street Interchange (WIS54), Ninth St. to Larsen Rd. Mainline
1133-03-72, 1133-04-84 Bundled Projects
Prime Contractor: Vinton Construction Co.
Project Construction Leader: OTIE



Key Work Accomplished:

- Closed down the Mason Street Interchange.
- Completed demolition of the existing Mason Street Bridge over US 41.
- Completed structure excavation and started pile driving for B-5-637 (Mason over US 41).
- Prepared for deck pour on Bridge B-5-635 (US 41 NB over 9th St.)
- Continued work on Retaining Wall R-5-223, R-5-222, R-5-227 & R-5-230.

Key Work Scheduled:

- Begin abutment and pier work for B-05-637.
- Pour Deck for B-05-635 (US 41 NB over 9th Street) pending weather conditions.
- Continue work on retaining walls.
- Begin pavement removal and earthwork on Mason Street and Interchange ramps and continue storm sewer work.

Public Relations:

- Working with local residents and business owners to address their questions.

Current Contract Status

Date of Award	Aug. 9, 2011
Notice to Proceed	Sept. 8, 2011
Original Contract Completion	Oct. 15, 2012
DBE Goal/Committed	7%/7%
Anticipated/Actual Completion	Oct. 15, 2012

Category	Contract Amount	Approved Changes	Total	Pending Changes	Cost At Complete	Paid-To-Date
WisDOT Management	\$					
Consultant Services	\$					
Prime Contractor	\$					
Change Allowance	\$					
Total	\$					

Activity Name	Origins Duration	Start	Finish	2012											
				Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct			
11330372 Mason Street / WIS 54 Interchange	402	22-Mar-11 A	02-Aug-12												
PS&E FINAL (DUE IN MADISON) - Mason St / WIS 54 Interchange	1	22-Mar-11 A	22-Mar-11 A												
PS&E Ready For Letting - Mason St / WIS 54 Interchange	1	12-Jul-11 A	12-Jul-11 A												
Award - Mason St / WIS 54 Interchange	20	12-Jul-11 A	25-Aug-11 A												
Issue Construction NTP - Mason St / WIS 54 Interchange	0	08-Aug-11 A	08-Aug-11 A												
Construction ; P - Mason St / WIS 54 Interchange	279	23-Aug-11 A	02-Aug-12												
11330484 Ninth St - Larsen Rd Mainline	402	22-Mar-11 A	15-Oct-12												
PS&E FINAL (DUE IN MADISON) - Ninth St - Larsen Rd Mainline	1	22-Mar-11 A	22-Mar-11 A												
PS&E Ready For Letting - Ninth St - Larsen Rd Mainline	0	12-Jul-11 A	25-Aug-11 A												
Award - Ninth St - Larsen Rd Mainline	20	12-Jul-11 A	09-Aug-11 A												
Issue Construction NTP - Ninth St - Larsen Rd Mainline	0	08-Sep-11 A	08-Sep-11 A												
Construction ; P - Ninth St - Larsen Rd Mainline	280	09-Sep-11 A	15-Oct-12												

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

MONTHLY PROGRESS REPORT SCHEDULE
 March 2012
 Mason Street/WIS 54 Interchange; Project ID 1133-03-72
 Ninth Street - Larsen Road Mainline; Project ID 1133-04-84

Date Date: 01-Mar-12
 Run Date: 13-Mar-12
 Page 1 of 1



CONSTRUCTION PROJECT DETAIL

WIS 29 Mainline (CTH J – Duck Creek), CTH EB Ramps, US 41 SB Off-ramp, New Shawano Ave., WIS 29/CTH EB North Stormwater Pond, Shawano Ave Cul-de-sac South, Duck Creek B-05-650 & 651, CTH RK (South Frontage Rd)

Park & Ride 9202-07-73, 08-75, 08-84

Prime Contractor: Hoffman Construction Co.

Project Construction Leader: DAAR Engineering



Key Work Accomplished:

- o Razed buildings and cleared and grubbed trees & brush in conflict with project.
- o Began storm sewer work.

Key Work Scheduled:

- o Continue storm sewer work and bore 66-Inch pipe under STH 29.
- o Strip topsoil and begin placing strip drains.
- o Excavate detention pond and begin earthwork activities.
- o Install temporary barrier wall and traffic control items as required.

Public Relations:

- Working with local residents and business owners to address their questions.

Current Contract Status

Date of Award	Dec. 22, 2011
Notice to Proceed	Feb. 06, 2012
Original Contract Completion	Nov. 26, 2012
DBE Goal/Committed	9%/10%
Anticipated/Actual Completion	Nov. 26, 2012

Category	Contract Amount	Approved Changes	Total	Pending Changes	Cost At Complete	Paid-To-Date
WisDOT Management	\$					
Consultant Services	\$					
Prime Contractor	\$					
Change Allowance	\$					
Total	\$					

Activity Name	Original Duration	Start	Finish	2012													
				Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec			
92020773 Wis 29 Mainline (CTH J-Duck Crk), CT	339	01-Aug-11 A	28-Nov-12														
PS&E FINAL (DUE IN MADISON) - WIS 29 ML(CTH J-Duck Crk), CTH E	1	01-Aug-11 A	01-Aug-11 A														
PS&E Ready For Letting - WIS 29 ML(CTH J-Duck Crk), CTH EB Ramps	1	13-Dec-11 A	13-Dec-11 A														
Award - WIS 29 ML(CTH J-Duck Crk), CTH EB Ramps, US 41 SB Offram	20	22-Dec-11 A	22-Dec-11 A														
Issue Construction NTP - WIS 29 ML(CTH J-Duck Crk), CTH EB Ramps	0	06-Feb-12 A	06-Feb-12 A														
Construction ; P - WIS 29 ML(CTH J-Duck Crk), CTH EB Ramps, US 41	185	05-Mar-12 A	26-Nov-12														
92020875 CTH RK (South Frontage Rd) Park & F	338	01-Aug-11 A	28-Nov-12														
PS&E FINAL (DUE IN MADISON) - CTH RK (South Frontage Rd) Park &	1	01-Aug-11 A	01-Aug-11 A														
PS&E Ready For Letting - CTH RK (South Frontage Rd) Park & Ride	1	13-Dec-11 A	13-Dec-11 A														
Award - CTH RK (South Frontage Rd) Park & Ride	20	22-Dec-11 A	22-Dec-11 A														
Issue Construction NTP - CTH RK (South Frontage Rd) Park & Ride	1	06-Feb-12 A	06-Feb-12 A														
Construction ; P - CTH RK (South Frontage Rd) Park & Ride	198	05-Mar-12 A	26-Nov-12														
92020884 Duck Creek B-05-650 & 651	330	01-Aug-11 A	28-Nov-12														
PS&E FINAL (DUE IN MADISON) - Duck Creek B-05-650 & 651	1	01-Aug-11 A	01-Aug-11 A														
PS&E Ready For Letting - Duck Creek B-05-650 & 651	1	13-Dec-11 A	13-Dec-11 A														
Award - Duck Creek B-05-650 & 651	20	22-Dec-11 A	22-Dec-11 A														
Issue Construction NTP - Duck Creek B-05-650 & 651	1	06-Feb-12 A	06-Feb-12 A														
Construction ; P - Duck Creek B-05-650 & 651	160	10-Apr-12*	26-Nov-12														

<p>Actual Work</p> <p>Remaining Work</p> <p>Critical Remaining Work</p> <p>Milestone</p>	<p>MONTHLY PROGRESS REPORT SCHEDULE</p> <p>March 2012</p> <p>WIS 29 Mainline; Project ID 9202-07-73</p> <p>CTH RK (South Frontage Rd) Park & Ride; Project ID 9202-08-75</p> <p>Duck Creek B-05-650/651; Project ID 9202-08-84</p>	<p>Data Date: 01-Mar-12</p> <p>Run Date: 19-Mar-12</p> <p>Page 1 of 1</p>
--	---	---





ATTACHMENTS


Sample




WINNEBAGO COUNTY CONTRACT LET PACKAGES

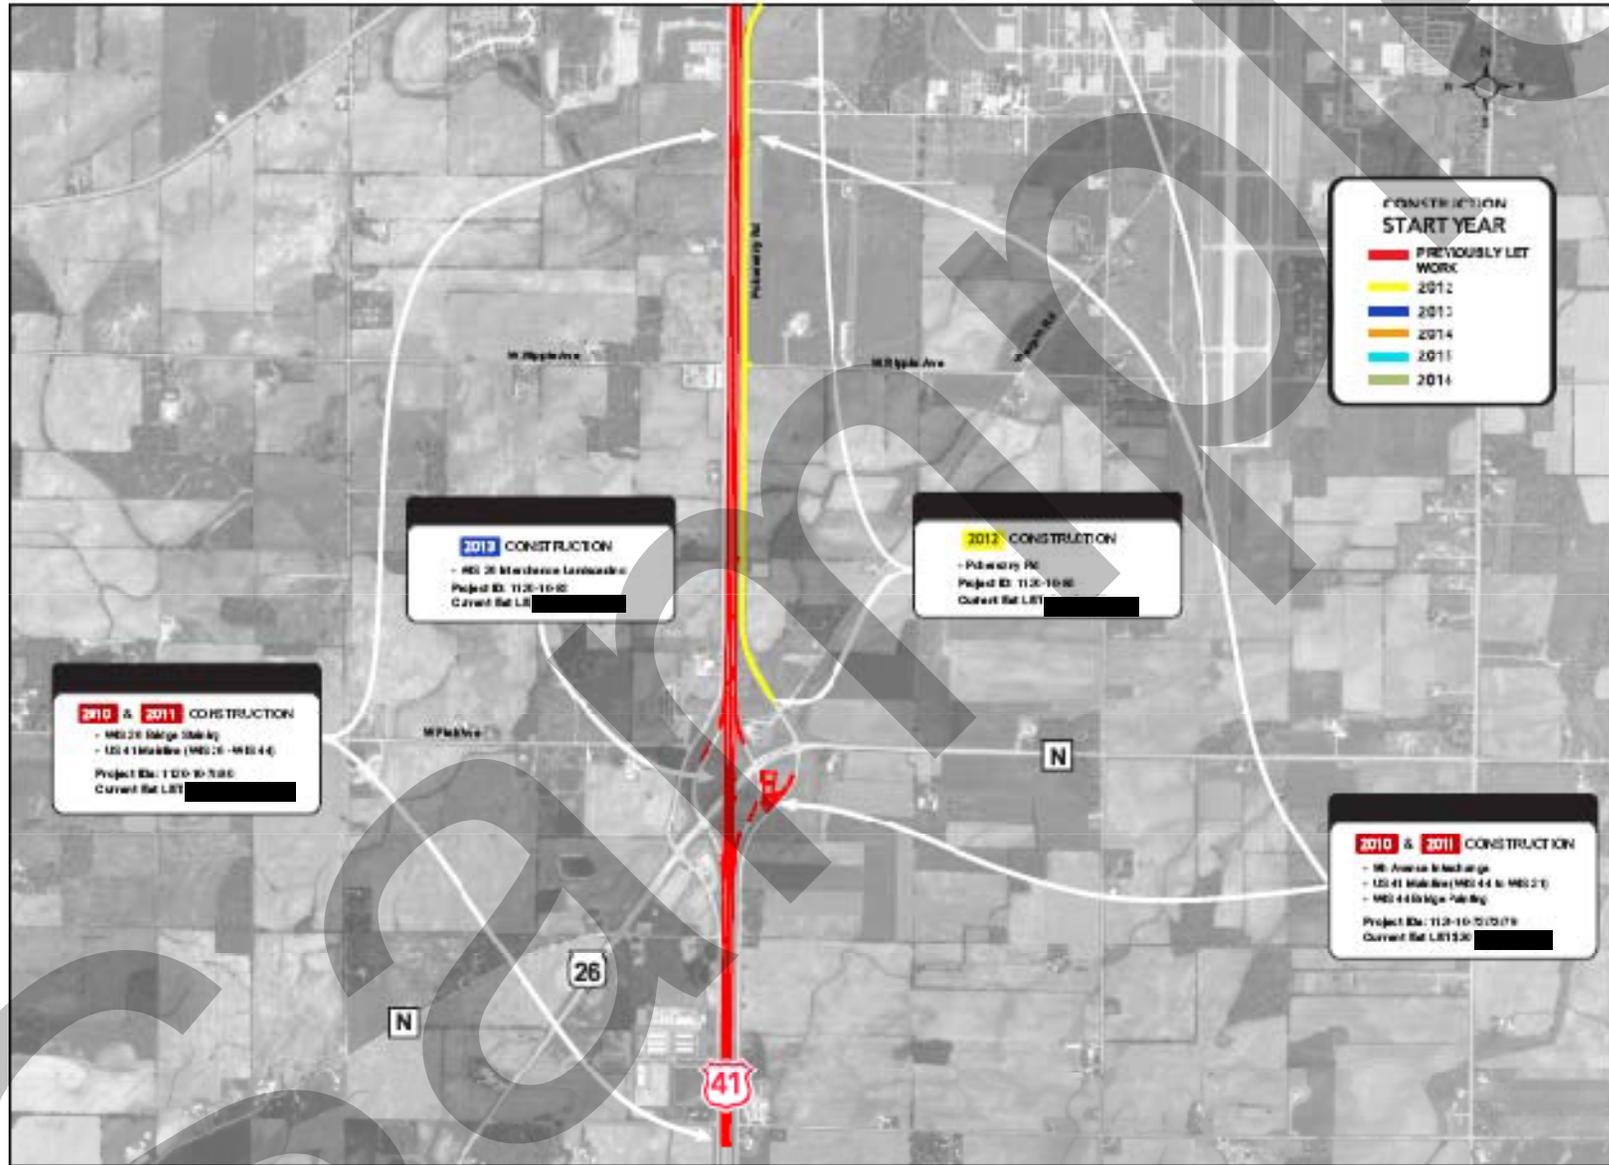

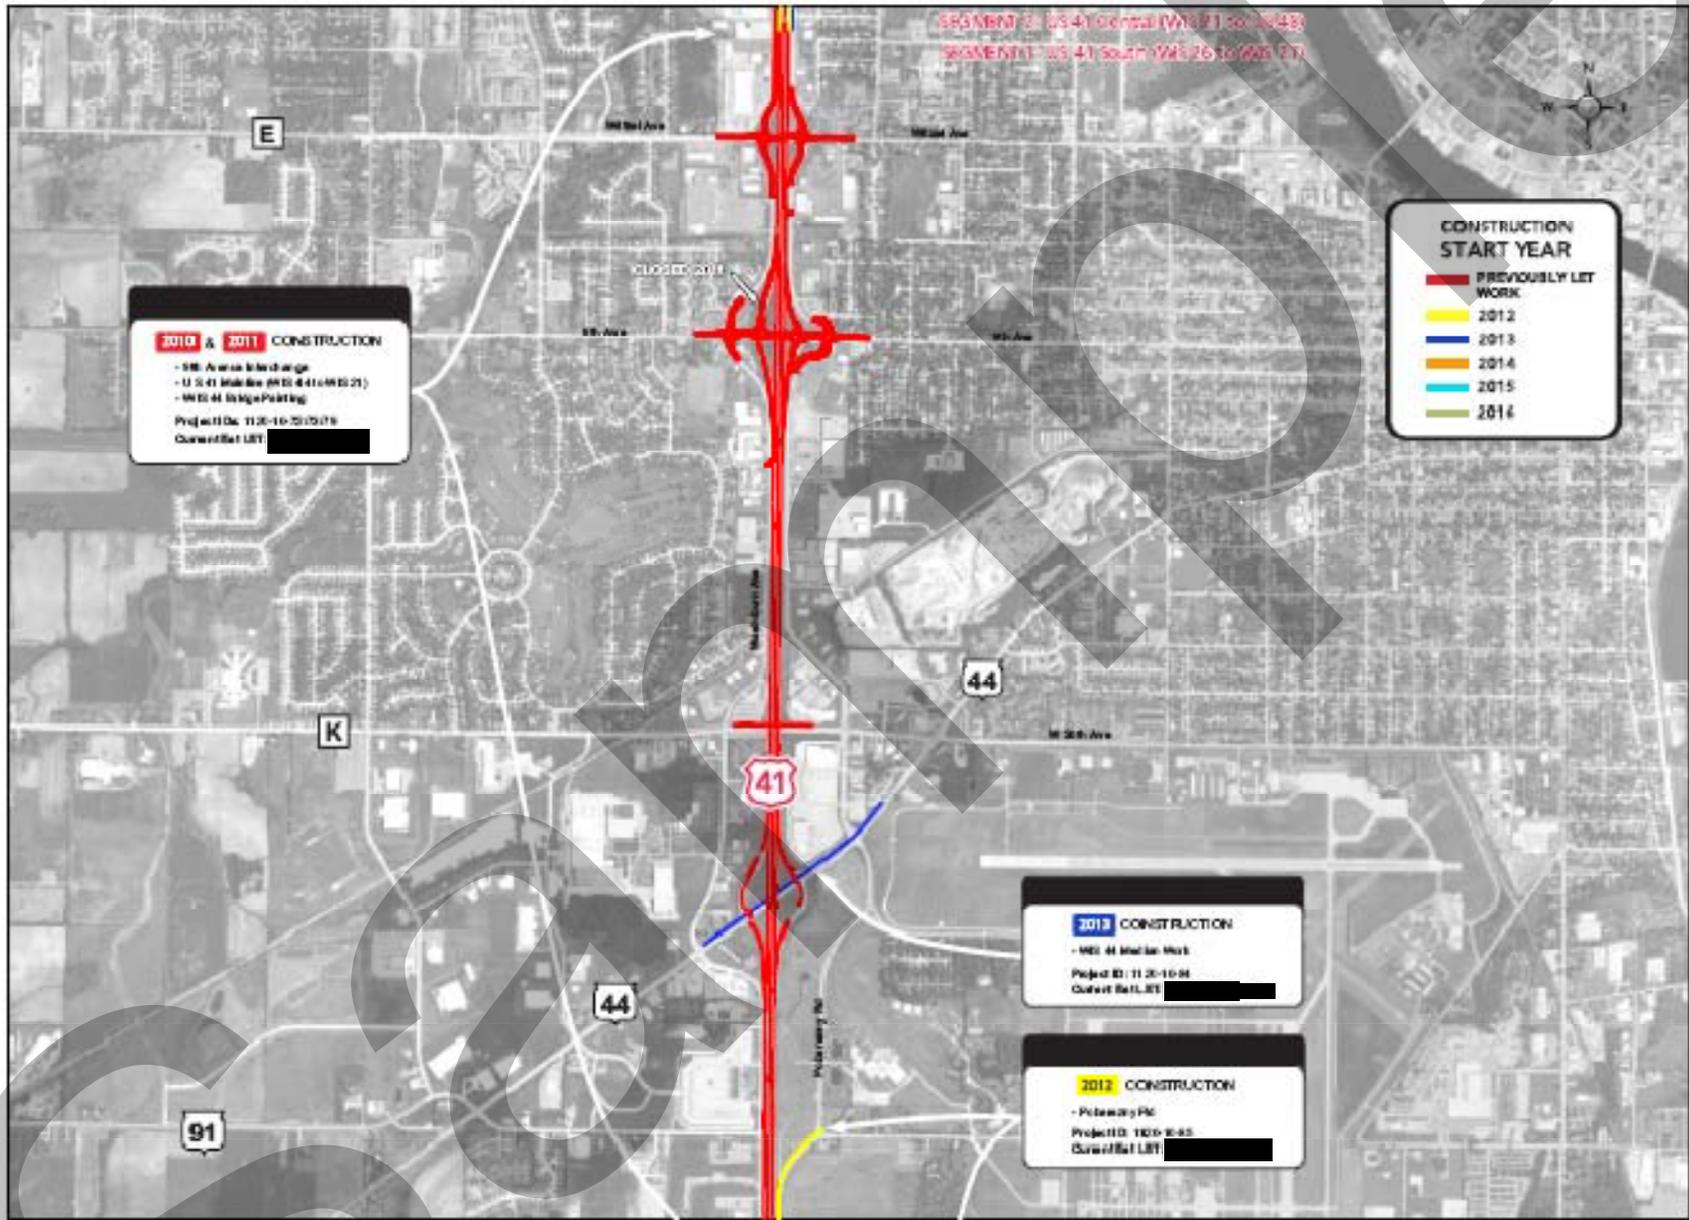


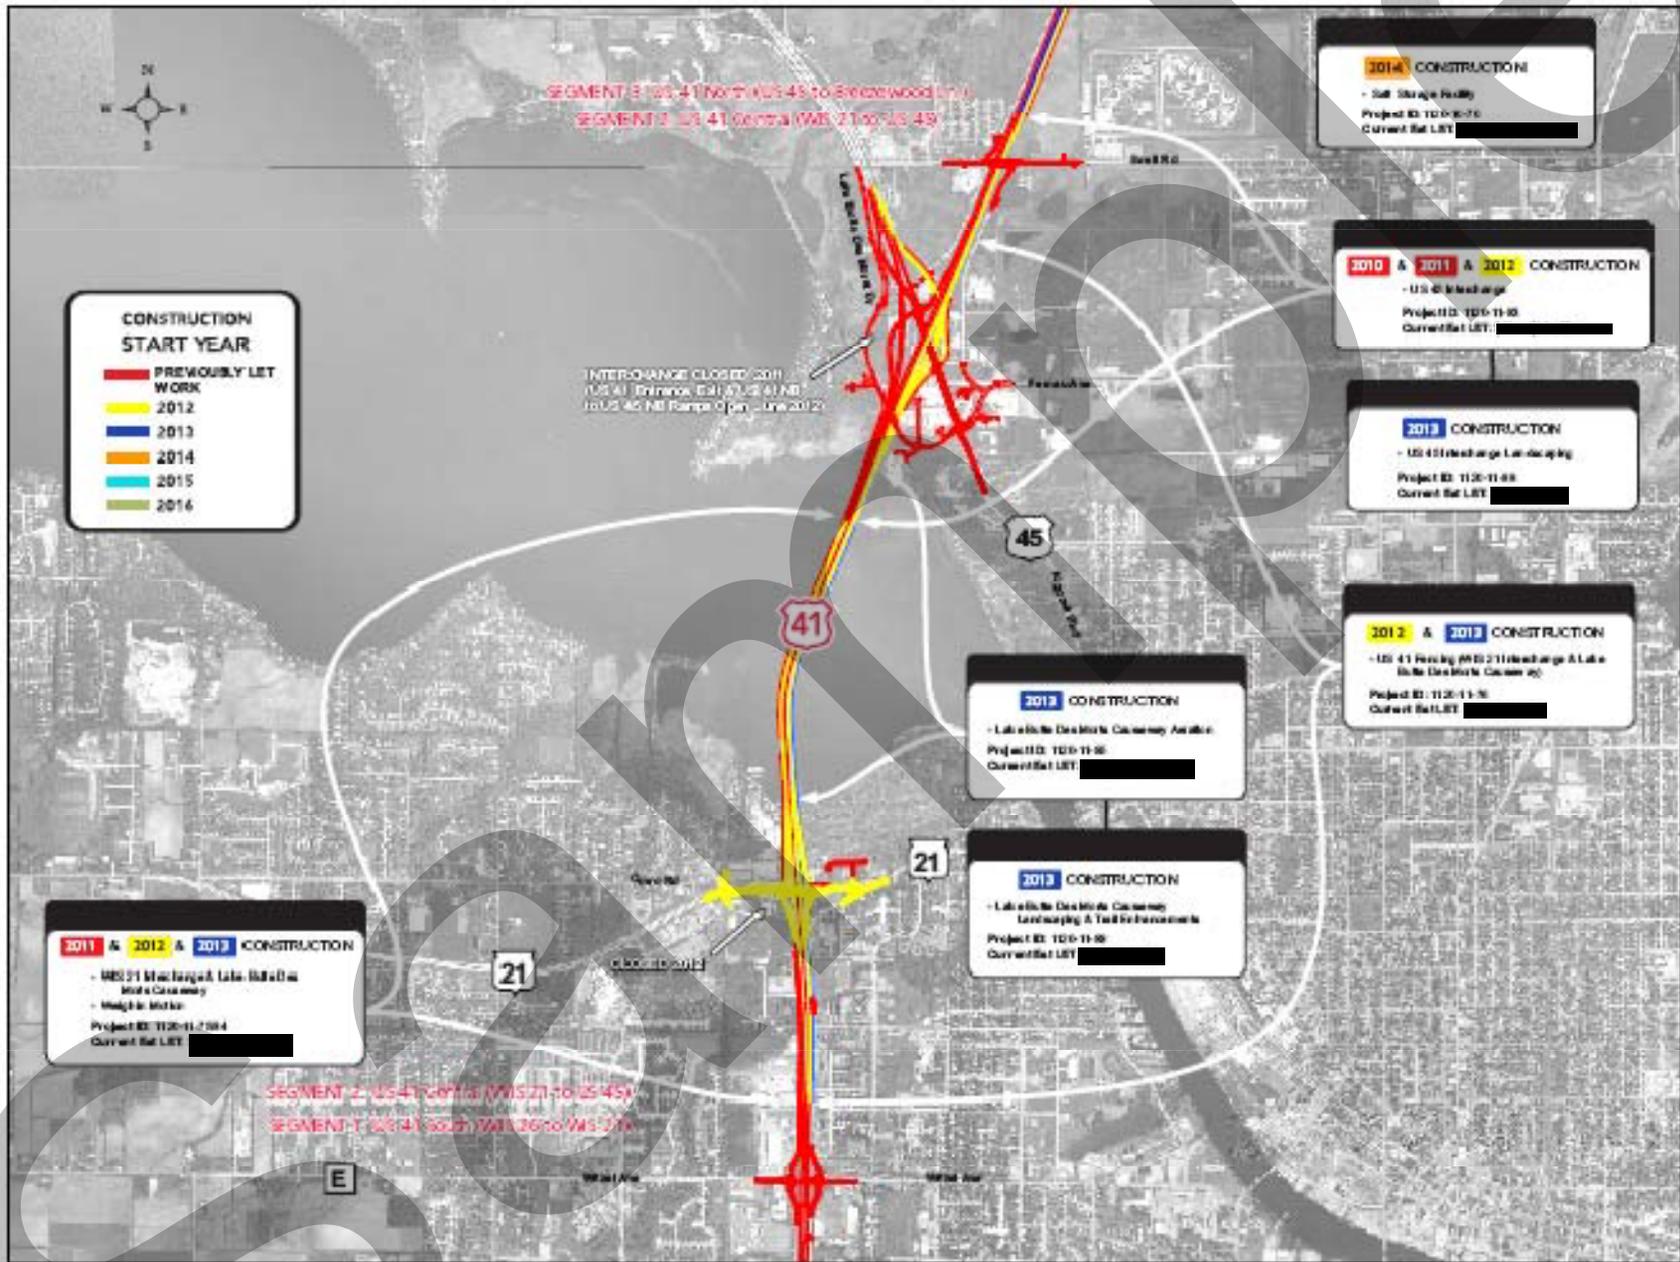


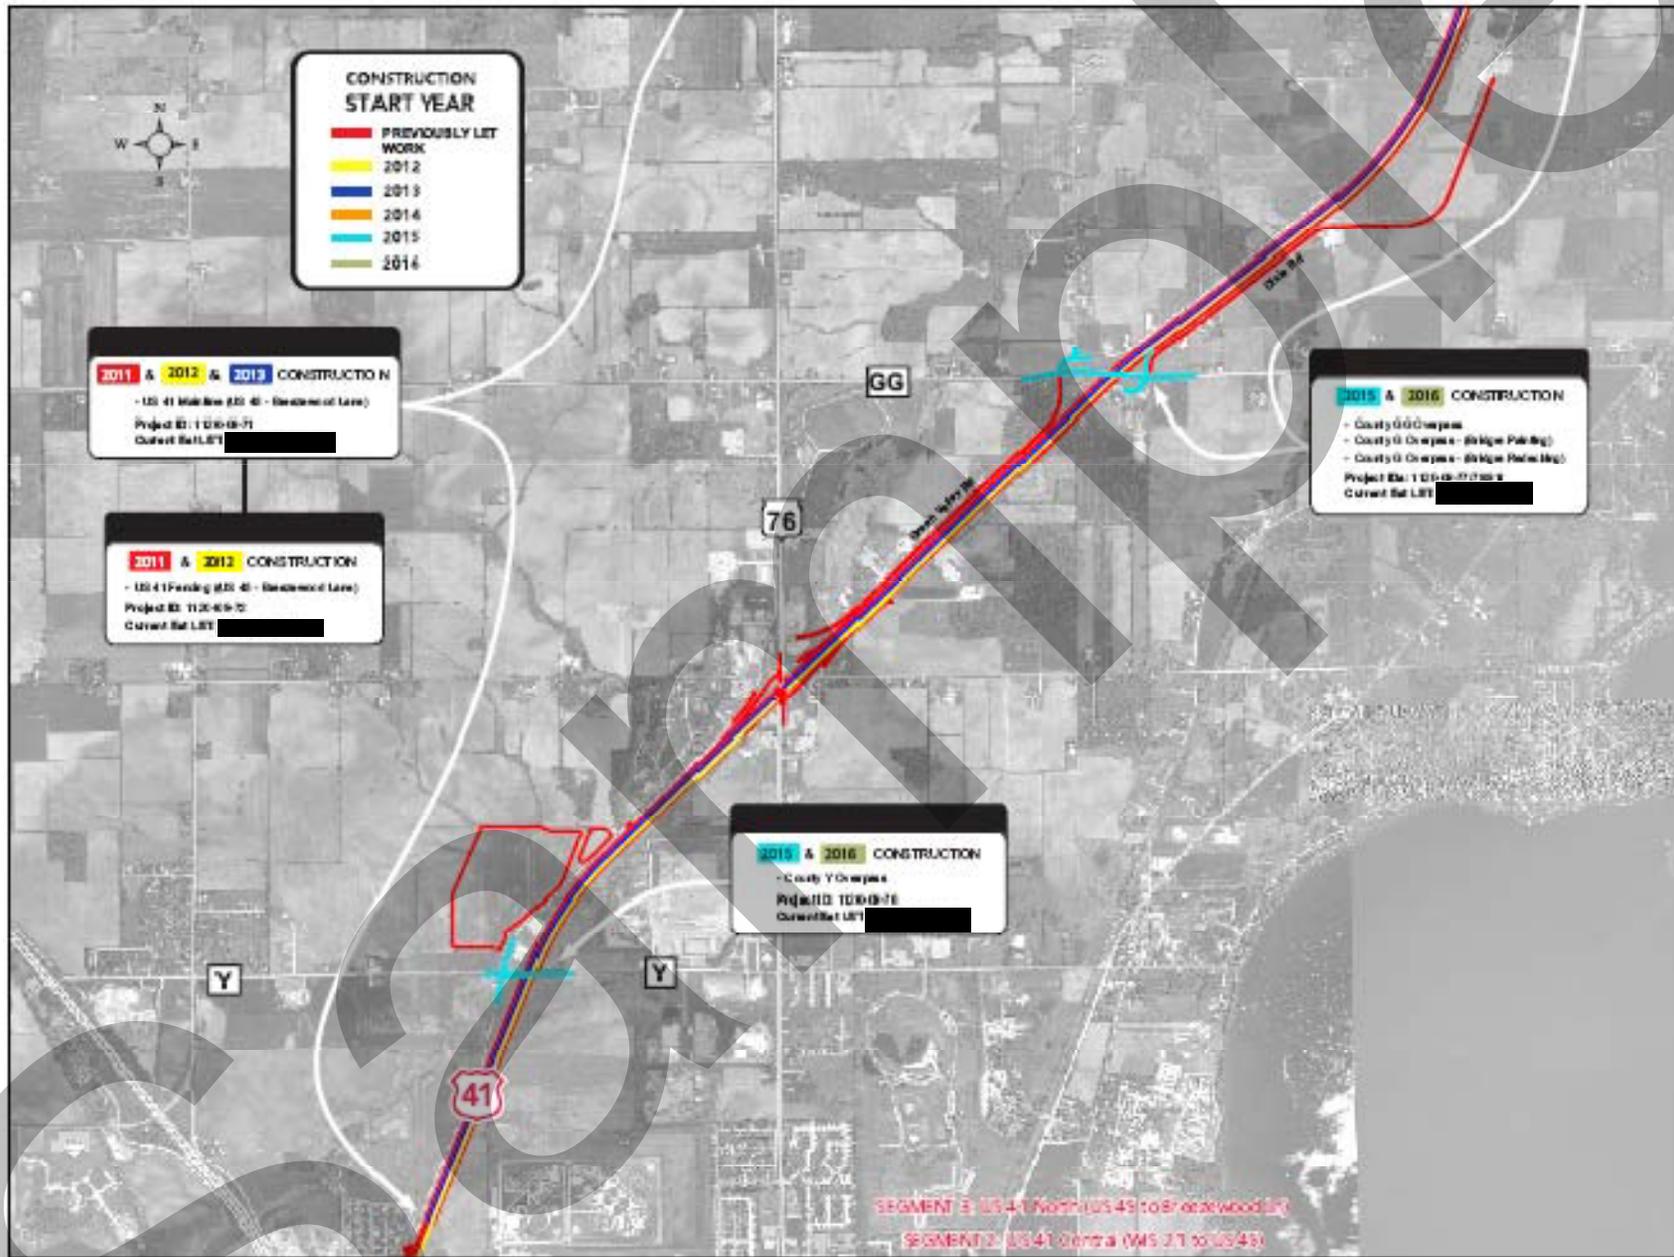





BROWN COUNTY CONTRACT LET PACKAGES

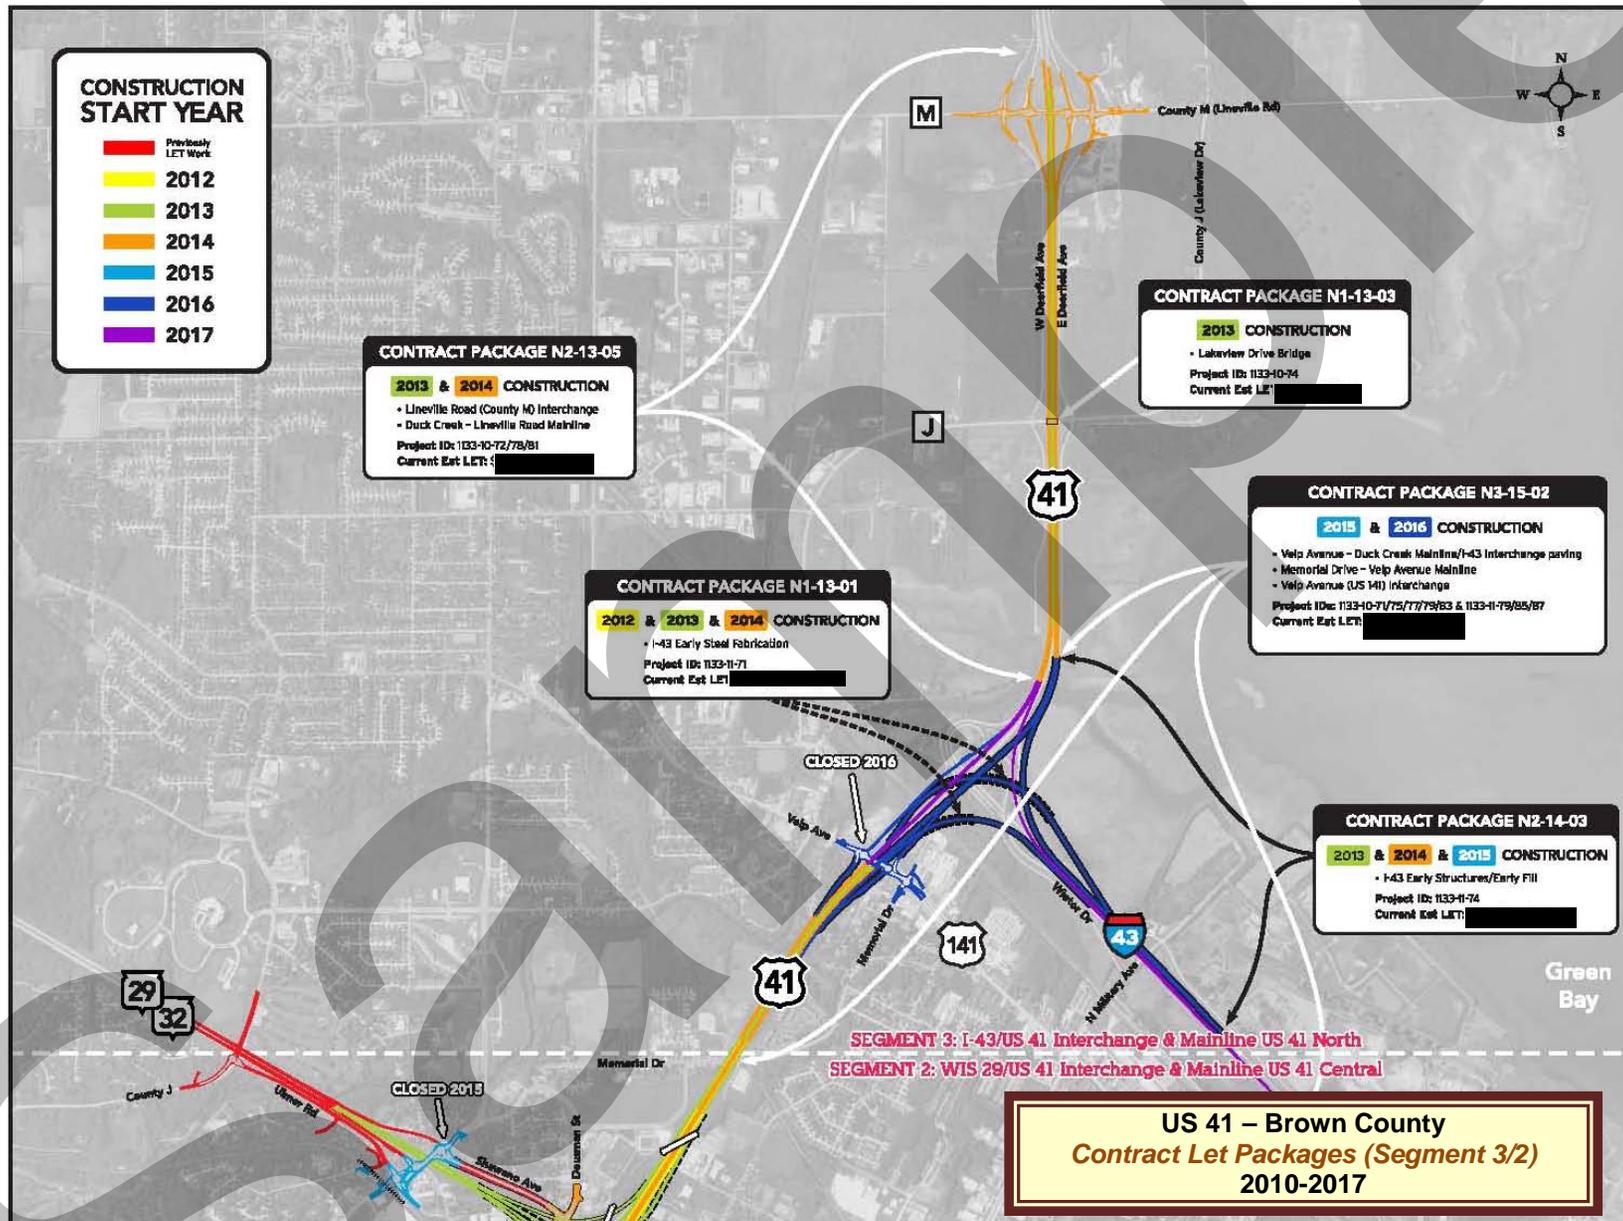

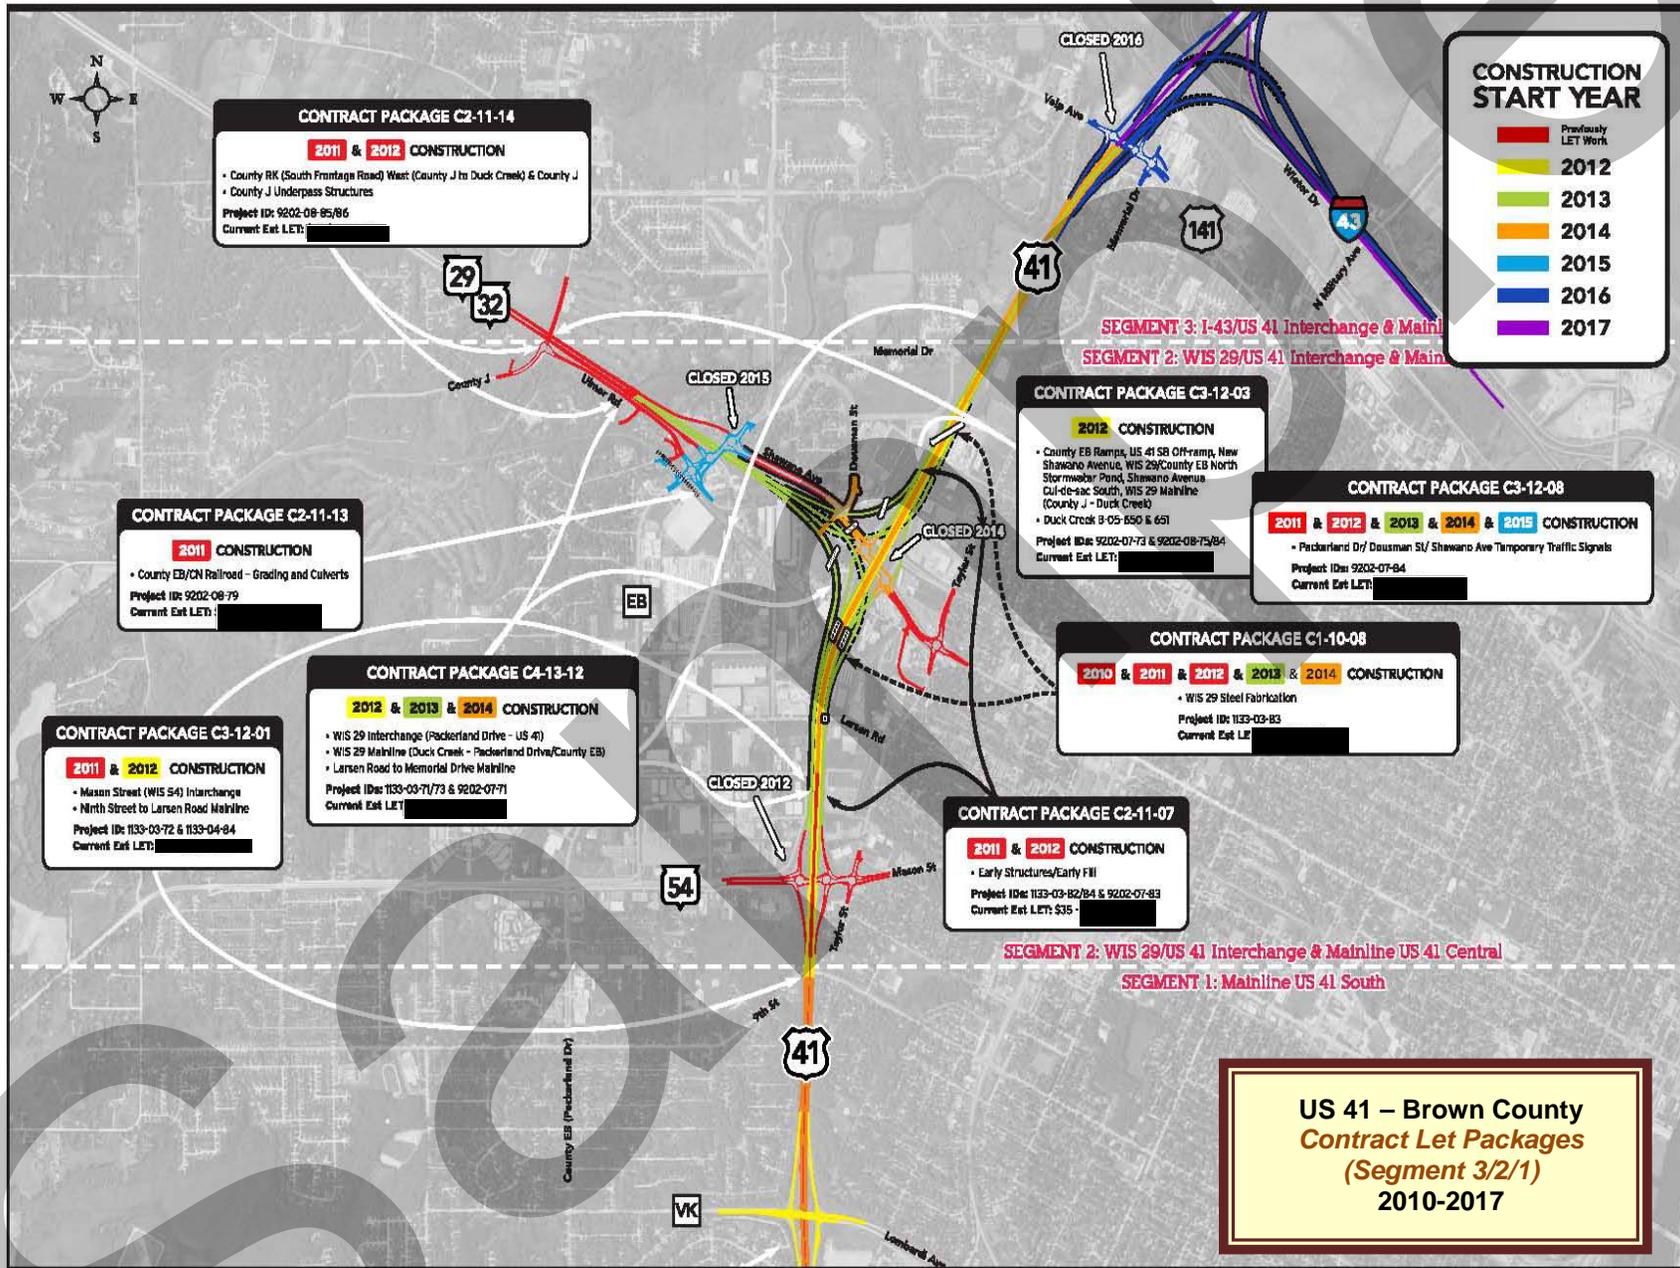

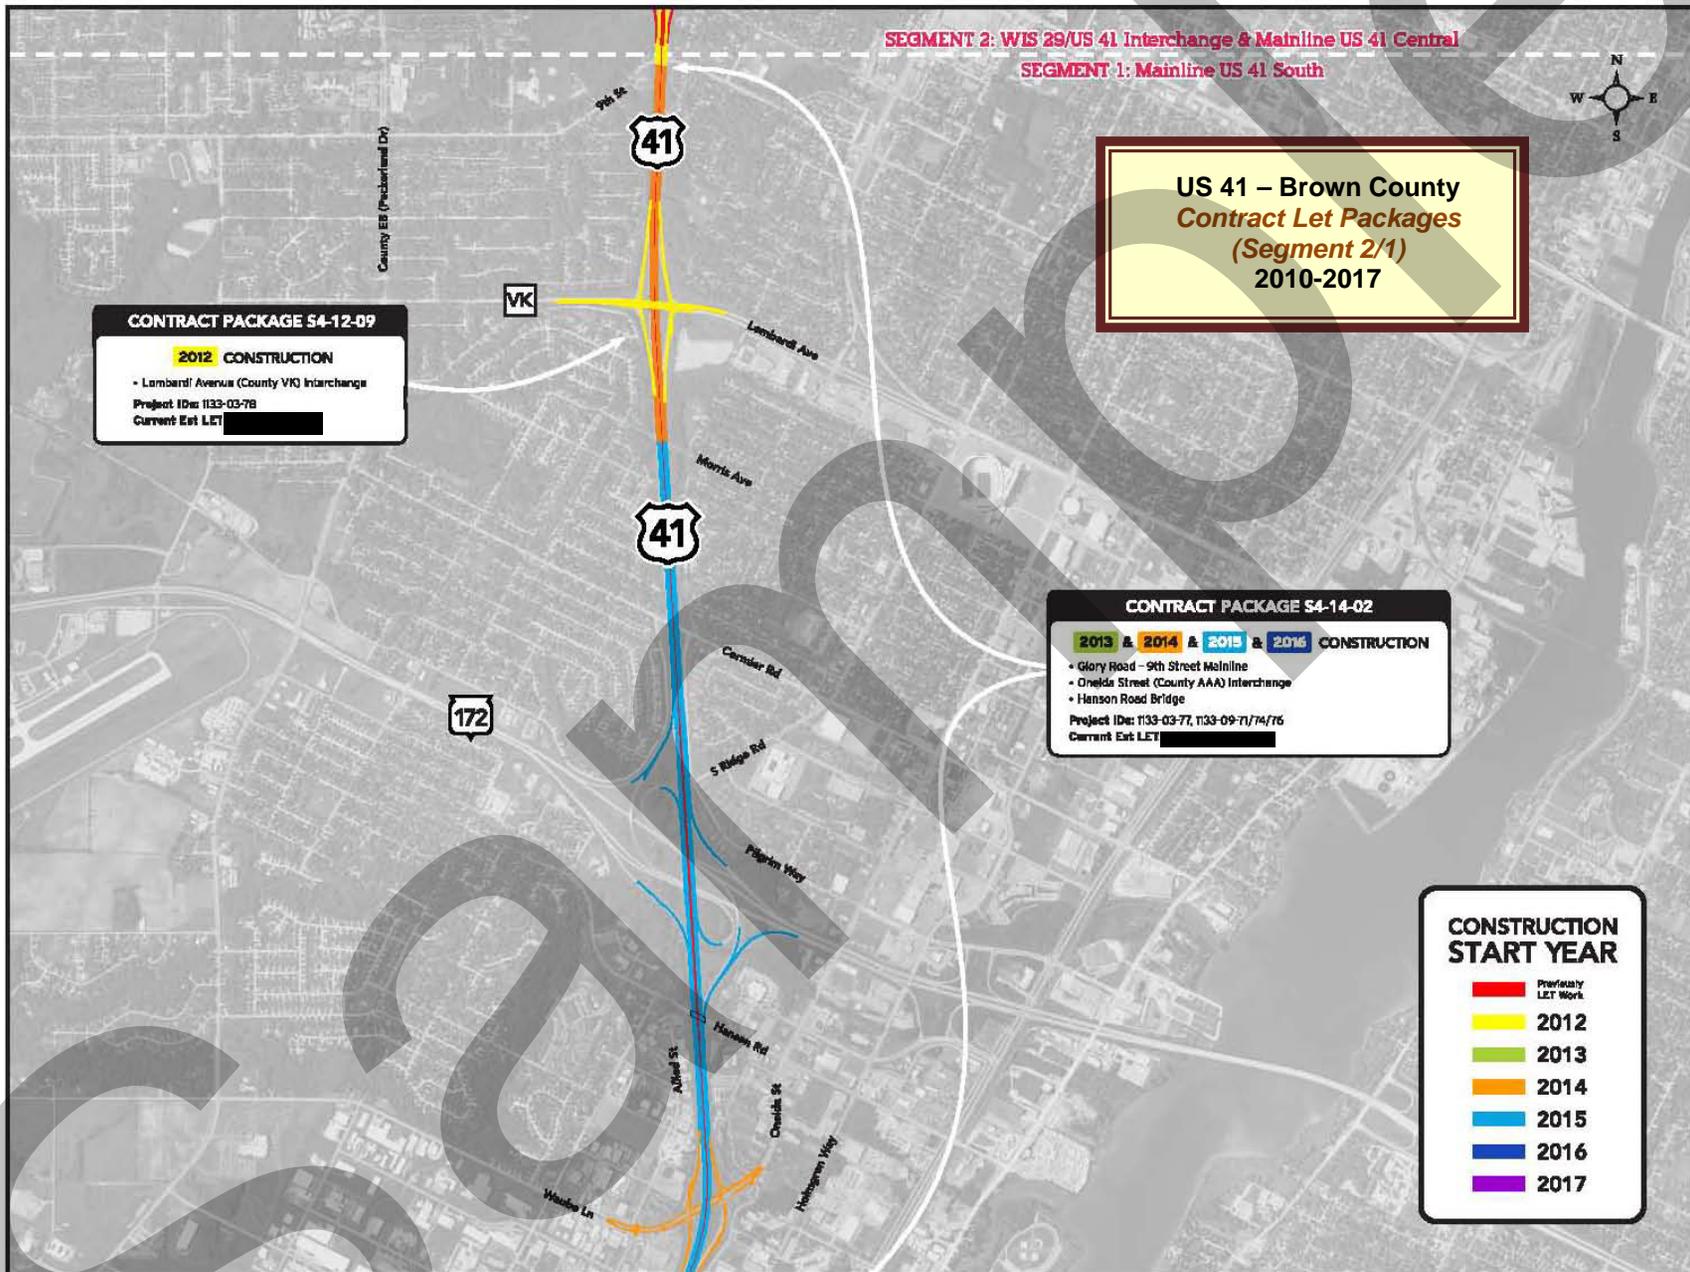

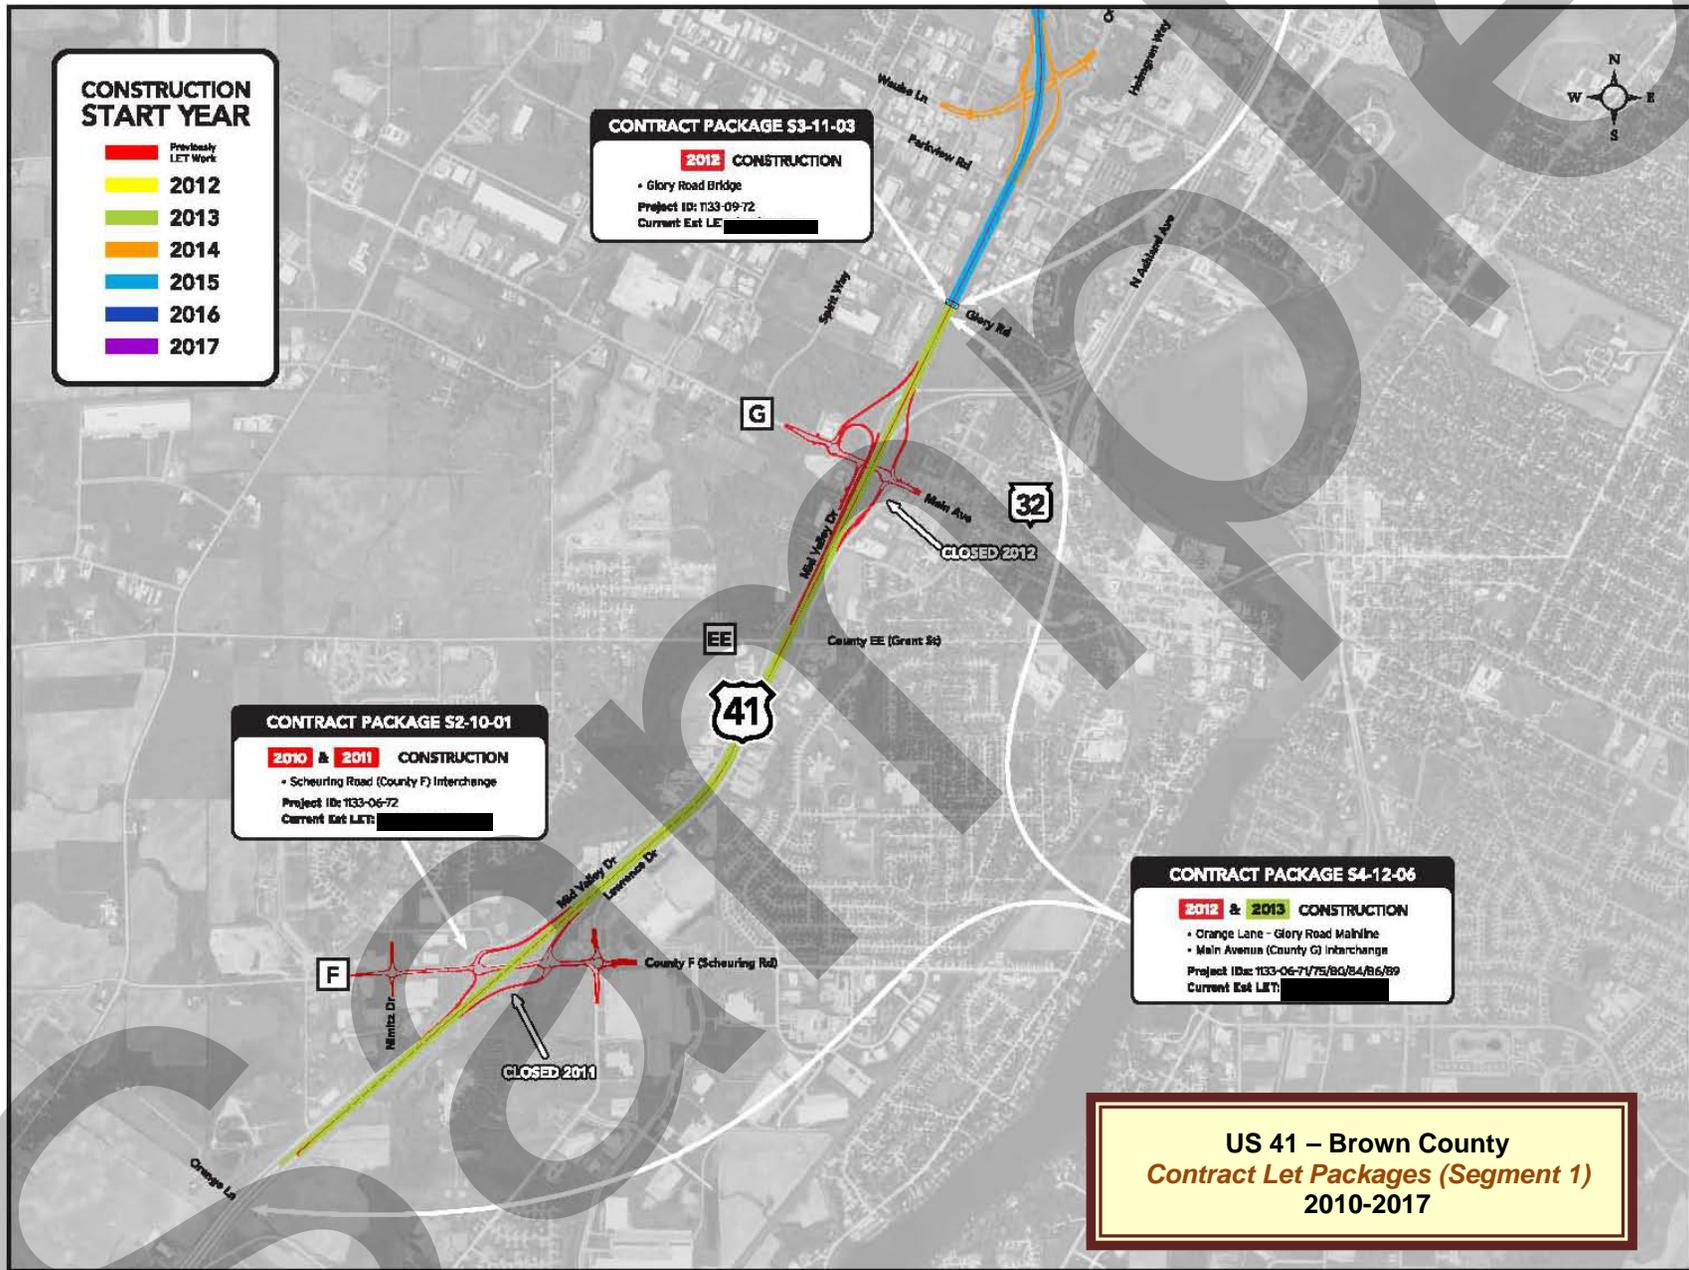

**US 41 Corridor Project
Calendar Year 2009 and 2010 Delivery Schedule
Winnebago and Brown County Construction Projects**

Contract Number	Project ID	Project Description	DESIGN PHASE				CONSTRUCTION PHASE		
			Draft PS&E Review	Right-of-Way Clear	Central Office PS&E Date	Central Office Ad Date	Central Office Let Date	Notice-To-Proceed Start Construction	Construction Substantially Complete
2009 CONSTRUCTION									
Winnebago County									
	1120-11-71	Washburn St & Witzel Ave	11/30/08 A	03/16/09 A	01/30/09 A	Complete	05/27/09 A	07/30/09 A	09/10/10 A
	1120-11-72	Fountain Ave/Snell Rd Overpass	11/30/08 A	12/21/09 A	01/30/09 A	Complete	05/27/09 A	07/06/09 A	07/30/10 A
	1120-11-73	Fernau Ave, Snell Rd, & Stillman Dr	11/30/08 A	03/30/09 A	01/30/09 A	Complete	05/27/09 A	07/21/09 A	08/27/10 A
	1120-09-73	STH 114 Ramp Improvements	01/03/09 A	N/A	03/03/09 A	05/12/09 A	06/09/09 A	Complete	10/02/09 A
	1120-10-76	STH 26 Crash Investigation Sites	02/01/09 A	N/A	04/01/09 A	05/12/09 A	06/09/09 A	09/18/09 A	10/23/09 A
	1120-11-79	Razing and Removal 11201179	12/15/08 A	N/A	01/30/09 A	05/12/09 A	06/09/09 A	07/17/09 A	09/15/09 A
	1120-11-74	Lk Butte Des Morts Dr & SB Grading	11/30/08 A	07/31/08 A	01/30/09 A	Complete	06/23/09 A	08/13/09 A	10/29/10 A
	1120-09-82	Oshkosh Wetland Mitigation	01/30/09 A	N/A	03/30/09 A	06/09/09 A	07/14/09 A	08/10/09 A	11/13/09 A
	1120-10-75	STH 44 Intchg Ramp Terminal Improvements	11/30/08 A	N/A	01/30/09 A	06/09/09 A	07/14/09 A	09/30/09 A	10/30/09 A
	1120-09-75	STH 76 Ramps	07/28/09 A	N/A	09/28/09 A	11/10/09 A	12/08/09 A	03/31/10 A	06/25/10 A
	1120-10-71	CTH K Overhead	08/09/09 A	07/31/09 A	09/28/09 A	11/10/09 A	12/08/09 A	02/03/10 A	06/18/10 A
	1120-11-80	North Washburn Sidewalk	05/31/09 A	N/A	07/31/09 A	11/10/09 A	12/09/09 A	07/22/10 A	09/2/10 A
	1120-11-81	Witzel Ave RAB & Street Ltg	08/13/09 A	N/A	10/13/09 A	11/10/09 A	12/09/09 A	07/22/10 A	09/2/10 A
Brown County									
S1-09-01	1133-06-73	Storm Water Detention Pond	09/03/08 A	N/A	11/03/08 A	05/12/09 A	06/09/09 A	04/20/09 A	06/30/09 A
C1-09-01	9202-07-77	Razing / Removal 92020777	02/13/09 A	N/A	03/23/09 A	05/12/09 A	06/09/09 A	07/21/09 A	12/09/09 A
2010 CONSTRUCTION									
Winnebago County									
	1120-09-83	Breezewood Interchange & US 45 Breezewood NB Widet	12/08/09 A	02/09/10 A	02/09/10 A	04/13/10 A	05/11/10 A	06/25/10 A	10/17/11 A
	1120-11-83	USH 45 Interchange	12/15/09 A	N/A	02/01/10 A	04/13/10 A	06/08/10 A	07/27/10 A	09/07/12
	1120-09-79	Green Valley Rd & Dixie Rd	03/02/10 A	N/A	03/01/10 A	06/08/10 A	07/13/10 A	09/14/10 A	10/14/10 A
	1120-10-72	9th Avenue Interchange	12/01/09 A	02/01/10 A	02/01/10 A	05/11/10 A	07/28/10 A	08/27/10 A	05/18/12
	1120-10-73	WIS 44 to WIS 21 US 41 Mainline	11/25/09 A	02/01/10 A	02/09/10 A	05/11/10 A	07/28/10 A	08/27/10 A	05/18/12
	1120-10-79	WIS 44 B70-138 Painting	02/01/10 A	N/A	02/01/10 A	05/11/10 A	07/28/10 A	08/27/10 A	5/18/11 A
	1120-10-78	WIS 26 B-70-200 Stain	04/20/10 A	N/A	05/20/10 A	07/13/10 A	08/10/10 A	09/03/10 A	8/4/2011 A
	1120-10-80	WIS 26 to WIS 44 Mainline	04/20/10 A	01/05/10 A	05/20/10 A	07/13/10 A	08/10/10 A	09/03/10 A	05/18/12
	1120-09-71	US 45 to Breezewood Lane Mainline	05/06/10 A	01/13/10 A	07/30/10 A	11/09/10 A	12/14/10 A	03/17/11 A	05/24/13
	1120-09-72	US 45 to CTH G Fencing	05/04/10 A	N/A	07/30/10 A	11/09/10 A	12/14/10 A	05/10/11 A	12/16/11 A
	1120-10-74	WIS 44 to WIS 21 Fencing	11/25/09 A	N/A	07/30/10 A	11/09/10 A	12/14/10 A	05/10/11 A	11/15/11 A
	1120-10-81	WIS 26 to WIS 44 Fencing	07/19/10 A	N/A	07/30/10 A	11/09/10 A	12/14/10 A	05/10/11 A	10/14/11 A
	1120-10-83	9th Avenue Interchange Lighting	05/26/10 A	N/A	08/02/10 A	11/09/10 A	12/14/10 A	05/31/11 A	07/15/11 A
Brown County									
S1-10-03	1133-06-76	Shopko Detention Pond	09/25/09 A	12/08/09 A	10/29/09 A	02/09/10 A	03/09/10 A	05/03/10 A	05/31/10 A
C1-10-02	9202-07-78	Razing / Removal 92020778	07/17/09 A	N/A	08/03/09 A	02/09/10 A	03/09/10 A	06/17/10 A	07/30/10 A
S1-10-04	1133-06-85	Scheuring Rd TMP	02/01/10 A	N/A	02/01/10 A	04/13/10 A	05/11/10 A	06/29/10 A	11/17/11 A
C1-10-08	1133-03-83	WIS 29 Steel Fabrication	02/03/10 A	N/A	02/16/10 A	05/11/10 A	06/08/10 A	07/12/10 A	10/09/14
S2-10-01	1133-06-72	Scheuring Road Interchange (CTH F)	01/07/10 A	03/08/10 A	03/08/10 A	05/11/10 A	06/08/10 A	07/22/10 A	04/13/12
C1-11-04	9202-07-85	WIS 29 Raze & Removal Phase 3	Complete	N/A	05/18/10 A	07/13/10 A	08/10/10 A	10/05/10 A	11/19/10 A

Tasks Completed
 Tasks Requiring Attention

Tasks Scheduled
 Tasks Impacting PS&E Date

ARRA Projects

**US 41 Corridor Project
Calendar Year 2011 and 2012 Delivery Schedule
Winnebago and Brown County Construction Projects**

Contract Number	Project ID	Project Description	DESIGN PHASE				CONSTRUCTION PHASE		
			Draft PS&E Review	Right-of-Way Clear	Central Office PS&E Date	Central Office Ad Date	Central Office Let Date	Notice-To-Proceed Start Construction	Construction Substantially Complete
2011 Construction									
Winnebago County									
	1120-11-75	STH 21 Interchange & Lake Butte Des Morts Causeway	09/01/10 A	02/02/09 A	02/01/11 A	03/08/11 A	07/12/11 A	8/17/2011 A	07/26/13
	1120-11-84	Weigh-in-Motion	09/01/10 A	N/A	02/01/11 A	03/08/11 A	07/12/11 A	8/17/2011 A	07/26/13
	1120-11-76	WIS 21 Intchg & LBDM Causeway Fencing	09/01/10 A	02/02/09 A	8/1/2011 A	11/8/2011 A	12/13/2011 A	1/9/2012 A	11/15/13
Brown County									
C1-11-06	9202-07-86	WIS 29 Raze & Removal Phase 4	10/01/10 A	N/A	10/01/10 A	01/11/11 A	02/08/11 A	03/31/11 A	05/20/11 A
C1-11-07	9202-07-81	WIS 29 Clearing & Grubbing Phase 1	10/01/10 A	N/A	10/01/10 A	01/11/11 A	02/08/11 A	03/29/11 A	5/19/11 A
C2-11-01	9202-07-74	Shawano / Taylor St Intersection TMP	10/01/10 A	N/A	12/06/10 A	02/08/11 A	03/08/11 A	4/25/11 A	11/1/11 A
	9202-07-79	Shawano Ave / Taylor St Intersection	10/01/10 A	12/15/10 A	12/06/10 A	02/08/11 A	03/08/11 A	4/25/11 A	11/1/11 A
	9202-07-80	Old Shawano Ave Connection	10/01/10 A	N/A	12/06/10 A	02/08/11 A	03/08/11 A	4/25/11 A	9/26/11 A
C2-11-02	9202-08-74	Shawano Ave Cul-de-sac North Obliteration, Southview Ct & Viewpoint Ct Obliteration	09/01/10 A	11/18/10 A	10/29/10 A	02/08/11 A	03/08/11 A	4/20/11 A	06/14/11 A
C2-11-15	1133-04-88	US 41/WIS 29 Soil Mitigation - Wick Drains	10/27/10 A	N/A	11/01/10 A	02/08/11 A	03/08/11 A	4/20/11 A	08/04/11 A
S2-11-02	1133-06-78	Scheuring Road Lighting	08/30/10 A	N/A	11/01/10 A	02/08/11 A	03/08/11 A	6/8/2011 A	10/09/11 A
C2-11-03	1133-04-75	Lambeau Street, City of Green Bay	09/23/10 A	01/06/11 A	10/29/10 A	03/08/11 A	4/12/2011 A	5/23/2011 A	7/22/11 A
C2-11-05	9202-07-72	CTH RK (South Frontage Rd) East (Duck Creek To CTH EB)	10/08/10 A	01/26/11 A	12/06/10 A	03/08/11 A	4/12/2011 A	5/26/2011 A	11/23/11 A
	9202-07-75	Parkside Court Noisewalls	10/08/10 A	01/26/11 A	12/06/10 A	03/08/11 A	04/12/11 A	06/01/11 A	11/23/11 A
	9202-08-81	WIS 29 / CTH EB South Stormwater Pond	10/08/10 A	N/A	12/06/10 A	03/08/11 A	04/12/11 A	06/01/11 A	11/23/11 A
C2-11-14	9202-08-85	CTH RK (South Frontage Rd) West (CTH J to Duck Creek) & CTH J	12/07/10 A	02/03/11 A	02/01/11 A	03/08/11 A	04/08/11 A	06/10/11 A	11/23/11 A
	9202-08-86	CTH J Underpass Structures	12/07/10 A	N/A	02/01/11 A	03/08/11 A	05/10/11 A	06/10/11 A	05/21/12
S3-11-01	1133-03-79	Morris Ave to 9th Street TMP	11/01/10 A	N/A	02/15/11 A	04/12/11 A	05/10/11 A	06/15/11 A	10/12/11 A
	1133-04-83	Ninth St - Larsen Rd TMP	08/31/10 A	N/A	02/15/11 A	04/12/11 A	05/10/11 A	06/20/11 A	10/12/11 A
	1133-06-82	Orange Ln to Glory Rd TMP	08/31/10 A	N/A	02/15/11 A	04/12/11 A	05/10/11 A	06/20/11 A	11/23/11 A
	1133-09-77	Glory Rd to Morris Ave TMP	11/01/10 A	N/A	02/15/11 A	04/12/11 A	05/10/11 A	06/20/11 A	10/12/11 A
S3-11-03	1133-09-72	Glory Road Bridge B-05-615	12/01/10 A	03/30/11 A	02/03/11 A	04/12/11 A	05/10/11 A	07/19/11 A	04/30/12
S3-11-04	1133-06-70	Hemlock Creek Box Culvert	12/01/10 A	N/A	02/03/11 A	04/12/11 A	05/10/11 A	06/20/11 A	12/28/11 A
	1133-09-75	Dutchman's Creek Box Culvert	12/01/10 A	N/A	02/03/11 A	04/12/11 A	05/10/11 A	06/20/11 A	12/28/11 A
C2-11-07	1133-03-82	Early Structures / Early Fill	12/01/10 A	03/25/11 A	02/01/11 A	05/10/11 A	06/14/11 A	7/21/2011 A	10/11/12
	1133-03-84	Beaver Dam Creek Box Culvert @ Van Bóxtel	12/01/10 A	03/29/11 A	02/01/11 A	05/10/11 A	06/14/11 A	07/22/11 A	12/5/11 A
	9202-07-83	Wetland Mitigation Site (Resort Rd)	12/01/10 A	N/A	02/01/11 A	05/10/11 A	06/14/11 A	07/22/11 A	06/01/12
C2-11-13	9202-08-79	CTH EB / CN Railroad - Grading & Culverts	12/01/10 A	N/A	02/03/11 A	05/10/11 A	06/14/11 A	8/30/2011 A	04/30/12
C3-12-01	1133-03-72	Mason St / WIS 54 Interchange	02/21/11 A	05/10/11 A	03/22/11 A	05/10/11 A	07/12/11 A	8/25/2011 A	08/02/12
	1133-04-84	Ninth St - Larsen Rd Mainline	02/21/11 A	05/10/11 A	03/22/11 A	05/10/11 A	7/12/11 A	09/08/11 A	10/15/12
S2-11-03	1133-06-77	CTH F / Mid Valley Drive Realignment	12/01/10 A	09/20/10 A	02/01/11 A	05/10/11 A	06/14/11 A	07/22/11 A	11/17/11 A
	1133-06-81	CTH G / Mid Valley Drive Re-Alignment	12/01/10 A	03/24/11 A	02/01/11 A	05/10/11 A	06/14/11 A	07/22/11 A	11/17/11 A
C3-12-08	9202-07-84	Packerland Dr/Dousman St/Shawano Ave Temporary Traffic Signals	03/02/11 A	N/A	05/02/10 A	07/12/11 A	8/9/11 A	11/07/11 A	10/16/15
S3-12-05	1133-04-78	Orange Ln - Ninth St & Larsen Rd - Memorial Dr Clearing & Grubbing	03/01/11 A	N/A	05/02/10 A	07/12/11 A	8/9/11 A	11/01/11 A	1/31/2012 A
C3-12-03	9202-07-73	WIS 29 ML(CTH J-Duck Ck), CTH EB Ramps, US 41 SB Offramp, New Shawano Ave.	06/02/11 A	4/25/11 A	8/1/2011 A	11/8/2011 A	12/13/11 A	2/6/2012 A	11/26/12
	9202-08-75	CTH RK (South Frontage Rd) Park & Ride	06/02/11 A	N/A	8/1/2011 A	11/8/2011 A	12/13/11 A	2/6/2012 A	11/26/12
	9202-08-84	Duck Creek B-05-650 & 651	06/02/11 A	N/A	8/1/2011 A	11/8/2011 A	12/13/11 A	2/6/2012 A	11/26/12
2012 CONSTRUCTION									
Winnebago County									
	1120-10-85	Poberezný Rd	10/11/11 A	N/A	11/1/11 A	2/14/2012 A	04/10/12	05/16/12	07/13/12
Brown County									
S4-12-06	1133-06-71	Orange Lane To Glory Rd ML	06/30/11 A	8/1/2011 A	8/29/2011 A	12/13/2011 A	01/10/12	3/1/2012 A	06/21/13
	1133-06-75	Ashland Ave B-05-119 & 120 Painting	06/30/11 A	N/A	8/29/2011 A	12/13/2011 A	01/10/12	3/1/2012 A	11/06/12
	1133-06-80	Main Ave / CTH G Interchange	06/30/11 A	8/1/2011 A	8/29/2011 A	12/13/2011 A	01/10/12	3/1/2012 A	11/06/12
	1133-06-84	Main Ave Intchg Stormwater Pond	06/30/11 A	N/A	8/29/2011 A	12/13/2011 A	01/10/12	3/1/2012 A	06/29/12
	1133-06-86	Main Ave Park & Ride	06/30/11 A	N/A	8/29/11 A	12/13/2011 A	01/10/12	3/1/2012 A	09/28/12
	1133-06-89	Calaway Stormwater Pond	06/30/11 A	N/A	8/29/11 A	12/13/2011 A	01/10/12	3/1/2012 A	06/29/12
N1-13-03	1133-10-74	Lakeview Dr B-05-129	12/3/11 A	N/A	2/1/12 A	06/12/12	07/10/12	08/15/12	12/31/12
C3-12-05	9202-08-73	Pamperin Park Access Rd Obliteration, Shawano Ave Elmhurst Ave Connection	9/2/11 A	N/A	11/1/11 A	06/12/12	07/10/12	08/15/12	09/28/12
N1-12-08	1133-10-84	North Segment Razing / Removal Phase 1	10/20/11 A	01/02/12 A	11/1/11 A	01/10/12	02/14/12	03/21/12	06/29/12
N1-13-01	1133-11-71	IH 43 Early Steel Fabrication	12/1/11 A	N/A	02/01/12	06/12/12	07/10/12	08/15/12	02/25/14
N1-12-09	1133-10-42	GBMSD Relocation (North)	N/A	N/A	N/A	N/A	06/12/12	07/19/12	10/11/12
S4-13-05	1133-06-83	Main Ave Interchange Lighting	06/02/11 A	N/A	8/29/11 A	04/10/12	05/08/12	06/14/12	11/06/12
S4-12-09	1133-03-78	Lombardi Ave / CTH VK Interchange	9/19/11 A	N/A	11/3/11 A	01/10/12	02/14/12	03/05/12	08/01/12
N1-13-11	1133-11-75	Beaver Dam Creek Box Culvert & Creek Re-Alignment	12/03/11 A	N/A	05/08/12	07/10/12	08/14/12	09/20/12	11/15/12
	1133-11-86	Velp Avenue Storm Water Pond	12/03/11 A	02/01/12	05/08/12	07/10/12	08/14/12	09/20/12	11/15/12
	1133-10-80	Island Court Cul-de-Sac	12/03/11 A	N/A	05/08/12	07/10/12	08/14/12	09/20/12	12/31/12
C5-12-08	9202-08-88	Shawano Ave Landscaping & Bike/Pedestrian Trail (CTH EB - Dousman St)	12/03/11 A	N/A	02/01/12	06/12/12	07/10/12	08/15/12	01/22/13
	9202-07-88	WIS 29 Fencing	12/03/11 A	N/A	02/01/12	06/12/12	07/10/12	08/15/12	12/12/12
N1-13-10	9202-08-83	Freedom Mitigation Site (v2)	11/09/11 A	08/23/11 A	02/01/12	04/10/12	05/08/12	06/14/12	09/14/12

Tasks Completed Tasks Requiring Attention
 Tasks Scheduled Tasks Impacting PS&E/Let Date



**US 41 Corridor Project
Calendar Year 2013 and 2014 Delivery Schedule
Winnebago and Brown County Construction Projects**


Contract Number	Project ID	Project Description	DESIGN PHASE				CONSTRUCTION PHASE		
			Draft PS&E Review	Right-of-Way Clear	Central Office PS&E Date	Central Office Ad Date	Central Office Let Date	Notice-To-Proceed Start Construction	Construction Substantially Complete
2013 Construction									
Winnebago County									
	1120-11-85	LBDM Causeway Aeration	06/02/12	N/A	08/01/12	12/11/12	01/08/13	02/13/13	11/15/13
	1120-11-88	US45 Interchange Landscaping	2/11/11 A	N/A	11/01/12	03/12/13	04/09/13	05/15/13	11/15/13
	1120-11-89	LBDM Causeway Landscaping & Trail Enhancements	3/28/11 A	02/12/10 A	6/1/11 A	03/12/13	04/09/13	05/15/13	11/01/13
	1120-10-82	WIS 26 Interchange Landscaping	6/20/11 A	N/A	11/01/12	03/12/13	04/09/13	08/14/13	11/15/13
	1120-10-84	WIS 44 Median Work	9/2/2011 A	N/A	11/01/12	02/12/13	03/12/13	04/17/13	11/15/13
Brown County									
C4-13-12	1133-03-73	WIS 29 Interchange (Packerland Dr to US41)	12/1/11 A	2/10/12 A	03/01/12	06/12/12	07/24/12	08/29/12	10/06/14
	1133-03-71	Larsen Rd - Memorial Drive ML	12/1/11 A	2/10/12 A	03/01/12	06/12/12	07/24/12	08/29/12	10/06/14
	9202-07-71	WIS 29 ML (Duck Creek - Packerland Dr/GTH EB)	12/1/11 A	02/08/11 A	03/01/12	06/12/12	07/24/12	08/29/12	10/06/14
N2-13-02	1133-11-72	East Deerfield Ave Cul-de-sac	09/02/12	11/01/12	11/01/12	07/09/13	08/13/13	09/19/13	05/15/14
N2-13-10	1133-11-73	Hurlbut St Cul-de-sac	09/02/12	N/A	11/01/12	02/12/13	08/06/13	09/12/13	05/15/14
C5-13-02	9202-08-78	Pamperin Park Trail Paving & Landscaping	09/02/12	N/A	11/01/12	03/12/13	04/09/13	07/25/13	11/01/13
S5-13-03	1133-06-88	Grant St Reconstruction	09/02/12	N/A	11/01/12	03/12/13	04/09/13	05/15/13	09/30/13
S5-13-07	1133-06-87	US 41 Fencing (Orange Ln - Glory Rd)	5/27/11 A	N/A	05/01/12	03/12/13	04/09/13	05/15/13	06/28/13
C4-13-03	9202-08-72	Dousman Street Obliteration	5/30/11 A	N/A	08/01/12	01/08/13	02/12/13	03/20/13	08/01/13
C4-13-11	1133-04-80	Ninth St Reconstruction	12/03/12	02/01/12	02/01/13	04/09/13	05/14/13	06/24/13	08/30/13
	9202-08-76	S Memorial Dr Access to Parkside Ct	12/03/12	02/01/12	02/01/13	04/09/13	05/14/13	06/20/13	08/30/13
N2-13-05	1133-10-72	Lineville Road (CTH M) Interchange	12/03/12	02/01/13	02/01/13	04/09/13	05/14/13	06/20/13	10/31/14
	1133-10-81	Duck Creek - Lineville Rd Mainline	12/03/12	02/01/13	02/01/13	04/09/13	05/14/13	06/20/13	10/31/14
	1133-10-78	Lineville Road Interchange Lighting	12/03/12	N/A	02/01/13	04/09/13	05/14/13	06/20/13	10/31/14
S4-14-02	1133-09-71	Glory Rd To Morris Ave ML	12/03/12	02/01/13	02/01/13	06/11/13	07/09/13	08/14/13	07/19/16
	1133-03-77	Morris Avenue to Ninth Street ML	12/03/12	02/01/13	02/01/13	06/11/13	07/09/13	08/14/13	07/19/16
	1133-09-76	Oneida Street (CTH AAA) Interchange	12/03/12	02/01/13	02/01/13	06/11/13	07/09/13	08/14/13	07/27/15
	1133-09-74	Hansen Rd B-05-611	12/03/12	N/A	02/01/13	06/11/13	07/09/13	08/14/13	11/16/15
S4-14-08	1133-03-70	Salt Storage Facility	12/03/12	N/A	02/01/13	06/11/13	07/09/13	08/14/13	11/15/13
2014 Construction									
Winnebago County									
	1120-10-70	Salt Storage Shed	09/02/13	N/A	11/01/13	03/11/14	04/08/14	05/13/14	11/14/14
Brown County									
N2-14-03	1133-11-74	IH 43 Early Structures/Early Fill	12/03/12	02/01/13	02/01/13	07/09/13	08/13/13	09/19/13	02/26/15
C4-14-13	1133-03-87	US 41 Bond - Woodman Overpass	12/03/13	N/A	02/01/14	04/08/14	05/13/14	06/19/14	11/14/14
S5-14-09	1133-06-79	Preserve Trail Overpass	12/03/13	N/A	02/01/14	04/08/14	05/13/14	06/19/14	11/14/14
S5-14-10	1133-09-82	WIS 172 Pioneer - North Overpass	12/03/13	N/A	02/01/14	04/08/14	05/13/14	06/19/14	11/14/14

Tasks Completed
 Tasks Requiring Attention
 Tasks Scheduled
 Tasks Impacting PS&E/LET Date




**US 41 Corridor Project
Calendar Year 2015 and 2016 Delivery Schedule
Winnebago and Brown County Construction Projects**

Contract Number	Project ID	Project Description	DESIGN PHASE				CONSTRUCTION PHASE		
			Draft PS&E Review	Right-of-Way Clear	Central Office PS&E Date	Central Office Ad Date	Central Office Let Date	Notice-To-Proceed Start Construction	Construction Substantially Complete
2015 Construction									
Winnebago County									
	1120-09-77	CTH GG Overpass B-70-287	12/03/12	N/A	02/01/13	06/09/15	07/14/15	08/19/15	11/15/16
	1120-09-78	CTH G Overpass B-70-67 Painting	12/03/12	N/A	02/01/13	06/09/15	07/14/15	08/19/15	11/15/16
	1120-09-81	CTH G Overpass B-70-67 Redecking	12/03/12	N/A	02/01/13	06/09/15	07/14/15	08/19/15	11/15/16
	1120-09-76	CTH Y Overpass B-70-284	12/03/12	N/A	02/01/13	06/09/15	07/14/15	08/19/15	11/15/16
Brown County									
N3-15-02	1133-10-77	Memorial Dr - Velp Ave ML	12/03/13	02/01/14	02/01/14	12/09/14	01/13/15	02/18/15	12/29/16
	1133-10-71	Velp Ave-Duck Creek ML / IH 43 Intchg	12/03/13	02/01/14	02/01/14	12/09/14	01/13/15	02/18/15	12/29/16
	1133-10-83	Memorial Dr - Lineville Rd Clearing & Grubbing	12/03/13	02/01/14	02/01/14	12/09/14	01/13/15	02/18/15	12/29/16
	1133-11-85	IH 43 System Interchange Lighting	12/03/13	N/A	02/01/14	12/09/14	01/13/15	02/18/15	12/29/16
	1133-11-79	Deerfield Docks Trail Connection	12/03/13	N/A	02/01/14	12/09/14	01/13/15	02/18/15	12/29/16
	1133-10-75	Velp Ave / USH 141 Interchange	12/03/13	02/01/14	02/01/14	12/09/14	01/13/15	02/18/15	12/29/16
	1133-10-79	Velp Ave Interchange Lighting	12/03/13	N/A	02/01/14	12/09/14	01/13/15	02/18/15	12/29/16
S5-15-02	1133-09-80	WIS 172 Interchange Landscaping	06/02/13	N/A	08/01/15	12/09/14	02/09/16	03/16/16	08/26/16
C5-15-09	1133-04-73	WIS 29 System Interchange Landscaping	09/02/14	N/A	11/01/14	02/10/15	03/10/15	04/15/15	11/16/15
C5-16-03	9202-08-77	Shawano Ave Landscaping & Bike/Pedestrian Trail (Taylor St to Du	12/03/13	N/A	02/01/14	06/10/14	07/08/14	08/13/14	08/25/15
2016 Construction									
Winnebago County									
Brown County									
C5-16-05	9202-08-80	Rivergrove Avenue Extension	12/03/14	02/01/15	02/01/15	06/09/15	07/14/15	08/19/15	05/31/16
N3-16-15	1133-11-80	US 41 Fencing (Memorial Dr - Lineville Rd)	06/02/14	N/A	08/01/14	01/12/16	02/09/16	03/16/16	12/29/16
N3-16-09	1133-11-81	IH 43 Fencing (Military Ave - Atkinson Dr)	06/02/14	N/A	08/01/14	01/12/16	02/09/16	03/16/16	12/29/16

Tasks Completed 
 Tasks Requiring Attention 
 Tasks Scheduled 
 Tasks Impacting PS&E/LET Date 



US 41 Project/Total Majors Program Funding

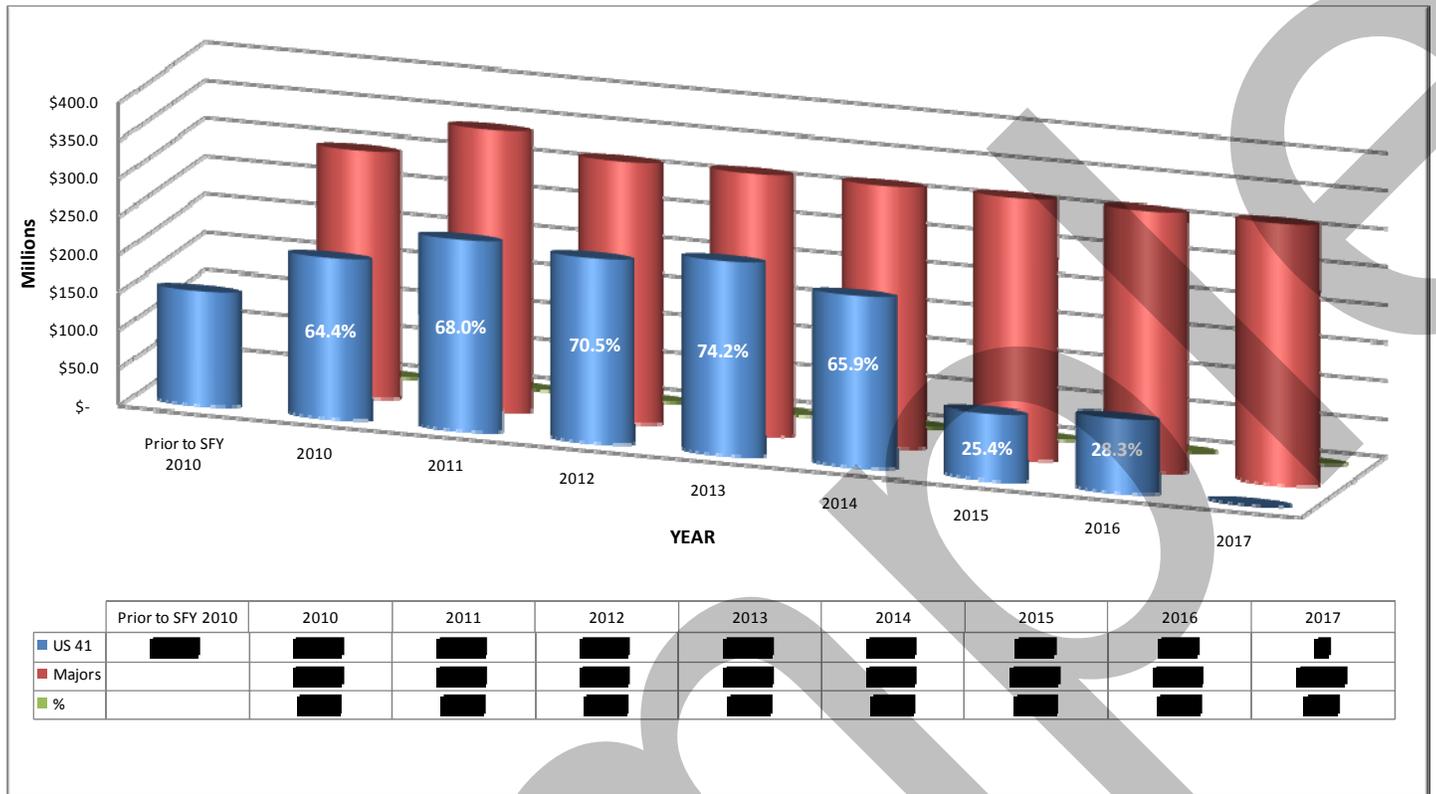

Cost Estimate by Cost Element & SFY (in millions)

	Prior to SFY 2010	SFY 2010	SFY 2011	SFY 2012	SFY 2013	SFY 2014	SFY 2015	SFY 2016	SFY 2017	TOTAL
Design	█	█	█	█	█	█	█	█	█	█
Real Estate	█	█	█	█	█	█	█	█	█	█
Utilities	█	█	█	█	█	█	█	█	█	█
Construction Costs	█	█	█	█	█	█	█	█	█	█
TOTAL	█	█	█	█	█	█	█	█	█	█
