



Wisconsin Department of Transportation

April 8, 2016

Division of Transportation Systems Development

Bureau of Project Development
4802 Sheboygan Avenue, Rm 601
P O Box 7916
Madison, WI 53707-7916

Telephone: (608) 266-1631
Facsimile (FAX): (608) 266-8459

NOTICE TO ALL CONTRACTORS:

**Proposal #26: 1206-04-65, WISC 2016 199
Sauk City - Cambridge
Yahara River B-13-0315 & B-13-0316
USH 12
Dane County**

Letting of April 12, 2016

This is Addendum No. 02, which provides for the following:

Special Provisions

Revised Special Provisions	
Article No.	Description
3	Prosecution and Progress
4	Traffic

Plan Sheets

Added Plan Sheets	
Plan Sheet	Plan Sheet Title (brief description of why sheet was added)
8A	Traffic Control Typical Sections

Other

Revise the contract time for completion from 30 working days to 50 working days (an increase in 20 working days).

The responsibility for notifying potential subcontractors and suppliers of these changes remains with the prime contractor.

Sincerely,

Mike Coleman

Proposal Development Specialist
Proposal Management Section

ADDENDUM NO. 02

1206-04-65

April 08, 2016

Special Provisions

3. Prosecution and Progress.

*Add the following to section titled **Staging**:*

Alternate staging will be permitted by the engineer as described in the Traffic article. Obtain approval from the engineer prior to using alternate staging.

4. Traffic.

*Add the following to section titled **Staging**:*


Alternate staging and traffic control will be permitted for Stage 1, Stage 2, and Stage 3 to construct the overlay on the outside lanes as shown in the plans and as directed by the engineer.

Plan Sheets


The following 8½ x 11-inch sheets are attached and made part of the plans for this proposal:

Added: 8A


END OF ADDENDUM

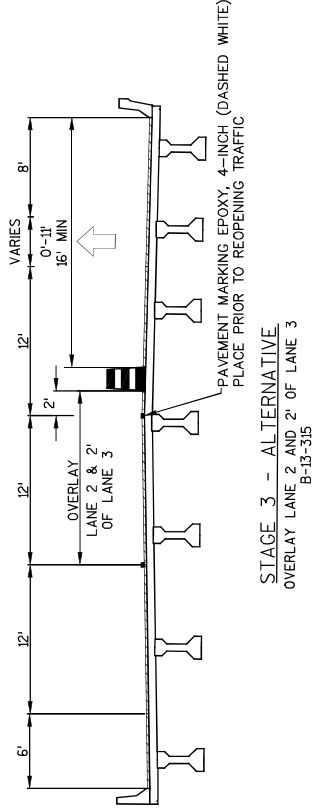

STAGE 3 - ALTERNATIVE
OVERLAY LANE 2 AND 2' OF LANE 3
B-13-315

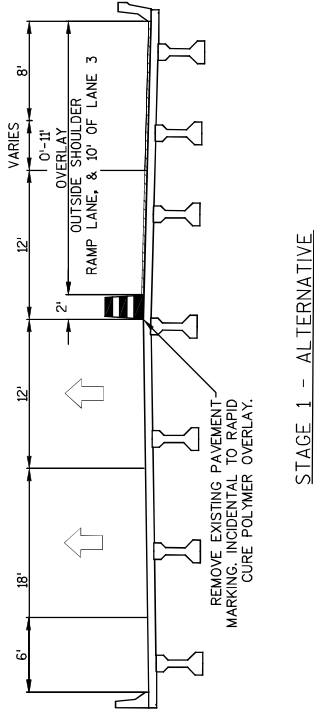

STAGE 1 - ALTERNATIVE
OVERLAY OUTSIDE SHOULDER RAMP LANE, AND 10' OF LANE 3
B-13-315

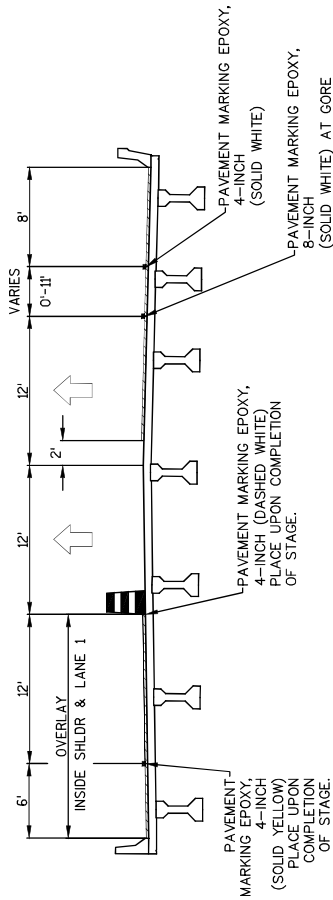

STAGE 2 - ALTERNATIVE
OVERLAY INSIDE SHOULDER AND LANE 1
B-13-315

Addendum No. 02
ID 1206-04-65
Added Sheet 8A
April 8, 2016

NOTES:
ALTERNATIVE STAGING SHOWN FOR EB TRAFFIC, WB SIMILAR.
FOLLOW STAGE 5/10 TRAFFIC CONTROL PLANS FOR STAGE 1 TRAFFIC ALTERNATIVE.
FOLLOW STAGE 1/6 TRAFFIC CONTROL PLANS FOR STAGE 2 ALTERNATIVE.
FOLLOW STAGE 3/8 TRAFFIC CONTROL PLANS FOR STAGE 3 ALTERNATIVE.

PROJECT NO: 1206-04-65	COUNTY: DANE	TRAFFIC CONTROL TYPICAL SECTIONS- ALTERNATIVE STAGING	SHEET 8A	E
FILE NAME : C:\USERS\JACKM\WORK\PROJECTS\120600-TC.DWG	PLOT DATE : 4/7/2016 4:01 PM	PLOT NAME : JACM, JOSHUA	PLOT SCALE : 1:1 IN:10 FT	WISDOT/CADD SHEET 42
25000 - 025000.TC - 025003.TC	HWY: USH 12			
