


ID 5845-04-72
City of Stoughton, West Main Street
Hoel Avenue to Page Street



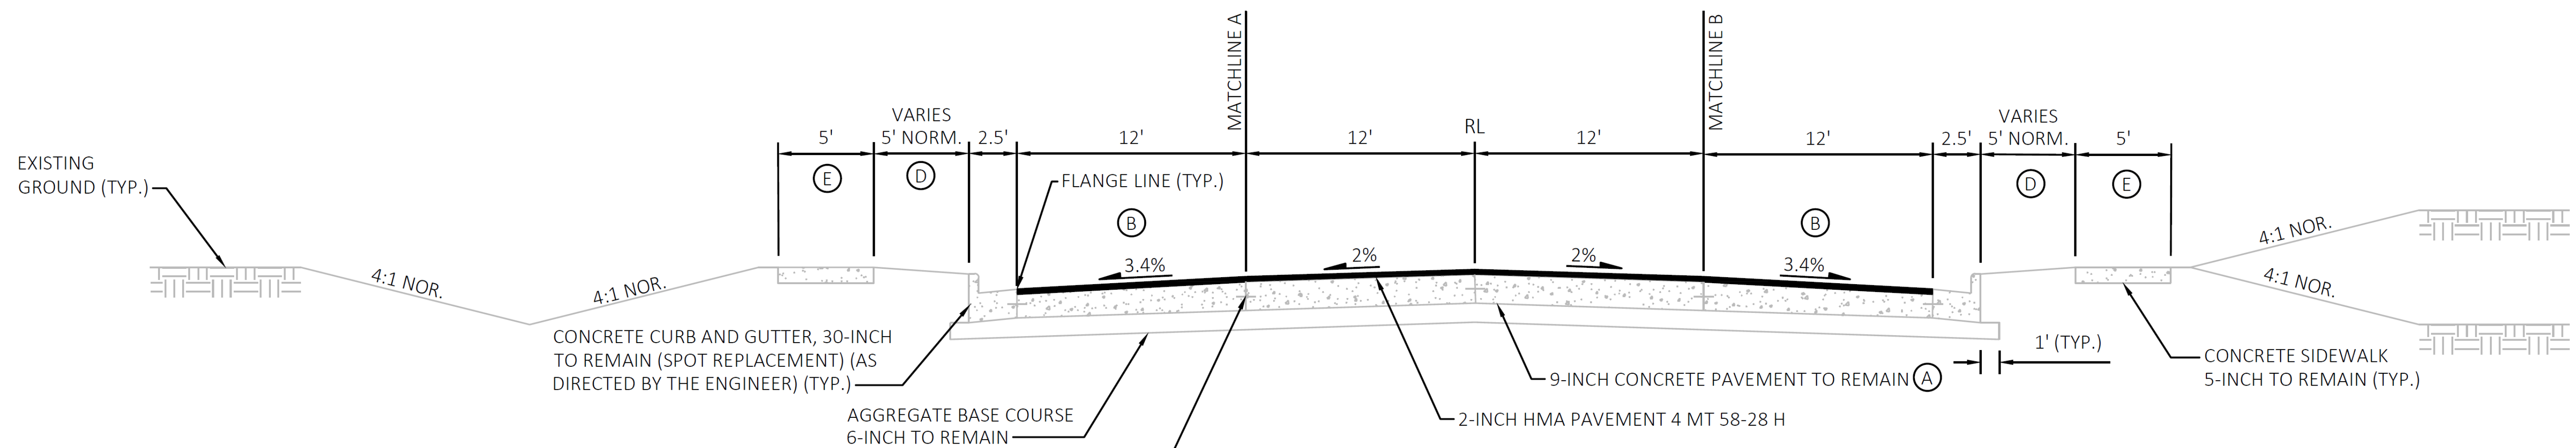

TYPICAL PROPOSED SECTION

Hoel Avenue to Van Buren Street

(A) CONCRETE JOINT AND CRACK CLEANING AND REPAIR REQUIRED AS DIRECTED BY THE ENGINEER. SEE STANDARD SPECIFICATIONS FOR ADDITIONAL INFORMATION.

BASE PATCHING CONCRETE REQUIRED AS SHOWN ON THE PAVEMENT REHABILITATION PLAN AND AS DIRECTED BY THE ENGINEER.


(B) REMOVING CONCRETE SURFACE PARTIAL DEPTH FROM 2-INCHES AT CONCRETE CURB AND GUTTER FLANGE LINE TO 0-INCHES AT 12-Feet FROM FLANGE.

(C) VARIES 12-Feet TO 10-Feet STATION 48+62 TO STATION 50+28.


(D) SEE CURB RAMP DETAILS FOR ADDITIONAL INFORMATION AT INTERSECTIONS. RESTORE DISTURBED AREAS WITH TOPSOIL; FERTILIZER TYPE B; SEEDING MIXTURE NO. 40; AND MULCHING.

(E) REPLACE CURB RAMP WITH CONCRETE SIDEWALK 4-INCH OVER BASE AGGREGATE DENSE $\frac{3}{4}$ -INCH, 4-INCHES

(F) SEE CONSTRUCTION DETAILS FOR UNDERDRAIN DIMENSIONS, MATERIALS, AND LOCATION.

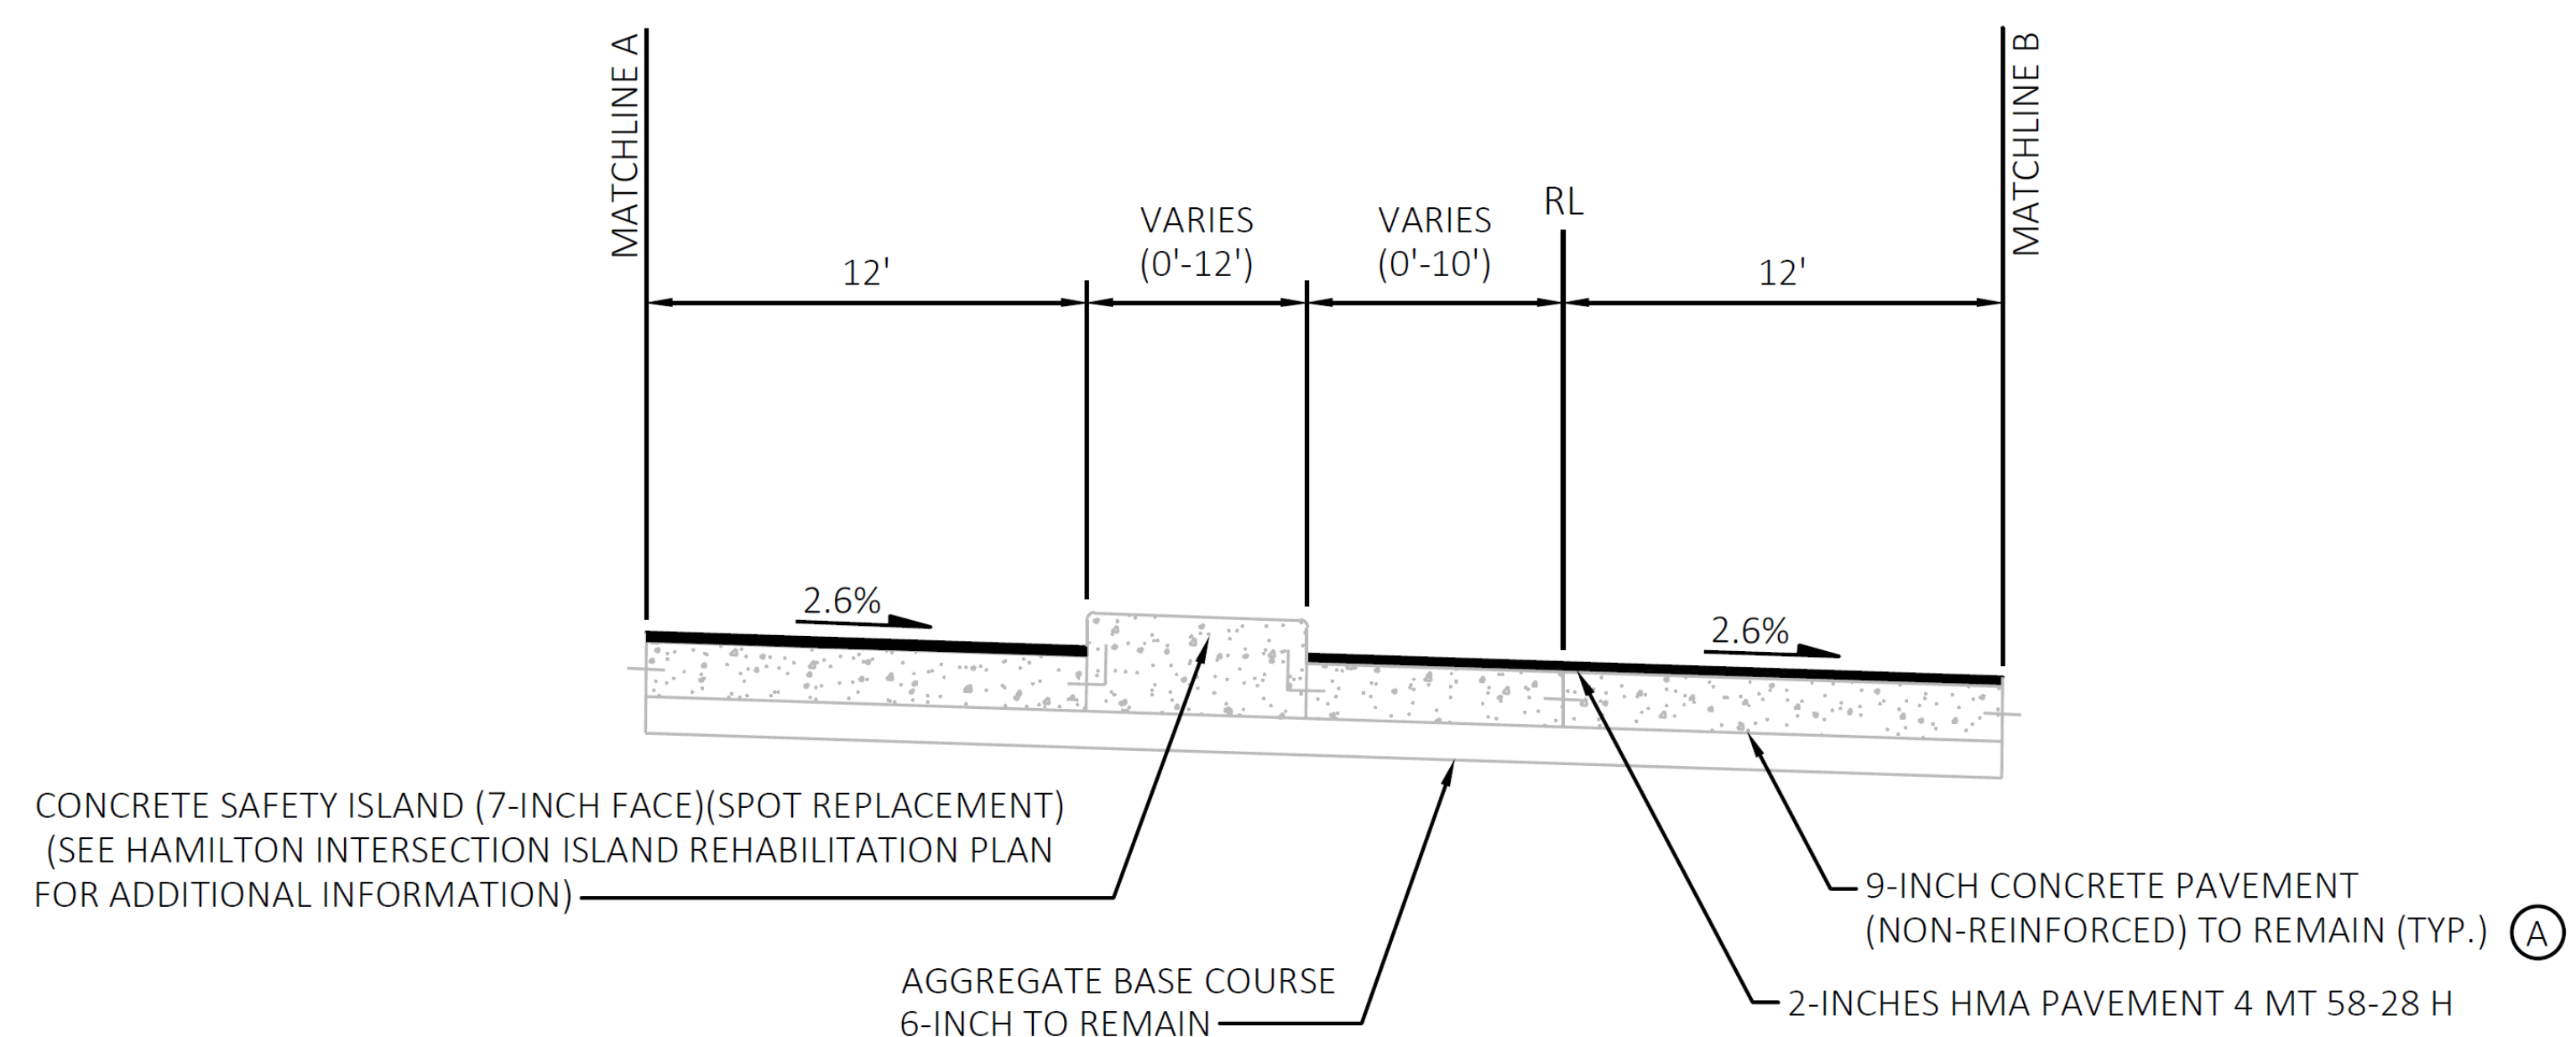


Island Near Hamilton Street

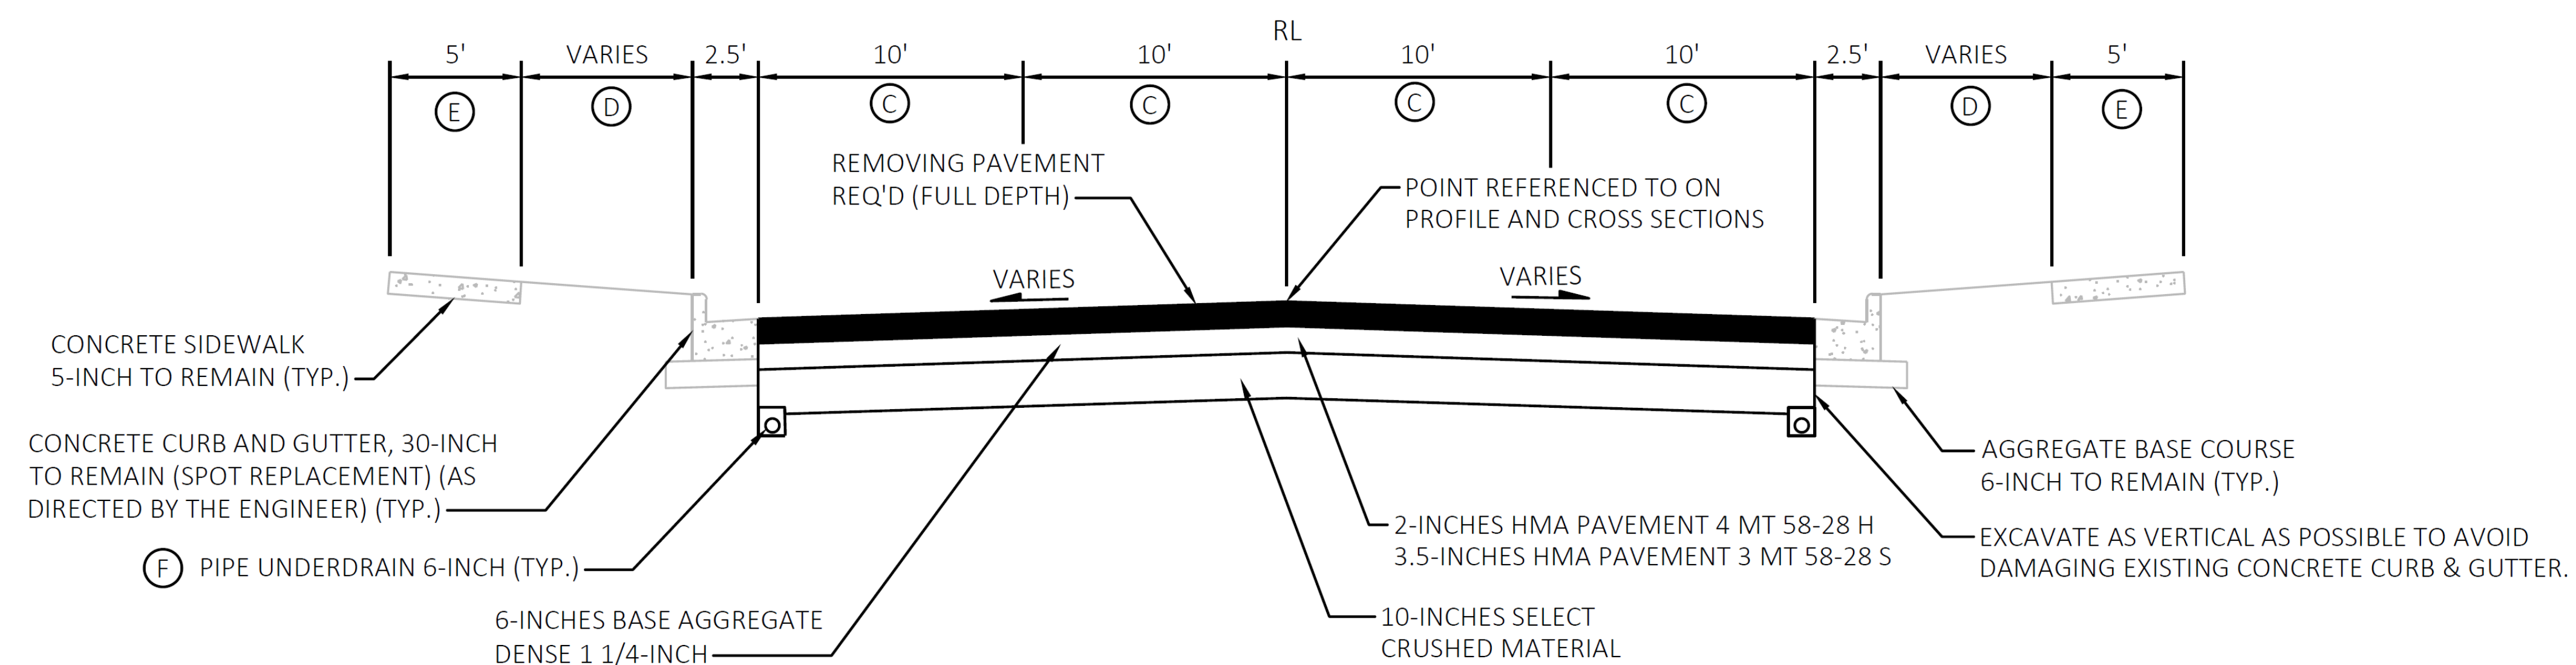






TYPICAL PROPOSED SECTION

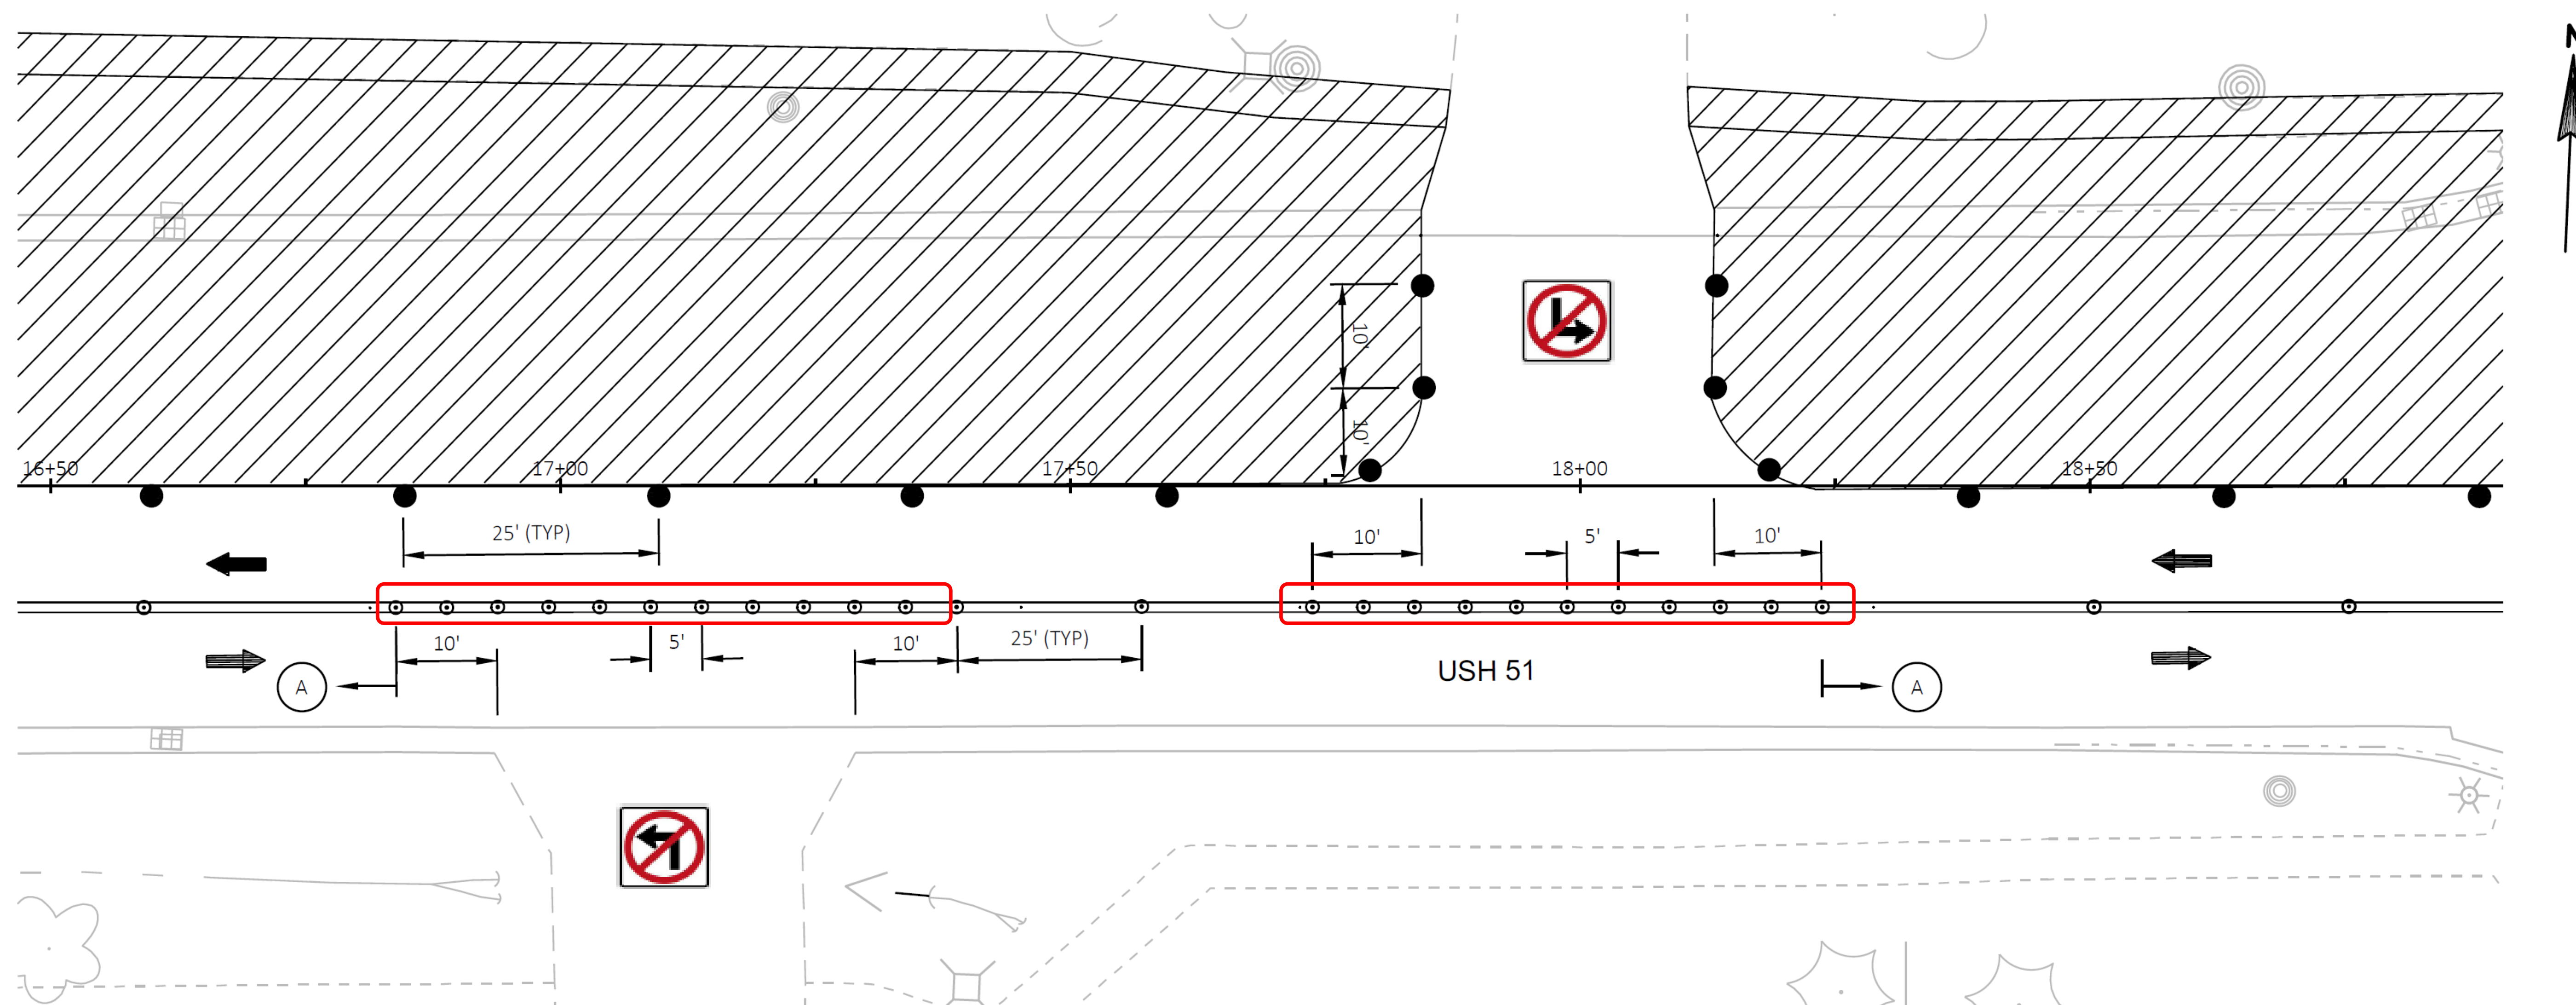Van Buren Street to Page Street



LEGEND

-  WORK ZONE
-  TRAFFIC FLOW ARROW
-  TRAFFIC CONTROL DRUM
-  FLEXIBLE TUBULAR MARKER POSTS AND BASES




 No left turns


TEMPORARY ACCESS TO DRIVEWAY DETAIL

Construction Staging Stage 1

Work zone on south side of US 51

Estimated start date: June 2, 2020

-  Work Zone
-  Sideroads open at all times
-  Sideroads have right in/right out access (no left turns or through movements)

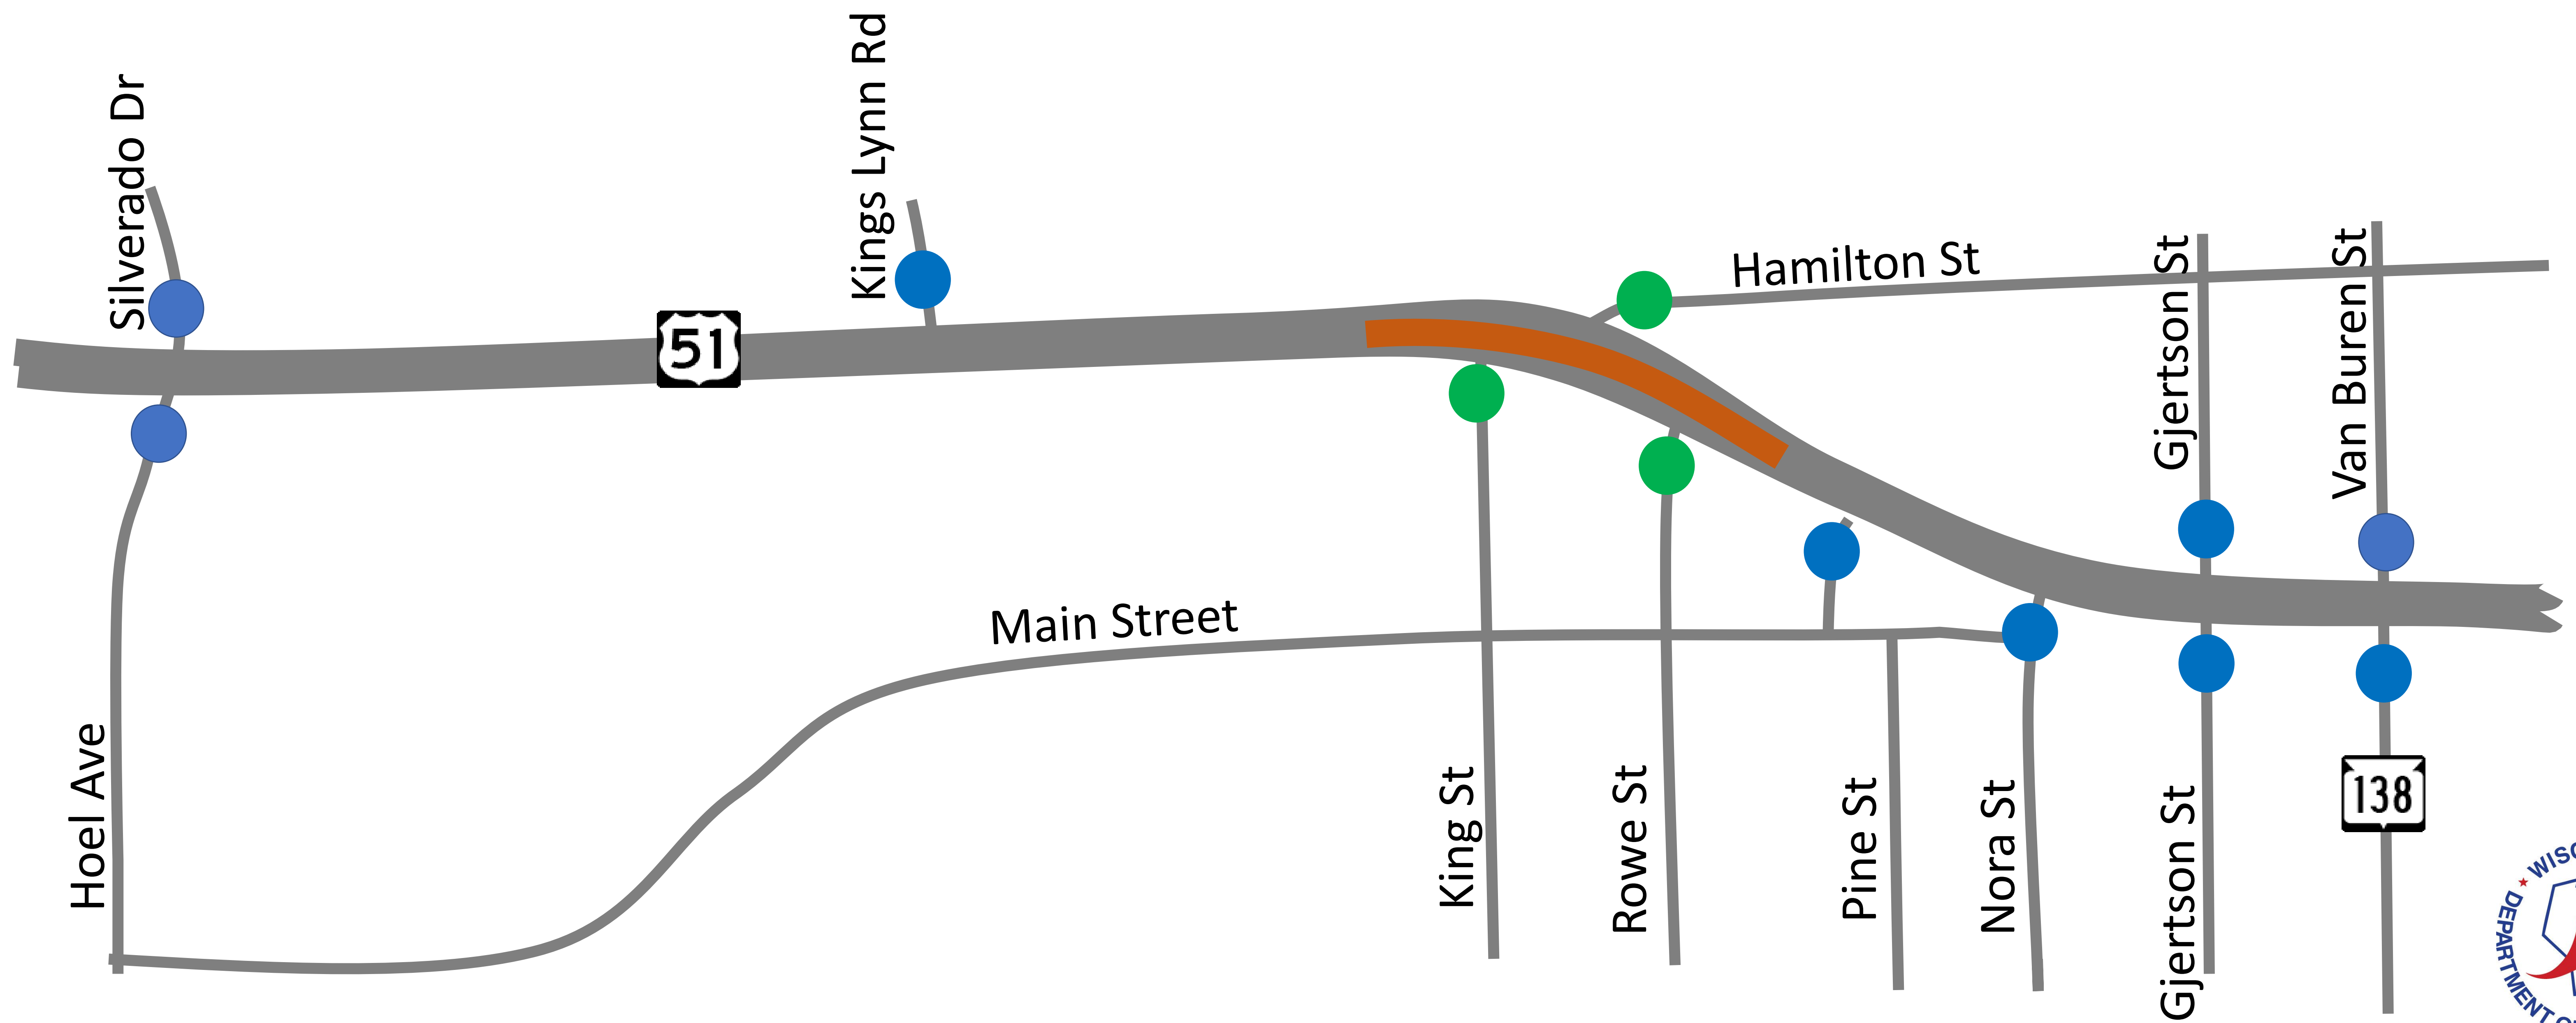


Construction Staging Stage 2

Work zone on south side of US 51

- Work Zone
- Sideroads open at all times
- Sideroads have right in/right out access (no left turns or through movements)
- Sideroads closed during Stage 2
- Alternate sideroad closures
One road needs to stay open while other is closed
- Short-term sideroad closures
~10 Calendar Days – not concurrent

NORTH

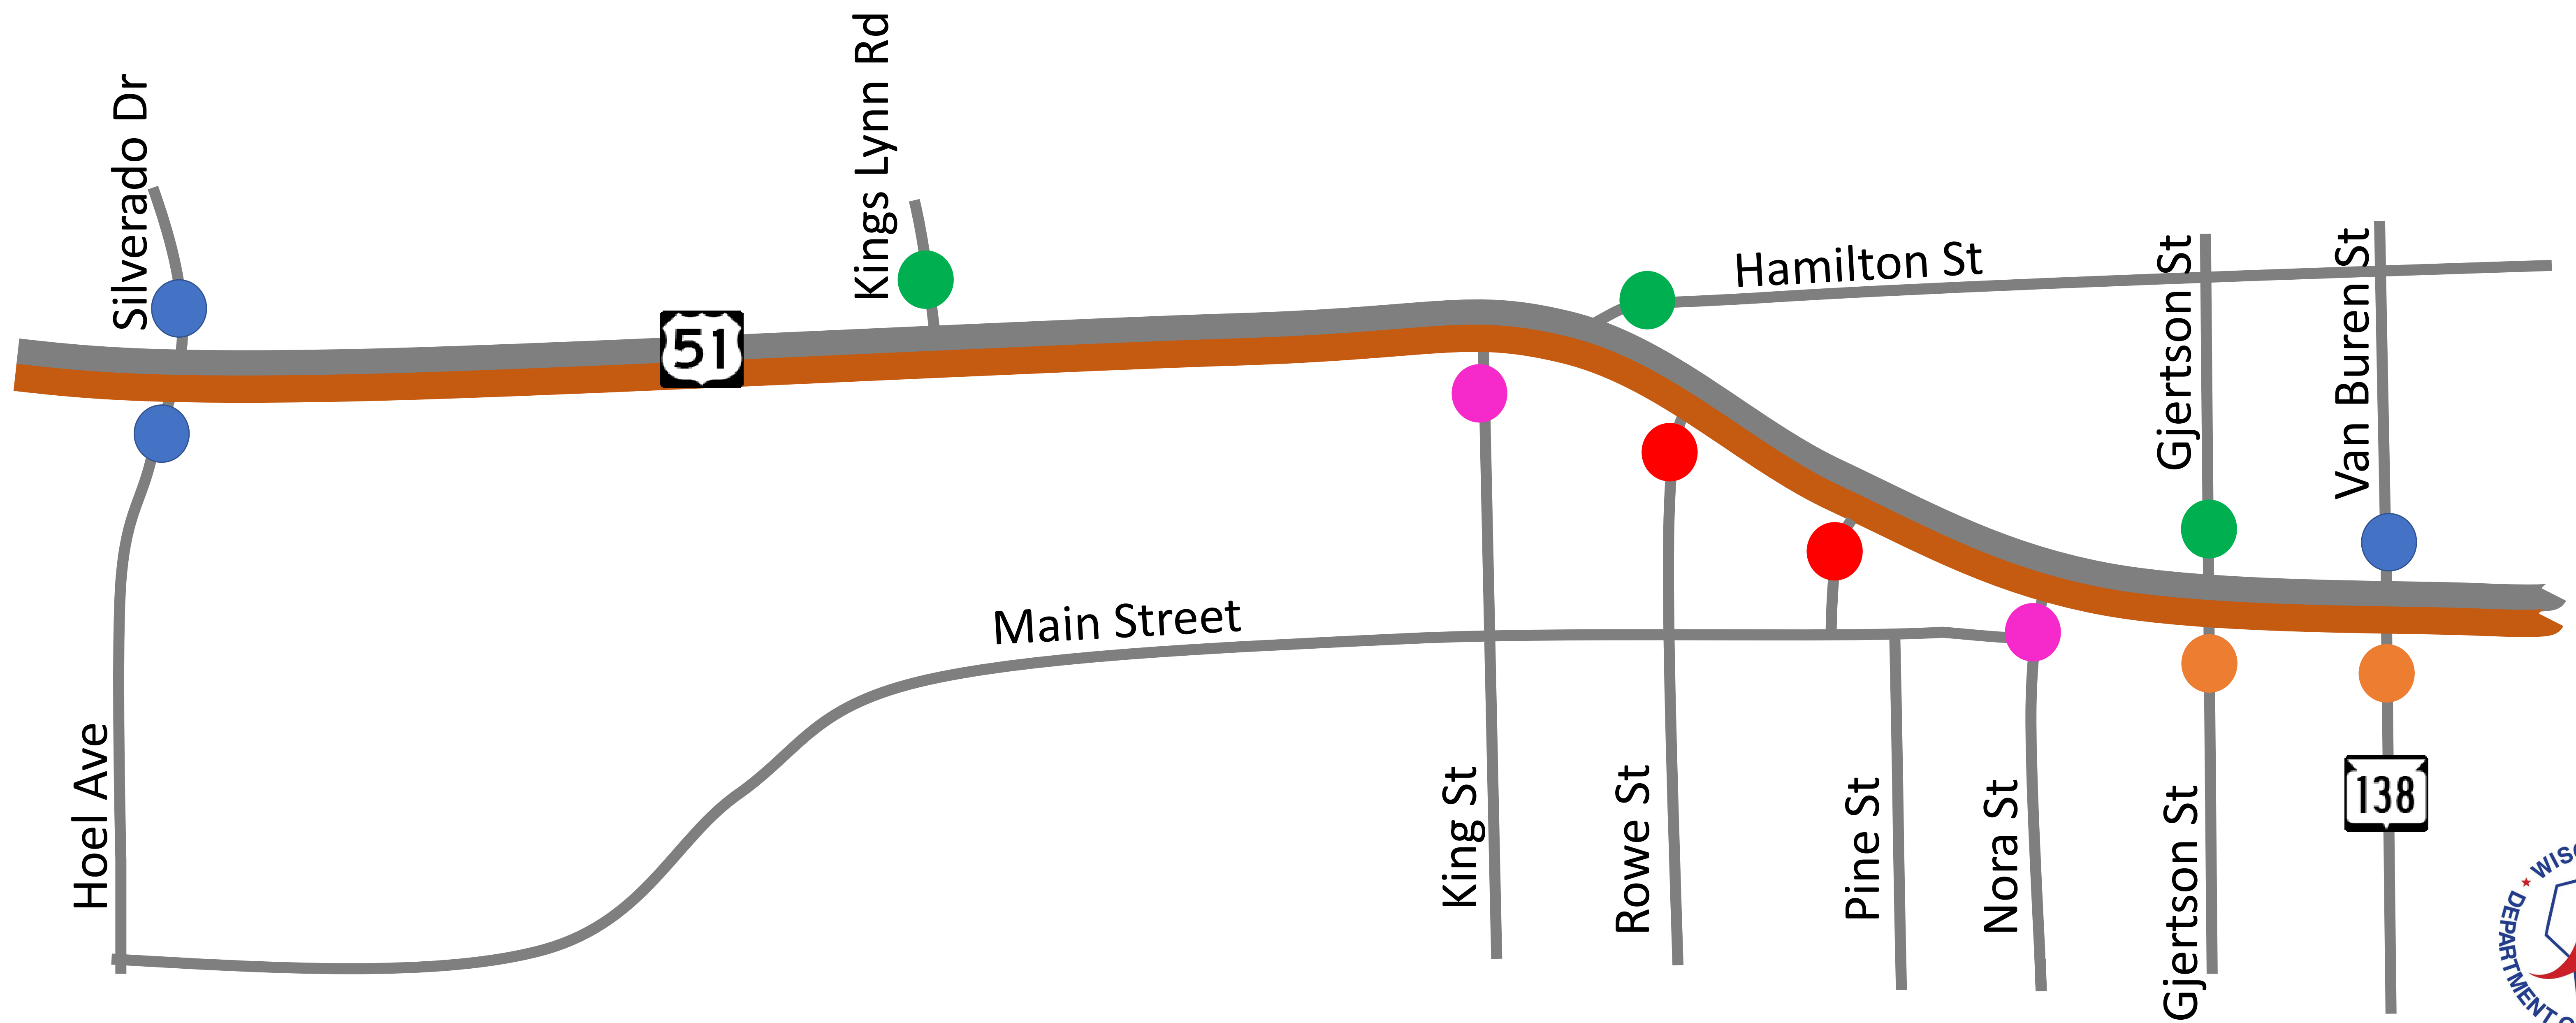


Construction Staging Stage 3

Work zone on north side of US 51

- Work Zone
- Sideroads open at all times
- Sideroads have right in/right out access (no left turns or through movements)
- Alternate sideroad closures
One road needs to stay open while other is closed
- Short-term sideroad closures
~10 Calendar Days – not concurrent

* In addition to these closures there will be a one-day sideroad closure during milling operations and a one-day sideroad closure during paving operations.

NORTH

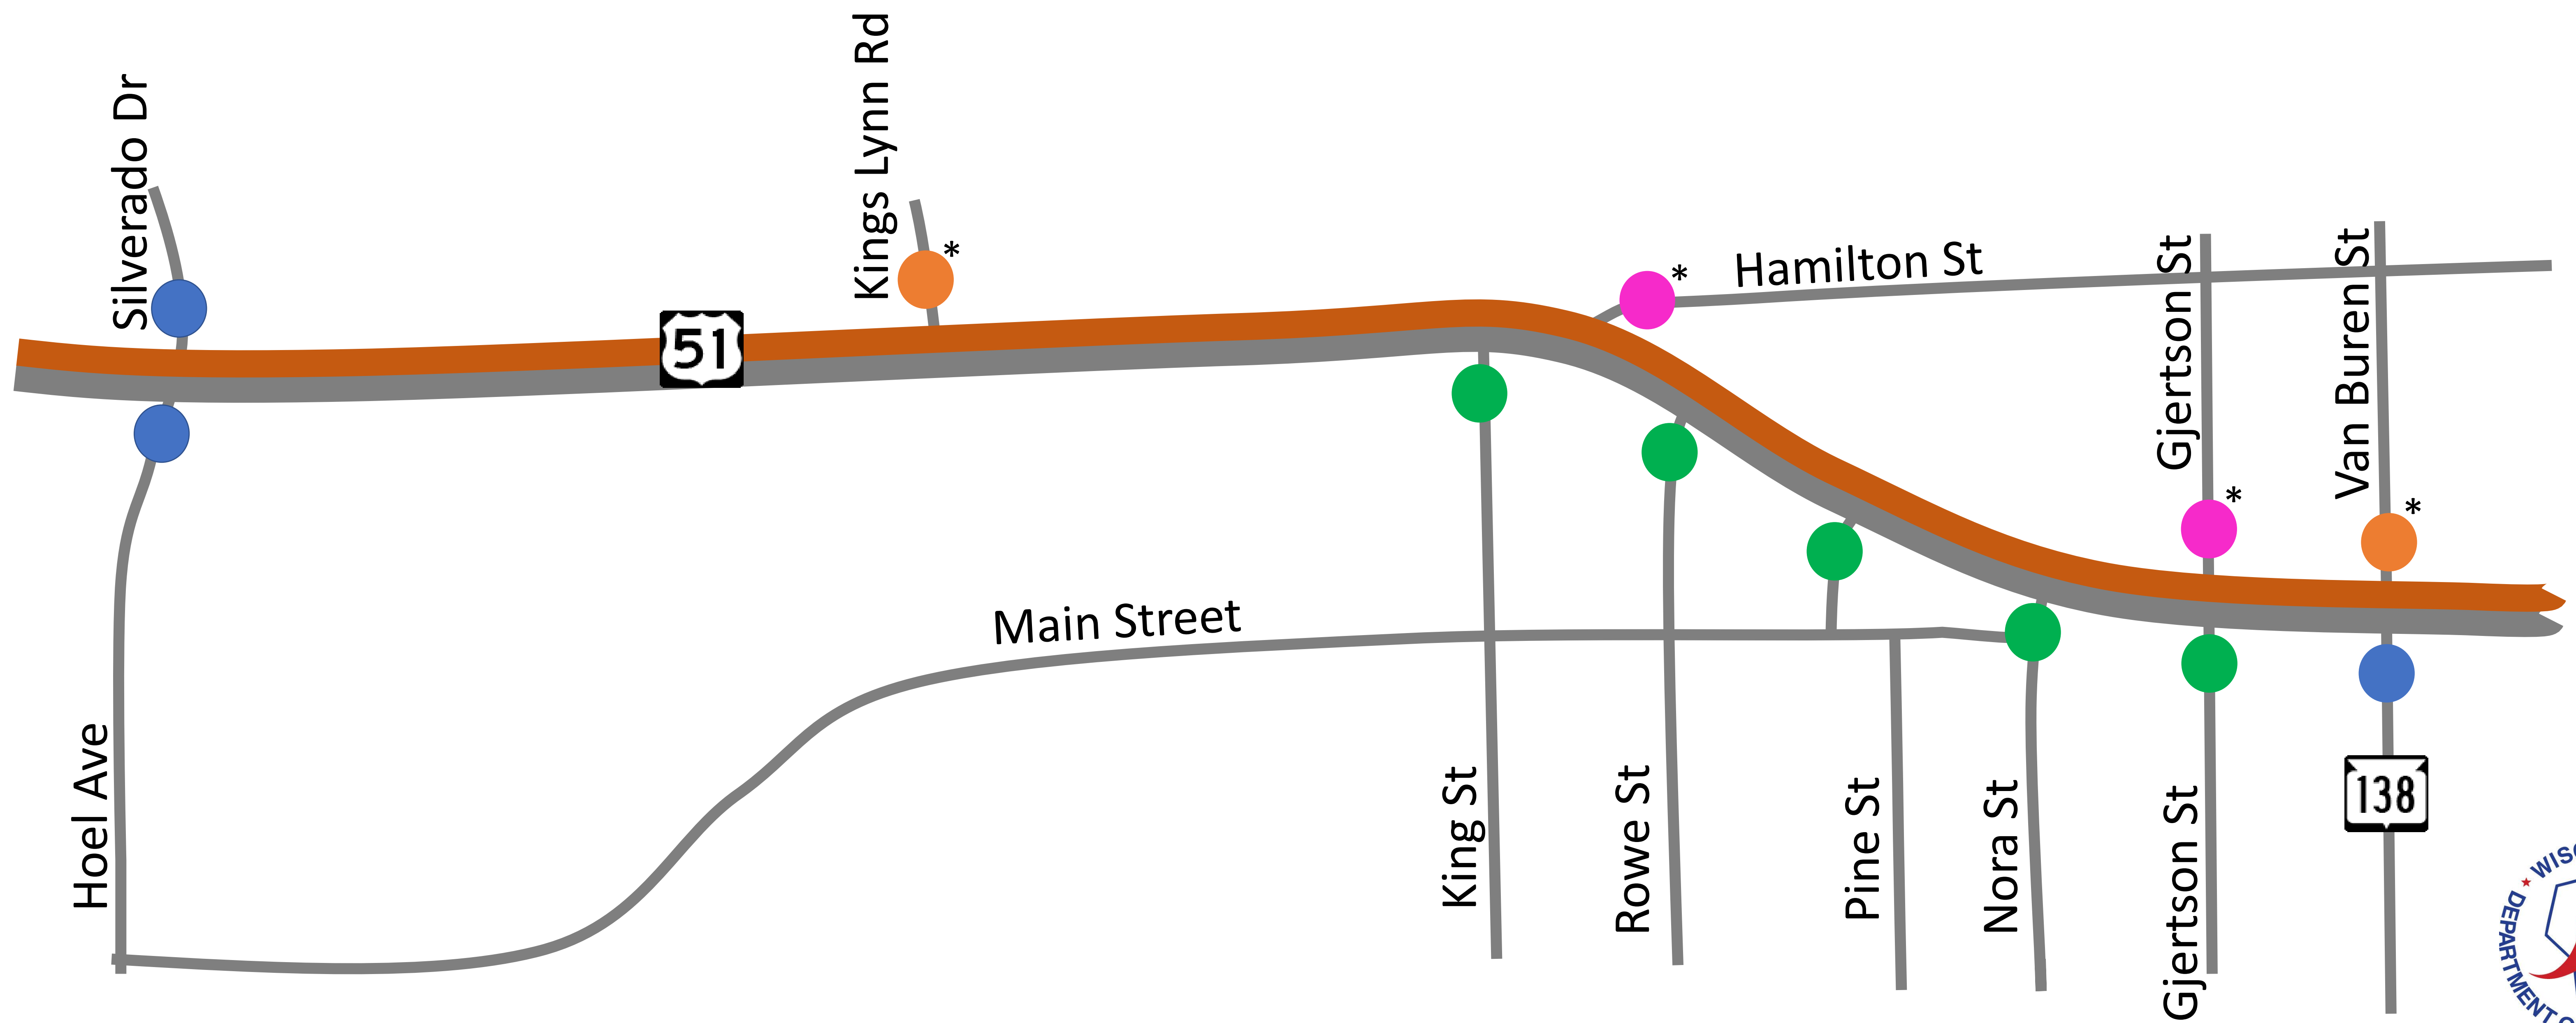

Construction Staging Stage 4

Work zone on south side of US 51

Estimated completion date: October 9, 2020



Work Zone

Sideroads open at all times

Sideroads have right in/right out access (no left turns or through movements)

* In addition to these closures there will be a one-day sideroad closure during milling operations and a one-day sideroad closure during paving operations.

WIS 138 (south leg) will have flagging operations to maintain traffic during milling and paving operations.

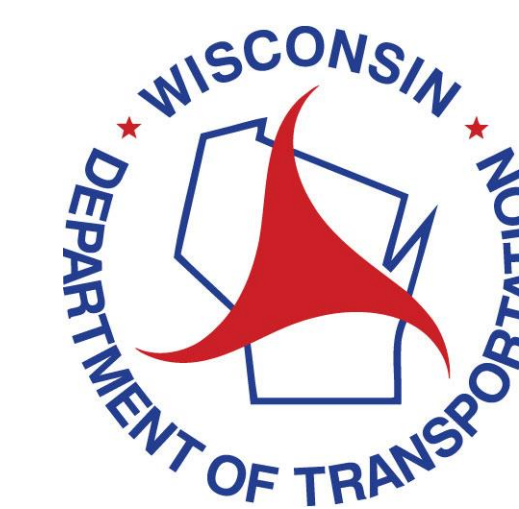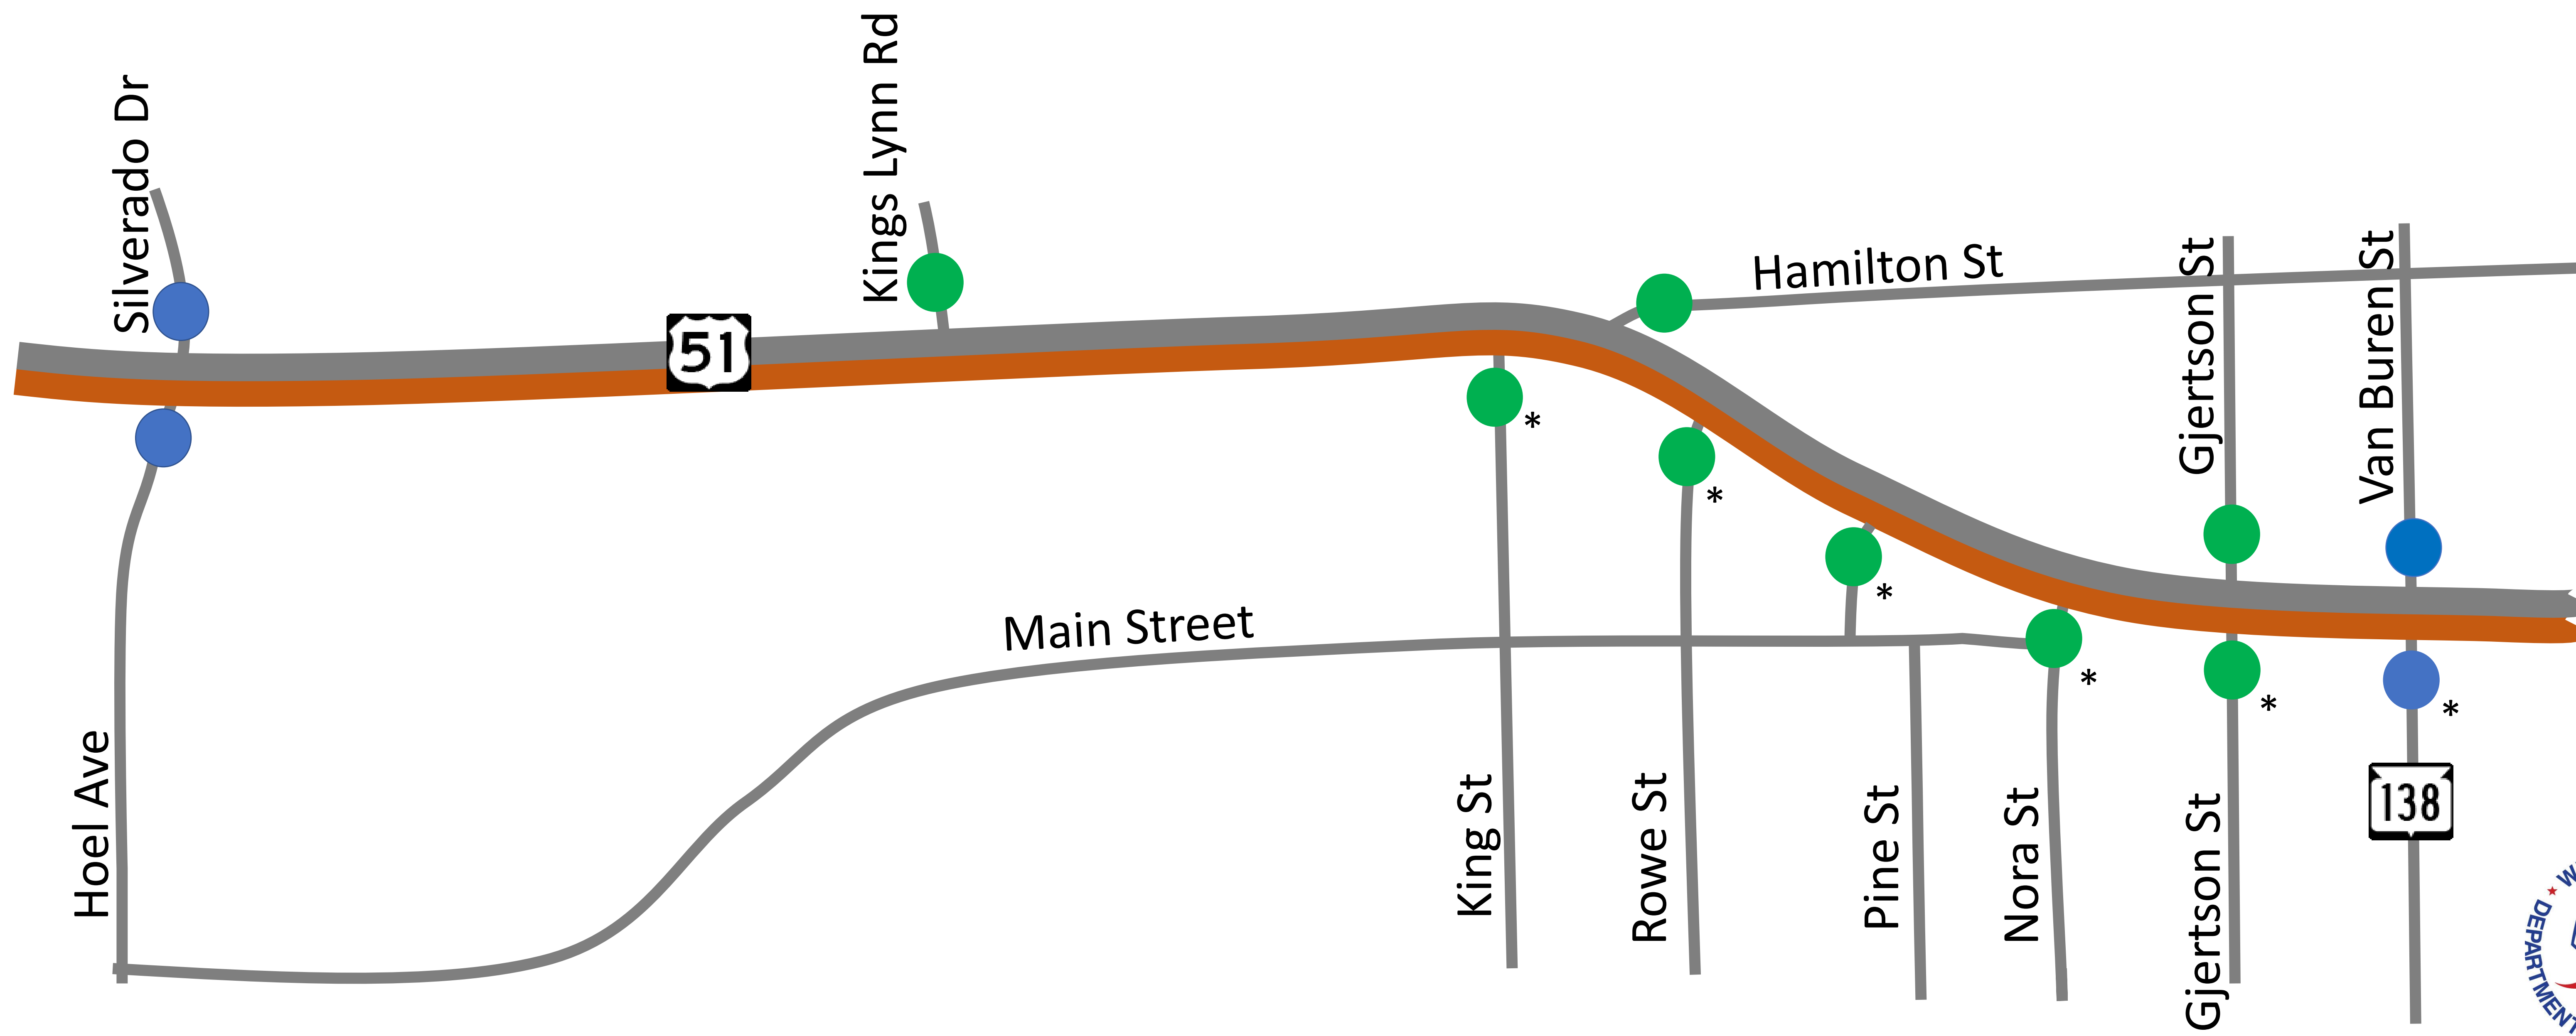


Detour

June 15, 2020 – August 28, 2020


- Work Zone
- Sideroad closed except to local traffic
- Short-term sideroad closures
~10 Calendar Days

- * See Construction Staging information for Short-term sideroad closures at WIS 138 (south) and Van Buren Street.
- ** The 10 consecutive calendar day closure of WIS 138 (south leg) and Page Street will not be allowed between Monday June 29 and Monday July 6 to avoid conflicts with the Independence Day Festival.

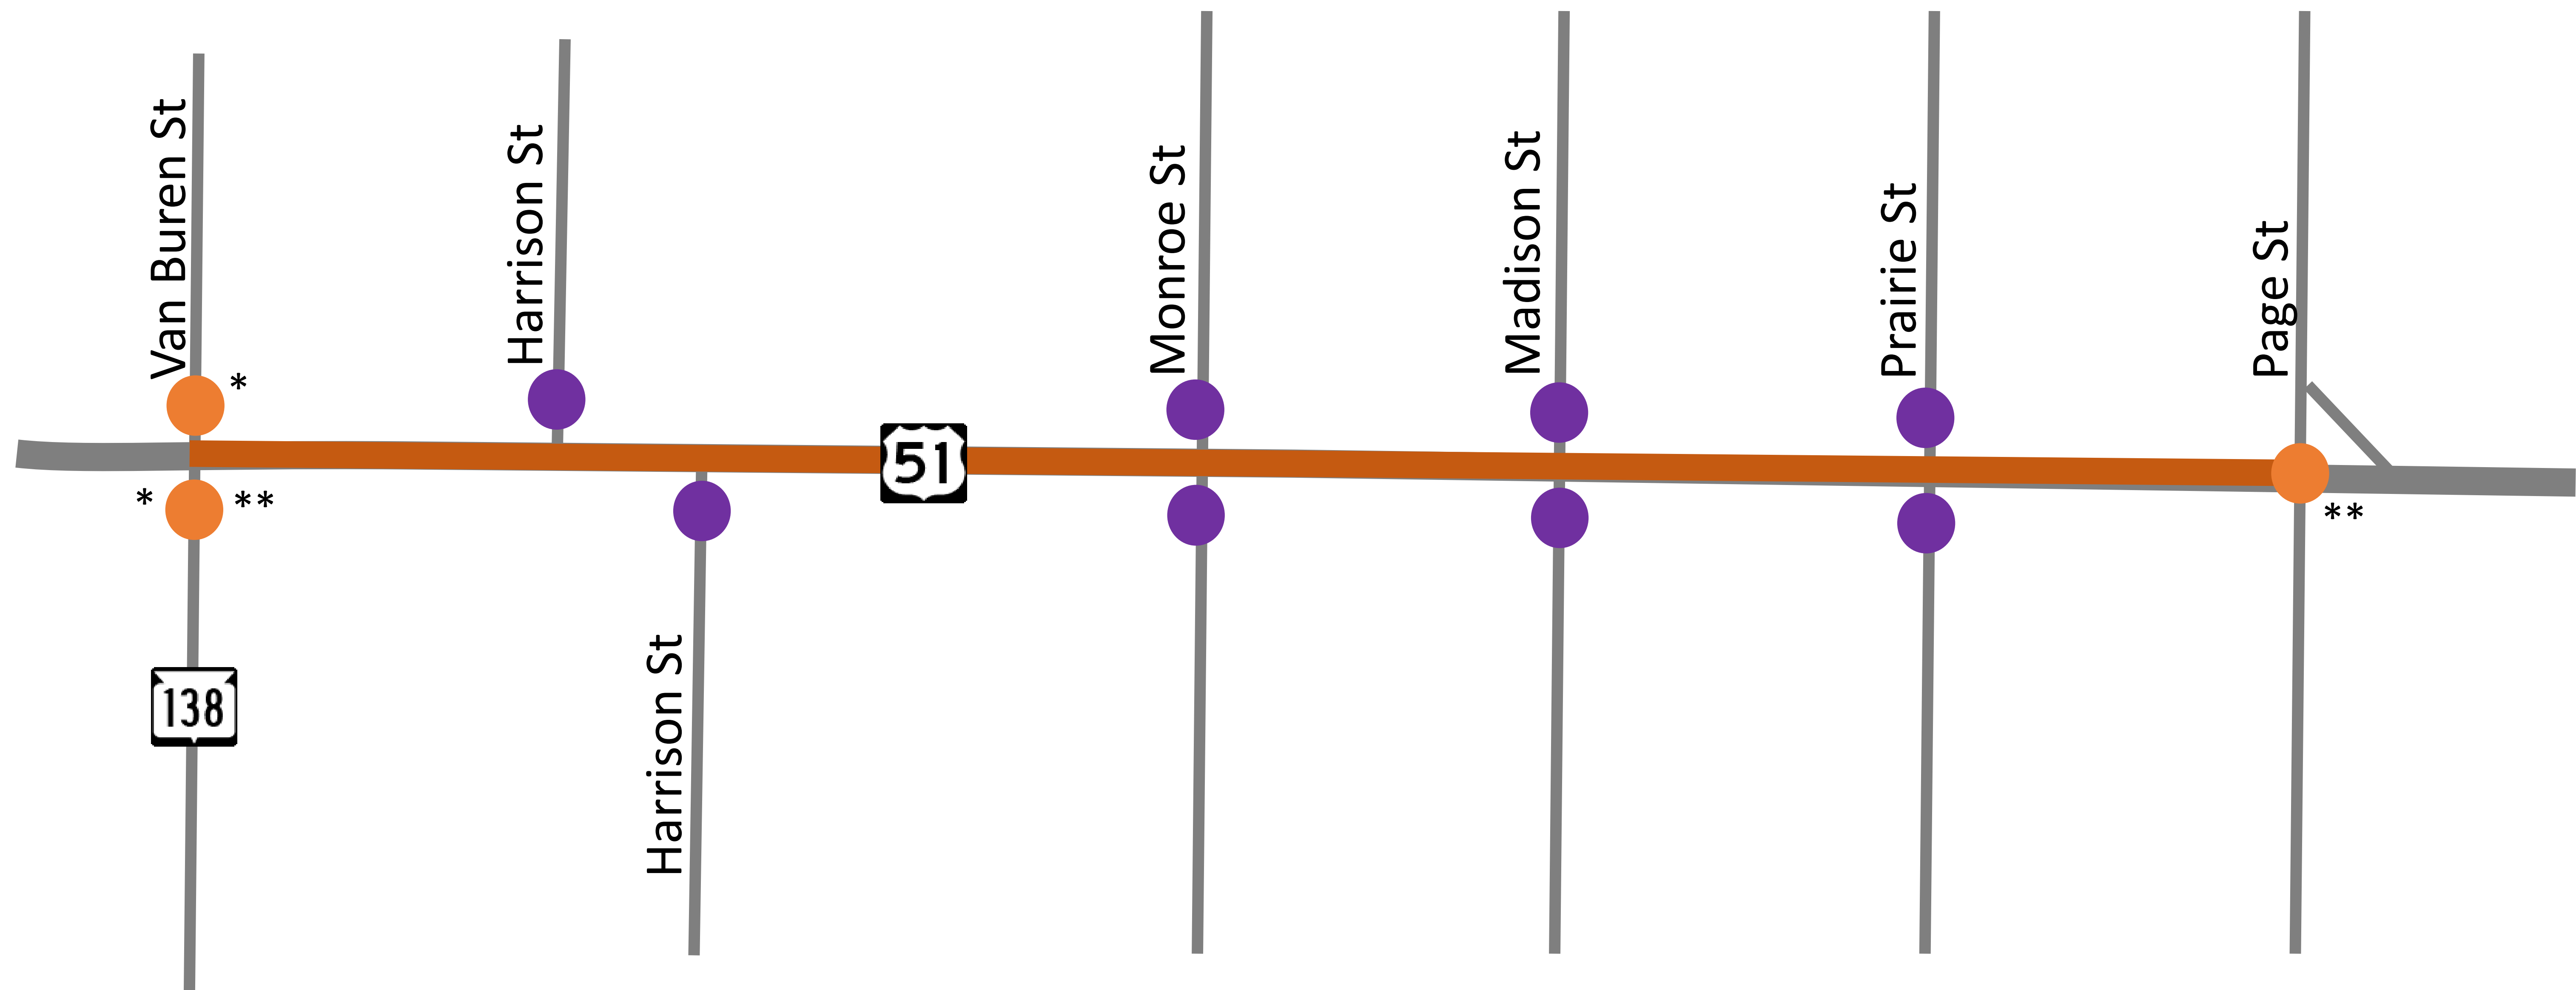


Construction Staging Stage 1

Median Island Near Hamilton Street

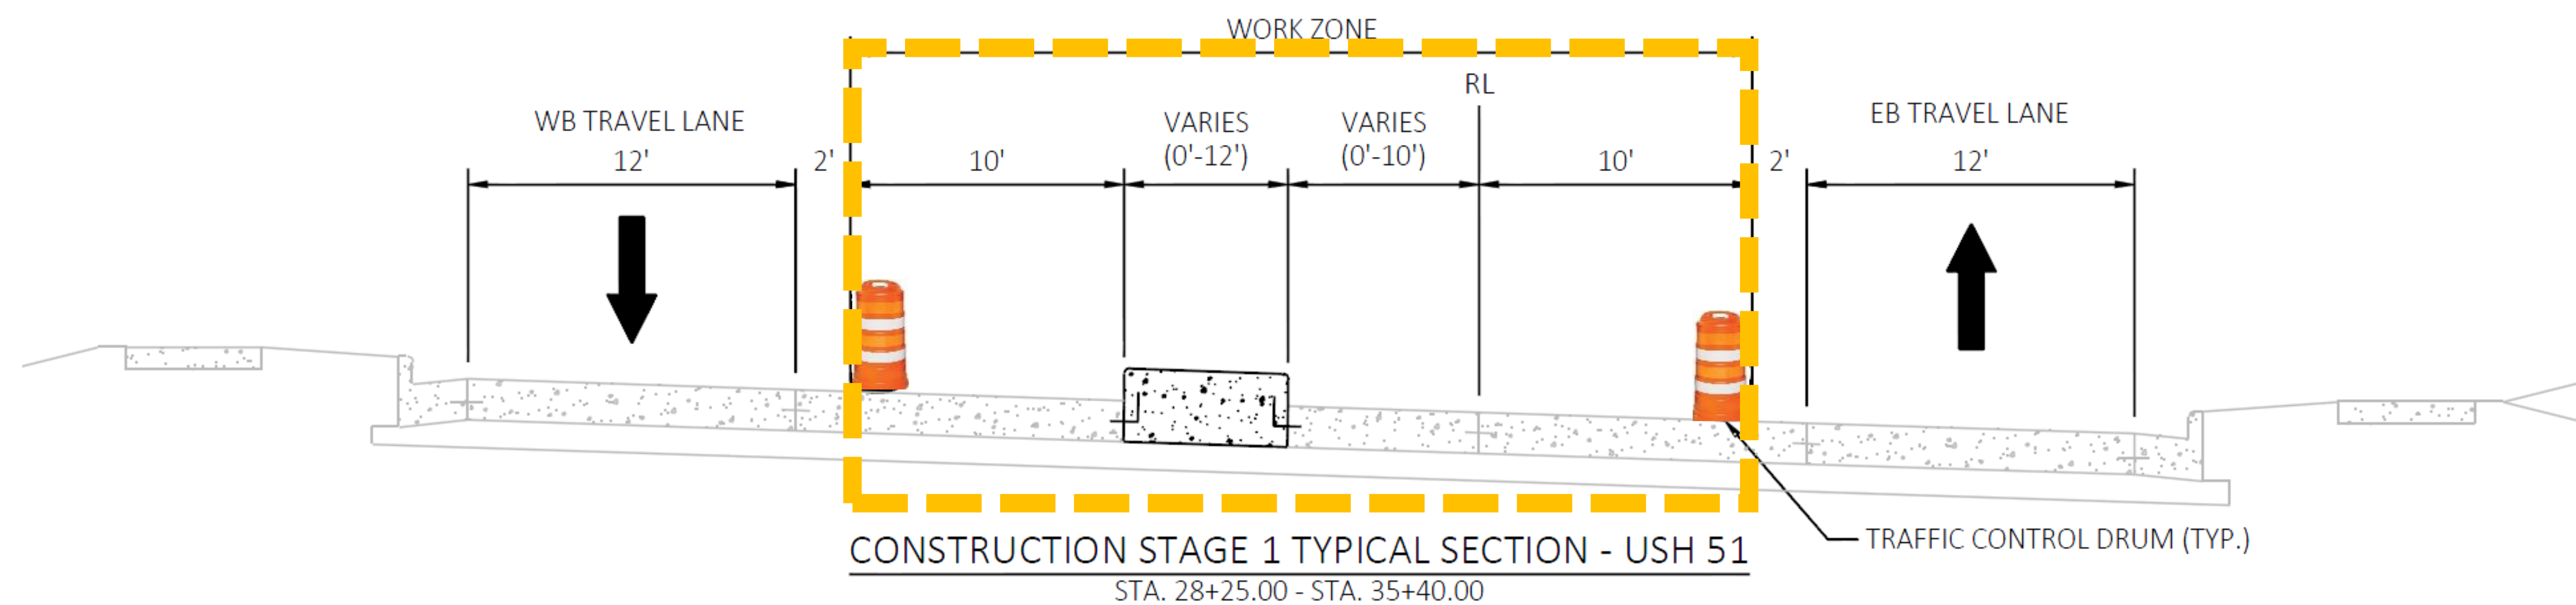

Construction Staging Stage 2


Construction on south side of US 51

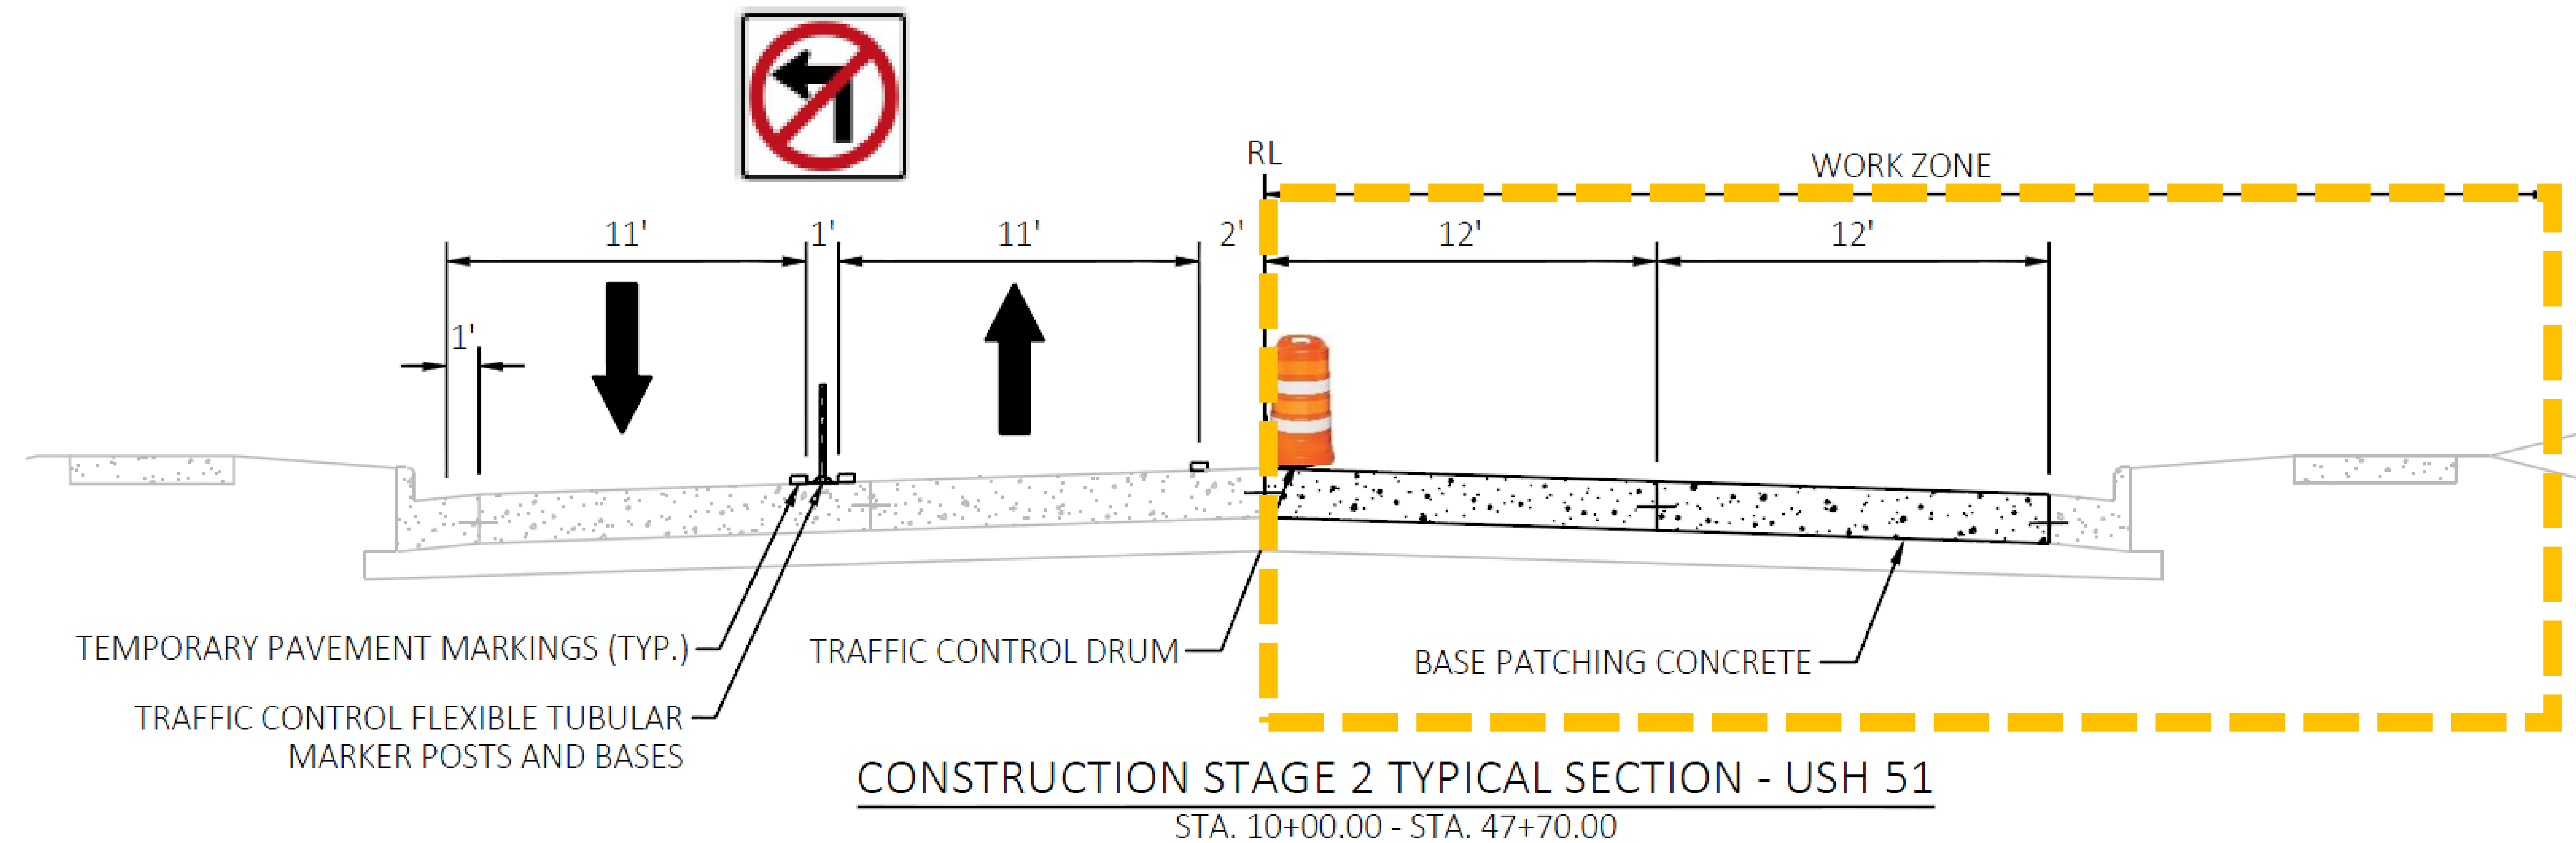

Right in/Right out access will be maintained to businesses and residences at all times.

Construction Staging Stage 3


Construction on north side of US 51

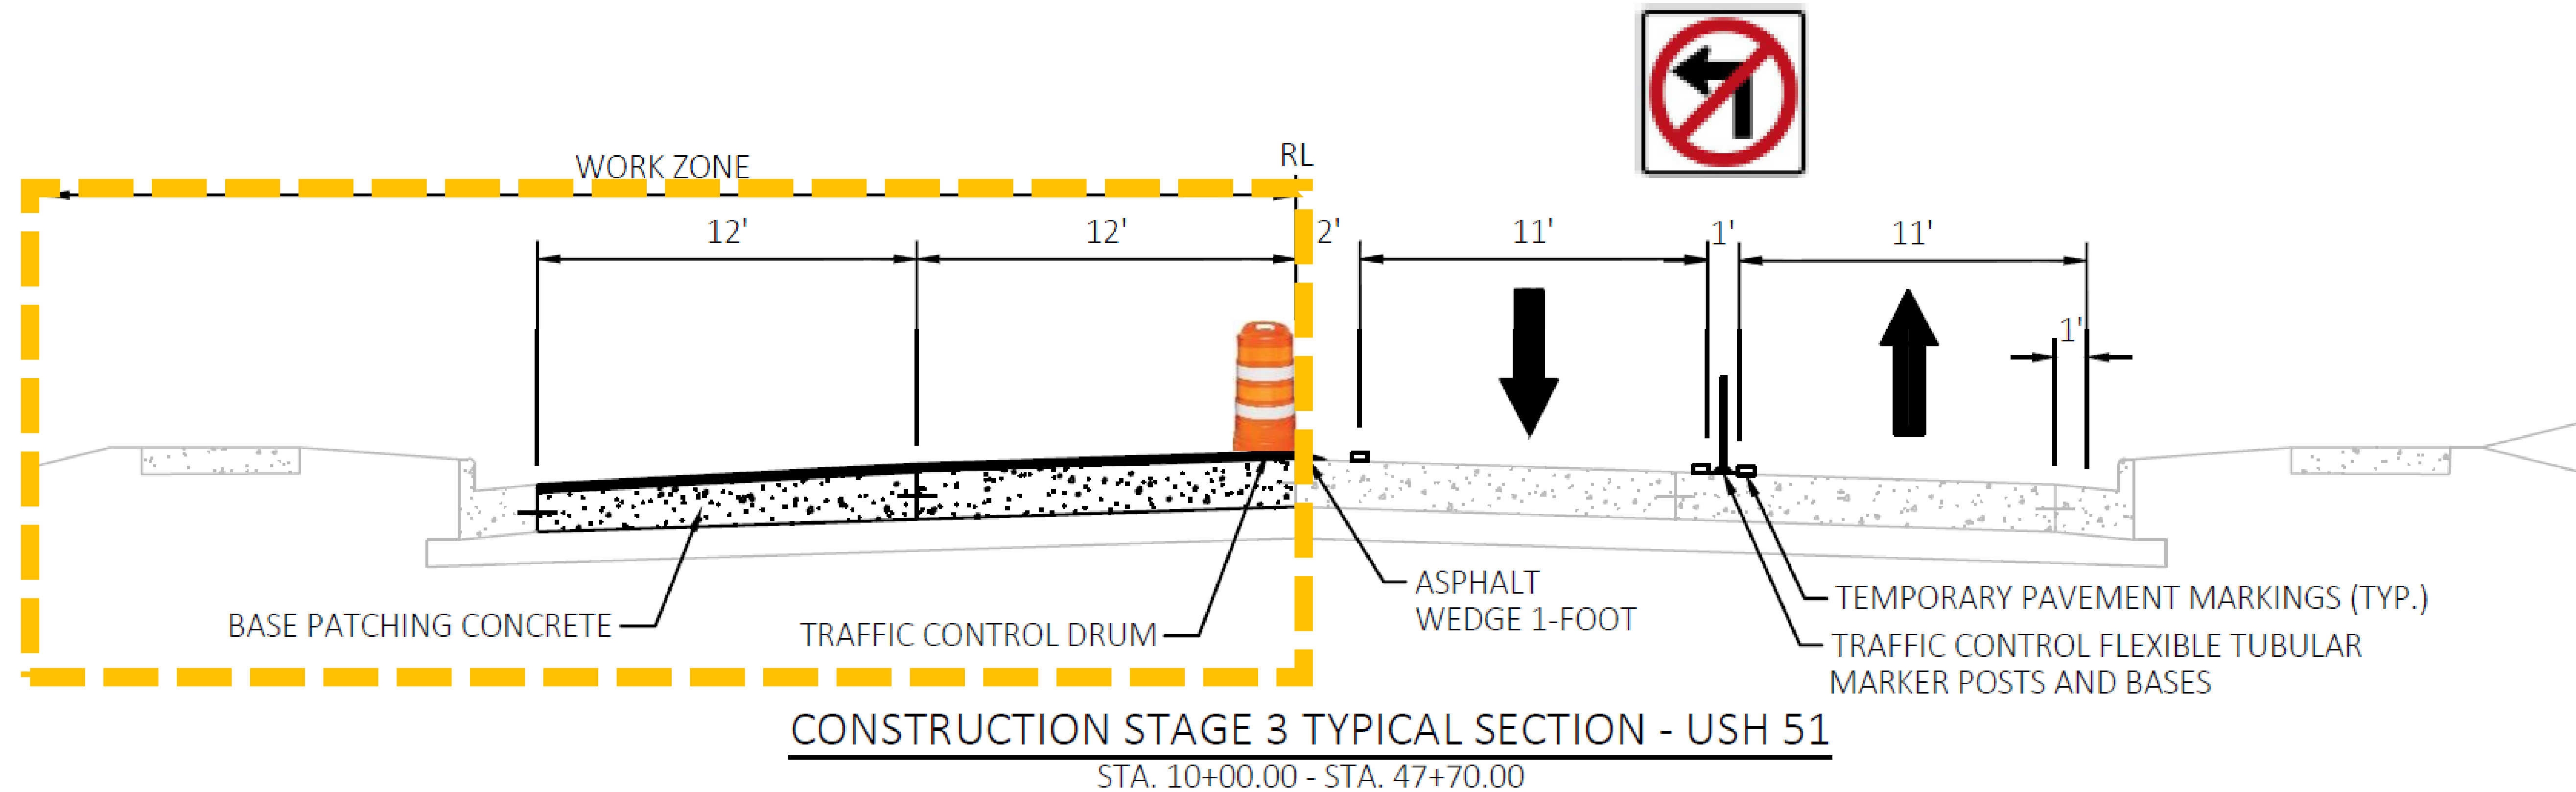

Right in/Right out access will be maintained to businesses and residences at all times.

Construction Staging Stage 4

Construction on south side of US 51

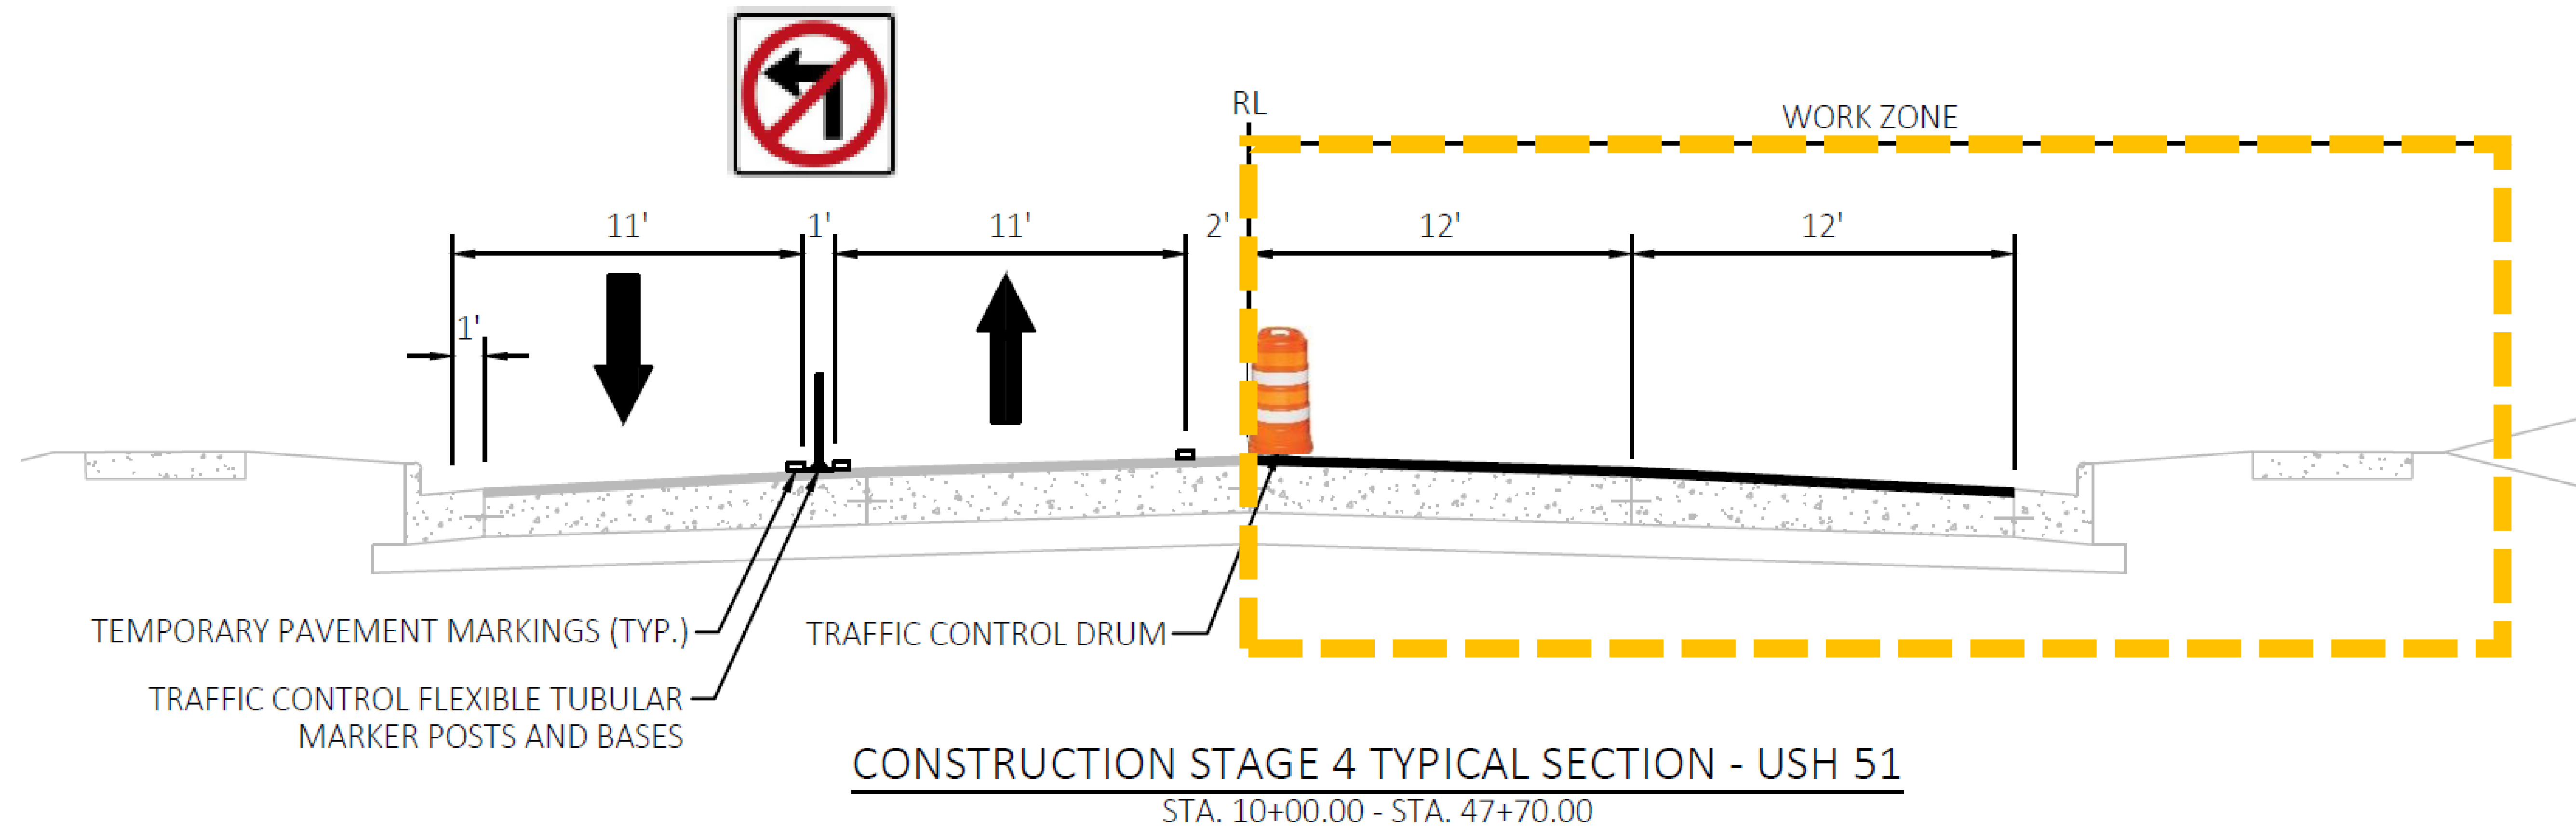

Right in/Right out access will be maintained to businesses and residences at all times.
