


Choosing the Appropriate Prosecution & Progress STSP Provisions

Working Day Contracts

Calendar Day Contracts

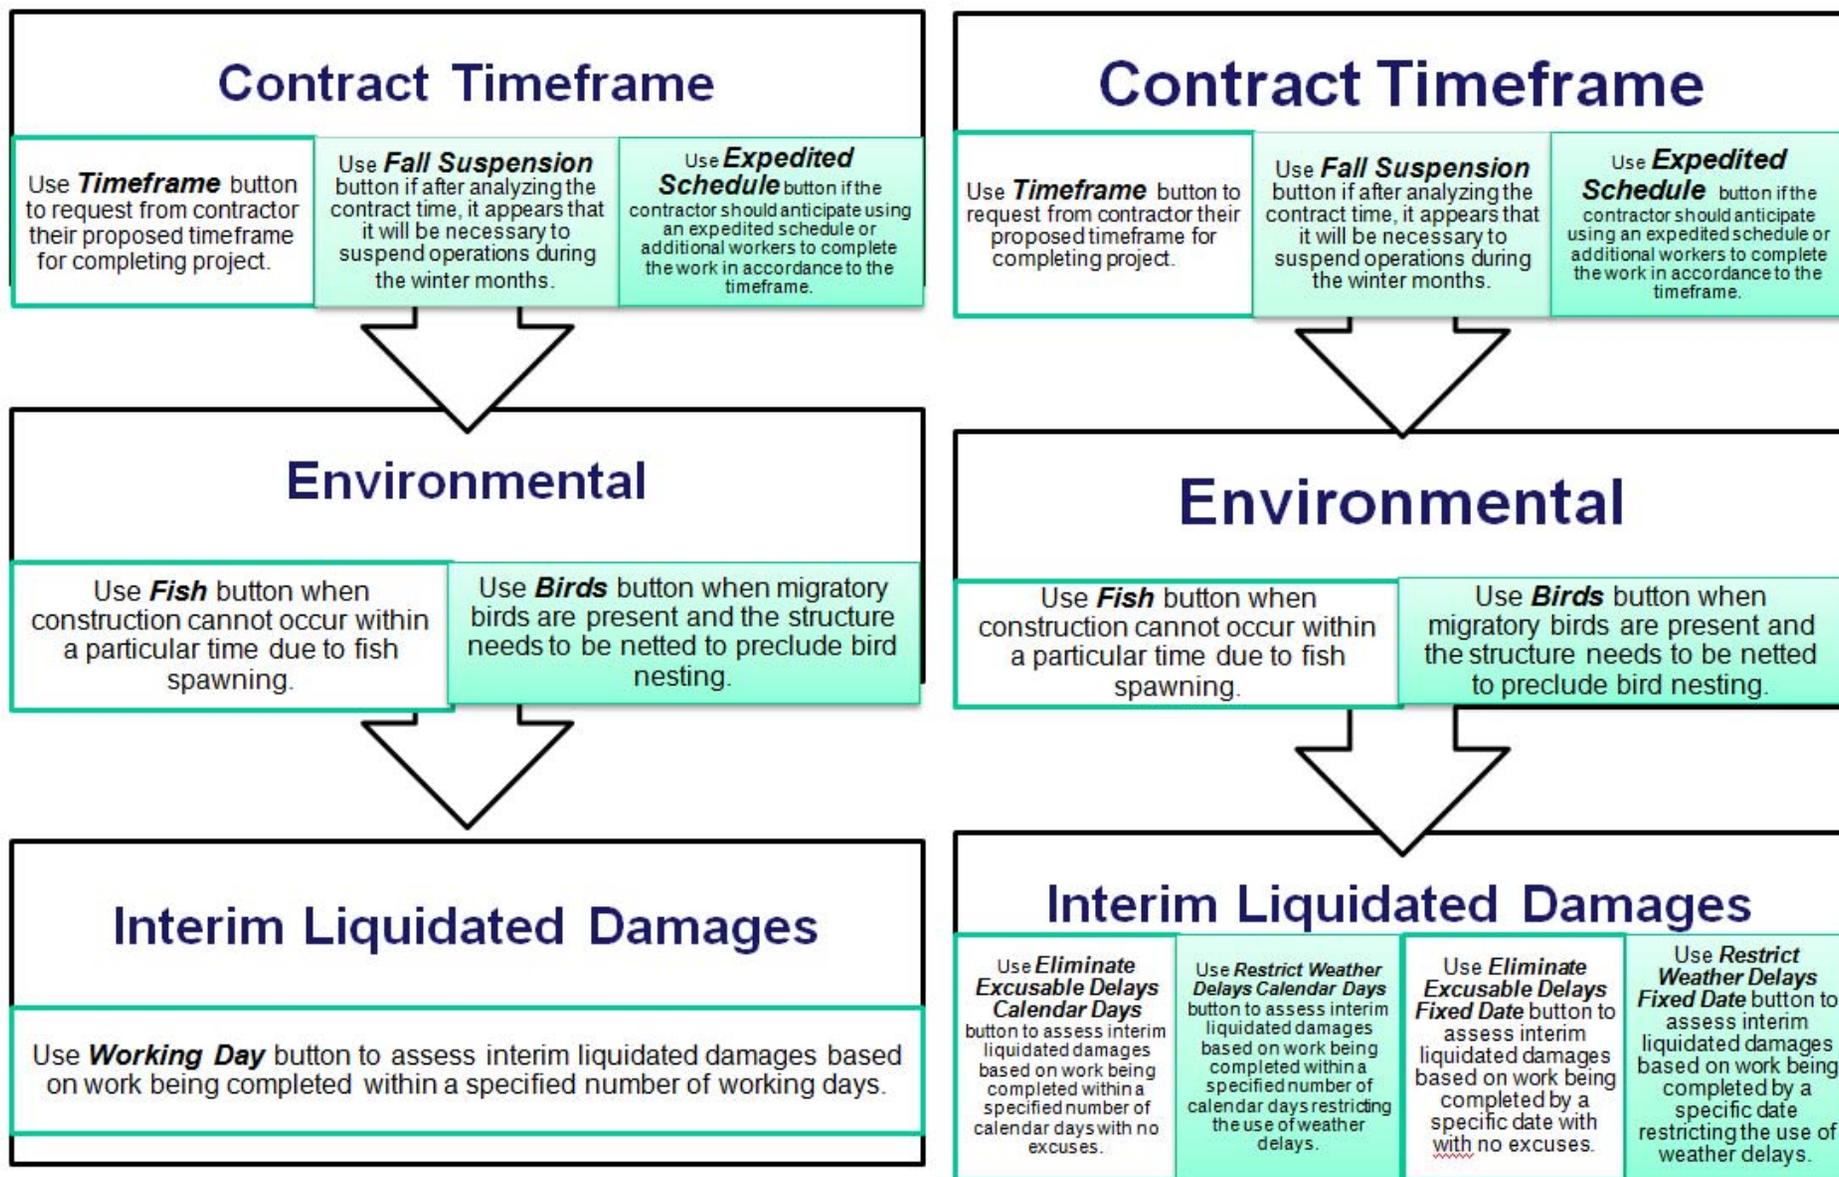

Completion Date Contracts

Contract Timeframe

Use **Timeframe** button to request from contractor their proposed timeframe for completing project.

Use **Expedited Schedule** button if the contractor should anticipate using an expedited schedule or additional workers to complete the work in accordance to the timeframe.



Environmental

Use **Fish** button when construction cannot occur within a particular time due to fish spawning.

Use **Birds** button when migratory birds are present and the structure needs to be netted to preclude bird nesting.



Interim Liquidated Damages

Use **Eliminate Excusable Delays Calendar Days** button to assess interim liquidated damages based on work being completed within a specified number of calendar days with no excuses.

Use **Restrict Weather Delays Calendar Days** button to assess interim liquidated damages based on work being completed within a specified number of calendar days restricting the use of weather delays.

Use **Eliminate Excusable Delays Fixed Date** button to assess interim liquidated damages based on work being completed by a specific date with no excuses.

Use **Restrict Weather Delays Fixed Date** button to assess interim liquidated damages based on work being completed by a specific date restricting the use of weather delays.

Use **Eliminate Excusable Delays Multiple Proj** button to assess interim liquidated damages for multiple projects with no excuses*.

*This STSP is written for calendar day contracts, but can be modified for use with other contract types.
